


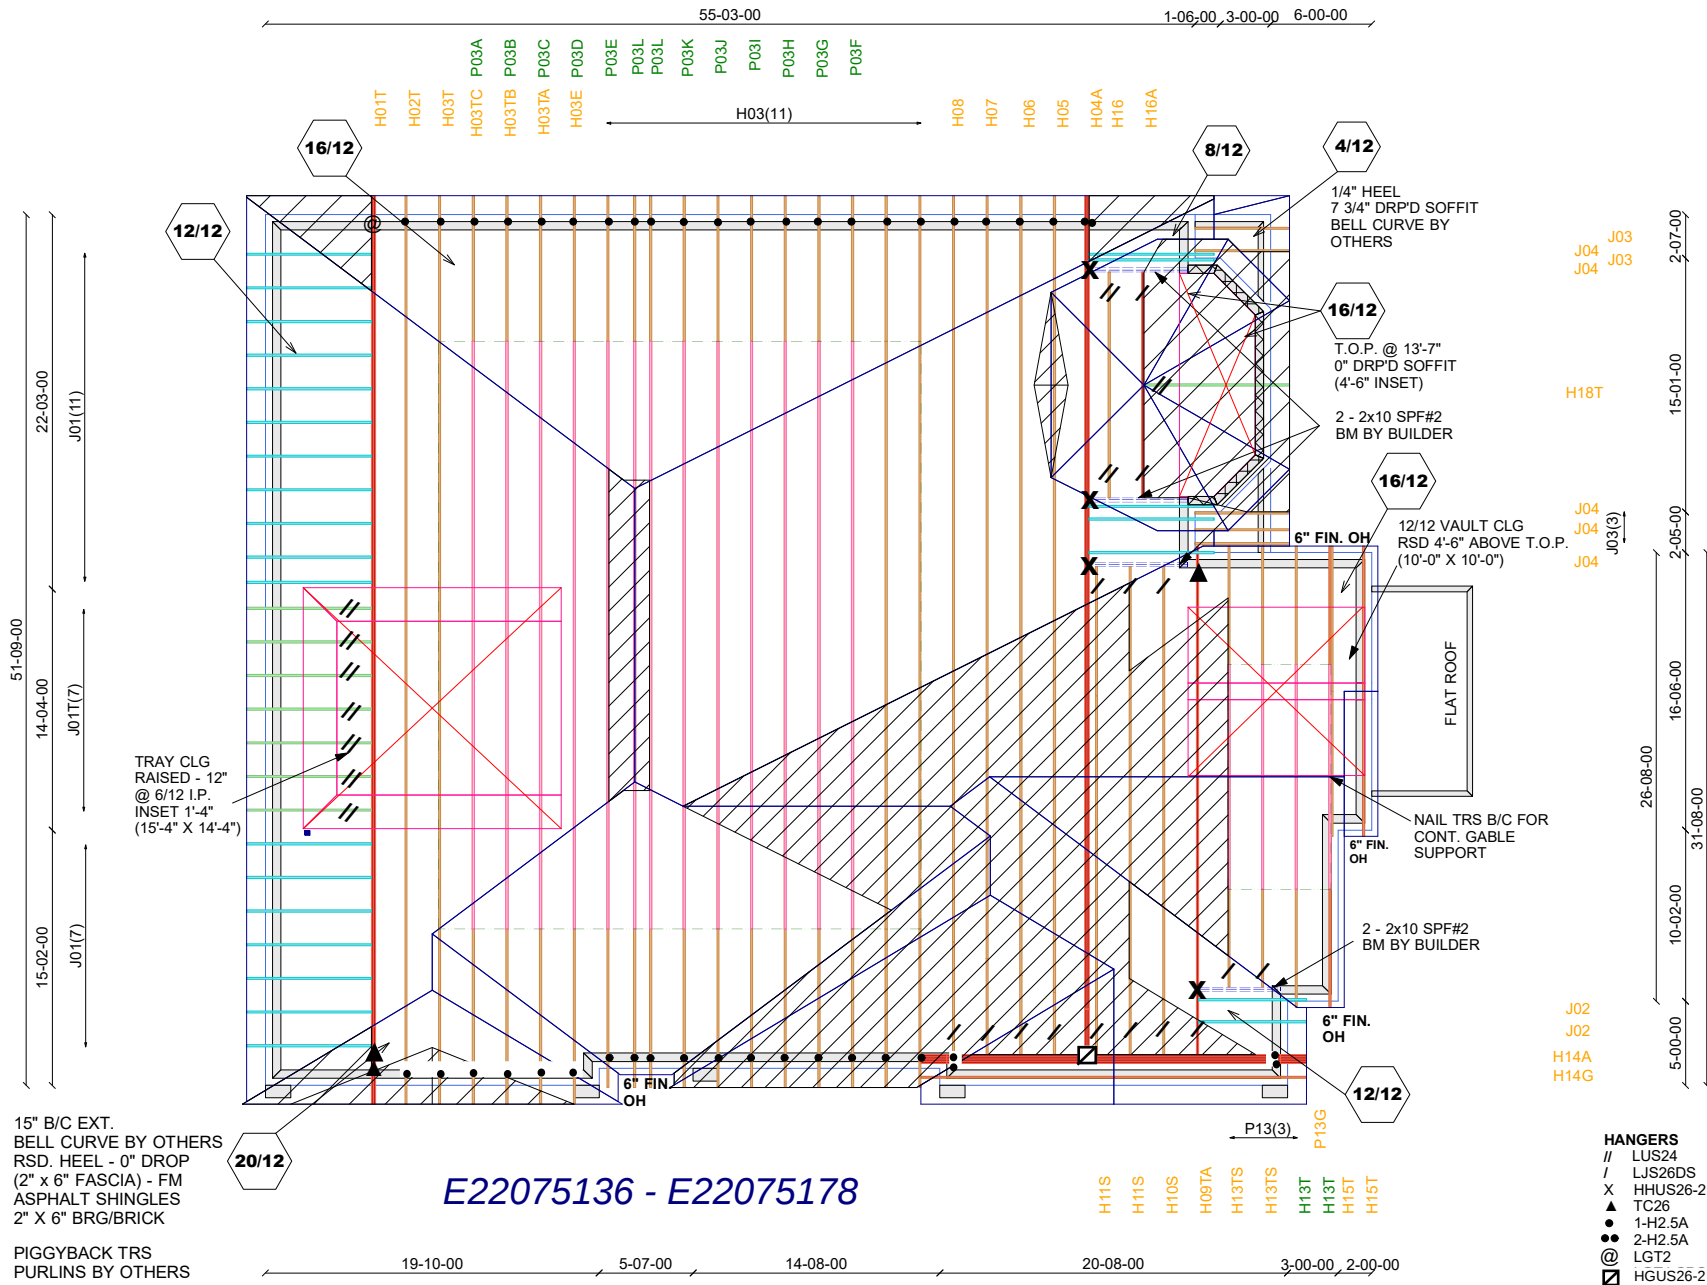

- HANGERS**
- // LUS24
 - / LJS26DS
 - X HHUS26-2
 - ▲ TC26
 - 1-H2.5A
 - 2-H2.5A
 - @ LGT2
 - ☑ HGUS26-2

Mitek V. 8.5.3.233

ALL CONVENTIONAL FRAMING TO CONFORM WITH PART 9 O.B.C. LATEST EDITION. ROOF RAFTERS THAT CROSS OVER TRUSSES TO BE 2X4 SPF #2 @ 24" O.C WITH A VERT. POST TO THE TRUSS UNDERNEATH AT EACH CROSS POINT. VERT. POSTS LONGER THAN 6' TO HAVE LATERAL BRACING SO THAT THE DISTANCE BETWEEN END POINTS & BETWEEN ROWS OF BRACING DOES NOT EXCEED 6'

CONVENTIONAL FRAMING BY OTHERS



Job Track: **45147**
Layout ID: **345817**
Plan Log: **117906**

Builder / Location:
GOLD PARK HOMES / VAUGHAN

Model / Elevation: "QUEENSLAND"
6001 / A LOT 104

Project: **PINE VALLEY PH 2**
Date: **7/20/2022** Designer: JBURROWS

THESE DRAWINGS CONSTITUTE THE PROPERTY OF ALPA ROOF TRUSSES INC., SHALL NOT BE REPRODUCED, PUBLISHED, OR REDISTRIBUTED IN ANY MANNER OR UTILIZED FOR ANY PURPOSE OTHER THAN THE MANUFACTURE OF TRUSSES BY ALPA ROOF TRUSSES INC AND WILL BE RETRACTED BY ALPA ROOF TRUSSES INC IF UTILIZED FOR ANY OTHER PURPOSE.

EWP DESIGN INC.

(905) 832-2250

FAX (905) 832-0286

RESPONSIBILITIES AND SPECIFICATIONS

RESPONSIBILITIES

1. EWP DESIGN INC. is responsible for the design of trusses as individual components.
2. It is the responsibility of others to ascertain that the design loads utilized on each drawing meet or exceed the actual dead load imposed by the structure, the live load imposed by the intended use and the snow load imposed by local building code or authorities with jurisdictions.
3. All dimensions are to be verified by the owner, contractor, architect or other authorities with jurisdictions before truss fabrication.
4. EWP DESIGN INC. bears no responsibility for the erection of trusses. Persons erecting trusses are cautioned to seek professional advice regarding the temporary and permanent bracing for the system. Bracing shown on EWP DESIGN INC. drawing is specified for the truss as a component only and forms an integral part of the truss design.
5. It is the truss manufacturer's responsibility to ensure that trusses are manufactured in conformance with specifications of EWP DESIGN INC. as outlined below.

SPECIFICATIONS

1. Trusses designed by EWP DESIGN INC. conform to the relevant section of the Ontario Building Code of Canada (Part 9 or Part 4) or to the Canadian code for farm buildings, whichever applies to the building type, as indicated on the EWP DESIGN INC. drawings, and conform to the design procedures established by the Truss Plate Institute of Canada. Unit stresses used for truss designs are as per the edition of CSA-O86 shown on EWP DESIGN INC. drawings.
2. Lumber is to be the size, species and grade as specified on EWP DESIGN INC. drawings.
3. Moisture content of lumber shall not exceed 19% in service unless specified otherwise.
4. Metal connector plates shall be applied to both faces of truss at each joint and shall be positioned as specified.
5. Top chords of trusses are assumed to be continuously braced laterally by roof sheathing or by purlins at intervals not exceeding 12.5 times the thickness of top chord member.
6. Bottom chords shall be laterally braced at intervals not exceeding 3M (10') o.c., where rigid ceiling is not applied directly to the underside of chords.

THESE DRAWINGS CONSTITUTE THE PROPERTY OF EWP DESIGN INC., SHALL NOT BE REPRODUCED, PUBLISHED, OR REDISTRIBUTED IN ANY MANNER OR UTILIZED FOR ANY PURPOSE OTHER THAN THE MANUFACTURE OF TRUSSES BY THE ALPA LUMBER GROUP, AND WILL BE RETRACTED BY EWP DESIGN INC. IF UTILIZED FOR ANY OTHER PURPOSE.

[illegible][illegible]

JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	H01T		2	JT 45147	E22075136(2)

PLATES (table is in inches)						
JT	TYPE	PLATES	W	LEN	Y	X
F	TMVW-t	MT20	4.0	6.0		
G	TMW+w	MT20	2.0	4.0		
H	TMWW-t	MT20	4.0	6.0		
I	TS-t	MT20	5.0	6.0		
J	TMVW+p	MT20	4.0	6.0		
K	TMWW-t	MT20	6.0	7.0	2.50	2.25
L	TTWW-h	MT20	10.0	12.0	Edge	4.75
M	TMVW-t	MT20	6.0	10.0	2.25	3.25
O	BMV1+p	MT20	4.0	6.0		
P	BMWW-t	MT20	4.0	6.0	2.00	2.75
Q	BS-t	MT20	5.0	6.0		
R	BMWWW-t	MT20	6.0	10.0	2.00	5.00
S	BMV+p	MT20	2.0	4.0		
T	BVMWW-l	MT20	10.0	12.0	5.00	7.00
U	BMWW+t	MT20	4.0	6.0		
V	BMWWW-t	MT20	5.0	6.0		
W	BVMWW-l	MT20	8.0	12.0	4.50	7.75
X	BMV+p	MT20	2.0	4.0		
Y	BMWWW-t	MT20	7.0	12.0		
Z	BS-t	MT20	5.0	6.0		
AA	BMWW+t	MT20	5.0	8.0	3.75	1.75
AB	BMWW-t	MT20	4.0	6.0	2.00	2.25
AC	BMV1+p	MT20	4.0	6.0		

Edge - INDICATES REFERENCE CORNER OF PLATE TOUCHES EDGE OF CHORD.

CONNECTION REQUIREMENTS

1) C1: A SUITABLE HANGER/MECHANICAL CONNECTION IS REQUIRED.

WIND LOAD APPLIED IS DERIVED FROM REFERENCE VELOCITY PRESSURE OF { 9.2} PSF AT {30-0-0} FT-IN-SX REFERENCE HEIGHT ABOVE GRADE AND USING EXTERNAL PEAK COEFFICIENTS, CpCg, BASED ON THE (MAIN WIND FORCE RESISTING SYSTEM).INTERNAL WIND PRESSURE IS BASED ON DESIGN {CATEGORY 2}. BUILDING MAY BE LOCATED ON (ROUGH TERRAIN) AT MINIMUM {1.000} MILES DISTANCE FROM OPEN TERRAIN., AND TRUSS IS DESIGNED TO BE LOCATED AT LEAST {0-0} FT-IN-SX AWAY FROM EAVE.TRUSS UPLIFT IS BASED ON TOP AND BOTTOM CHORD DEAD LOADS OF 6.0 PSF AND 7.4 PSF RESPECTIVELY.

NAIL VALUES					
PLATE	GRIP(DRY)	SHEAR	SECTION		
	(PSI)	(PLI)	(PLI)		
	MAX	MIN	MAX	MIN	MAX
MT20	650	371	1747	788	1987 1873
PLATE PLACEMENT TOL. = 0.250 inches					
PLATE ROTATION TOL. = 5.0 Deg.					
JSI GRIP= 0.90 (K) (INPUT = 0.90)					
JSI METAL= 0.92 (Y) (INPUT = 1.00)					

LATERAL BRACE(S) SHOWN SHALL BE 2X4 SPF#2



JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	H02T		1	JT 45147	E22075137

Alpa Roof Truss, Maple

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:06:58 2022 Page 1

ID:AdsF8nx1Uq6zWc uLADACeywtAv-90obhQDJyFac2yOSnq471pPiL0VuQ7sr1bO6zWyube

Scale = 1:89.4

The diagram illustrates a roof truss system with the following details:

- Dimensions:**
 - Overall width: 50'-0"
 - Overall height: 9'-5-1/2"
 - Bottom chord depth: 6'-0"
 - Top chord depth: 2'-0"
- Members:**
 - Top Chord:** 10x12 // (B-C), 4x6 // (C-D), 4x6 // (D-E), 5x6 = (E-F), 4x6 = (F-G), 2x4 // (G-H), 4x6 // (H-I), 4x10 // (I-J), 4x6 // (J-K), 4x6 // (K-L), 10x12 \\\ (L-M).
 - Bottom Chord:** 6x10 // (A-B), 4x6 = (B-C), 5x6 // (C-D), 5x6 = (D-E), 10x12 = (E-F), 5x6 = (F-G), 10x16 MT18HS (G-H), 5x6 = (H-I), 5x6 = (I-J), 4x6 = (J-K), 6x10 // (K-L).
 - Web Members:** W1, W2, W3, W4, W5, W6, W7, W8, W9, W10.
 - Diagonal Bracing:** T1, T2, T3, T4.
- Joints:** A, B, C, D, E, F, G, H, I, J, K, L, M, N, O, P, Q, R, S, T, U, V, W, X, Y, Z.
- Labels:** AD, AC, AB, AA, Z, Y, B1, B2, B3, W, V, U, B5, S, R, Q, P, O.

[illegible]

JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	H03	1		JT 45147	E22075138

Alpa Roof Truss, Maple

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:09:45 2022 Page 1
 ID:AdsF8nx1Ug6zWc uLADACeywtAv-n8OjkXE3dZdwacfY3OaHl1pHPKYp2qwQR3LSKKyubt

Scale = 1:84.9

TOTAL WEIGHT = 11 X 375 = 4128 LB

NUMBER

N. L. G. A. RULES

CHORDS

SIZE

LUMBER

DESCR.

A - C

2x6

DRY

No.2

SPF

C - E

2x6

DRY

No.2

SPF

E - H

2x6

DRY

No.2

SPF

H - J

2x6

DRY

No.2

SPF

J - L

2x6

DRY

No.2

SPF

W - A

2x6

DRY

No.2

SPF

X - U

2x6

DRY

No.2

SPF

U - R

2x6

DRY

No.2

SPF

R - O

2x6

DRY

No.2

SPF

O - M

2x6

DRY

No.2

SPF

REINFORCING MEMBERS

HW2

2x4

DRY

No.2

SPF

ALL WEBS

2x4

DRY

No.2

SPF

EXCEPT

B - V

2x3

DRY

No.2

SPF

N - K

2x3

DRY

No.2

SPF

DRY: SEASONED LUMBER.

PLATES (table is in inches)

JT	TYPE	PLATES	W	LEN	Y	X
A	TMV+p	MT20	2.0	4.0		
B	TMVW-t	MT20	5.0	6.0	2.00	1.50
C	TTWW-h	MT20	8.0	9.0	2.00	4.50
D, F, I						
D	TMVW-t	MT20	4.0	6.0		
E	TS-t	MT20	5.0	6.0		
G	TMW+w	MT20	2.0	4.0		
H	TS-t	MT20	5.0	6.0		
J	TTWW-h	MT20	8.0	9.0	2.00	4.50
K	TMVW-t	MT20	4.0	6.0	2.00	2.00
L	TBMW1-I	MT20	5.0	6.0	2.25	1.75
N, S, V						
N	BMVW-t	MT20	4.0	6.0		
O, R, U						
O	BS-t	MT20	5.0	6.0		
P	BMVW-t	MT20	4.0	6.0	2.50	1.75
Q	BMVW-t	MT20	5.0	8.0		
T	BMVW-t	MT20	4.0	6.0	2.50	1.75
W	BMVW1-t	MT20	5.0	6.0	2.00	3.00

DISPOSITIONS, SUPPORTS

AND LOADINGS

AND FABRICATOR

VERIFIED

BY

BUILDING DESIGNER

BEARINGS

	FACTORED	MAXIMUM FACTORED	INPUT	REQRD
	GROSS REACTION	GROSS REACTION	BRG	BRG
JT	VERT	HORZ	DOWN	HORZ
UPLIFT	IN-SX	IN-SX		
Y(L)	3593	0	3593	0
			-562	5-8
W	3546	0	3546	-337
			-550	5-8
				3-12

PROVIDE ANCHORAGE AT BEARING JOINT L FOR 562 LBS

FACTORED

UPLIFT

PROVIDE ANCHORAGE AT BEARING JOINT W FOR 550 LBS

FACTORED

UPLIFT

PROVIDE FOR 337 LBS

FACTORED HORIZONTAL REACTION AT JOINTW

UNFACTORED REACTIONS

	1ST LCASE	MAX./MIN. COMPONENT REACTIONS				
JT	COMBINED	SNOW	LIVE	PERM.LIVE	WIND	DEAD
SOIL						
Y(L)	2701	1426 / 0	560 / 0	0 / 0	324 / -861	715 / 0
W	2666	1408 / 0	553 / 0	0 / 0	383 / -847	706 / 0

HORIZONTAL REACTIONS

W	---	0 / 0	0 / 0	0 / 0	228 / -241	0 / 0	0 / 0
---	-----	-------	-------	-------	------------	-------	-------

BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) Y(L), W

BRACING

MAX. UNBRACED TOP CHORD LENGTH = 4.06 FT.

MAX. UNBRACED BOTTOM CHORD LENGTH = 6.25 FT OR RIGID CEILING DIRECTLY APPLIED.

ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED.

1 LATERAL BRACE(S) AT 1/2 LENGTH OF C-V, C-T, D-S, F-S, F-Q, G-Q, I-Q, J-P, J-N, B-W, K-Y.

2 LATERAL BRACE(S) AT 1/3 LENGTH OF D-T, I-P.

END VERTICAL(S) MUST BE SHEATHED OR HAVE BRACES AS INDICATED IN

THE MAX. UNBRACED LENGTH COLUMN OF THE TABLE BELOW

LOADING

TOTAL LOAD CASES: (18)

CHORDS				WEBS			
MEMB.	MAX. FACTORED FORCE (LBS)	FACTORED VERT. LOAD (PLF)	MAX. CSI (LC)	MEMB.	MAX. FACTORED FORCE (LBS)	MAX. CSI (LC)	
FR-TO		FROM TO	LENGTH	FR-TO			
A-B	-43 / 169	-95.2	-95.2	0.12 (13)	6.25	B-V	0 / 354
B-C	-3174 / 746	-95.2	-95.2	0.18 (13)	4.66	V-C	-128 / 292
C-D	-3118 / 743	-95.2	-95.2	0.40 (1)	4.41	C-T	-446 / 2338
D-E	-3714 / 822	-95.2	-95.2	0.43 (1)	4.08	T-D	-1702 / 462
E-F	-3714 / 822	-95.2	-95.2	0.43 (1)	4.08	D-S	-219 / 1166
F-G	-3727 / 825	-95.2	-95.2	0.35 (1)	4.17	S-F	-740 / 278
G-H	-3727 / 825	-95.2	-95.2	0.44 (1)	4.06	F-Q	-56 / 74
H-I	-3727 / 825	-95.2	-95.2	0.44 (1)	4.06	Q-G	-688 / 241
I-J	-3172 / 753	-95.2	-95.2	0.41 (1)	4.38	Q-I	-205 / 1094
J-K	-3294 / 764	-95.2	-95.2	0.18 (14)	4.56	P-I	-1644 / 452
K-Z	-1381 / 328	-95.2	-95.2	0.26 (1)	6.22	P-J	-435 / 2295
Z-L	-798 / 11	-95.2	-95.2	0.24 (1)	6.25	N-J	-149 / 371
W-A	-178 / 179	0.0	0.0	0.02 (13)	7.81	N-K	-131 / 307
						W-B	-3553 / 451
						Y-Z	-980 / 427
						Y-K	-2193 / 321
X-W	0 / 0	-134.7	-134.7	0.11 (1)	10.00		
W-V	-376 / 1772	-39.5	-39.5	0.35 (4)	6.25		
V-U	-225 / 1879	-39.5	-39.5	0.37 (4)	6.25		
U-T	-225 / 1879	-39.5	-39.5	0.37 (4)	6.25		
T-S	-426 / 3118	-39.5	-39.5	0.46 (1)	6.25		
S-R	-503 / 3714	-39.5	-39.5	0.53 (1)	6.25		
R-Q	-503 / 3714	-39.5	-39.5	0.53 (1)	6.25		
Q-P	-376 / 3173	-39.5	-39.5	0.49 (1)	6.25		
P-O	-140 / 1958	-39.5	-39.5	0.34 (1)	6.25		
O-N	-140 / 1958	-39.5	-39.5	0.34 (1)	6.25		
N-Y	-233 / 1978	-39.5	-39.5	0.50 (1)	6.25		
Y-L	-59 / 786	-39.5	-39.5	0.36 (1)	6.25		
L-M	0 / 0	-134.7	-134.7	0.06 (1)	10.00		

TRUSS HAS BEEN CHECKED FOR UNBALANCED LOADING

AS PER NBCC 4.1.6.2.(8)

WIND LOAD APPLIED IS DERIVED FROM REFERENCE VELOCITY PRESSURE OF { 9.2} PSF AT {30-0-0} FT-IN-SX REFERENCE HEIGHT ABOVE GRADE AND USING EXTERNAL PEAK COEFFICIENTS, CpCg, BASED ON THE (MAIN WIND FORCE RESISTING SYSTEM).INTERNAL WIND PRESSURE IS BASED ON DESIGN {CATEGORY 2}. BUILDING MAY BE LOCATED ON (ROUGH TERRAIN) AT MINIMUM {1.000} MILES DISTANCE FROM OPEN TERRAIN., AND TRUSS IS DESIGNED TO BE LOCATED AT LEAST {0-0} FT-IN-SX AWAY FROM EAVE.TRUSS UPLIFT IS BASED ON TOP AND BOTTOM CHORD DEAD LOADS OF 6.0 PSF AND 7.4 PSF RESPECTIVELY.

DESIGN CRITERIA

SPECIFIED LOADS:

TOP	CH.	LL	=	26.7	PSF
		DL	=	6.0	PSF
BOT	CH.	LL	=	10.5	PSF
		DL	=	7.4	PSF
TOTAL	LOAD	=	50.6	PSF	

SPACING = 24.0

IN. C/C

LOADING IN FLAT SECTION BASED ON A SLOPE OF 12.00/12

THIS TRUSS IS DESIGNED FOR COMMERCIAL OR INDUSTRIAL BUILDING REQUIREMENTS OF PART 4, NBCC 2015

THIS DESIGN COMPLIES WITH:
- PART 4 OF BCBC 2018 , ABC 2019
- PART 4 OF OBC 2012 (2019 AMENDMENT)
- CSA 086-14
- TPIC 2014

DESIGN ASSUMPTIONS
- SLOPE REDUCTION FACTOR USED
- PERCENTAGE OF GROUND SNOW LOAD IS USER-DEFINED.

(80 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) TIMES IMPORTANCE FACTOR EQUALS 26.7 P.S.F. SPECIFIED ROOF LIVE LOAD

ALLOWABLE DEFL.(LL)= L/360 (1.68")
CALCULATED VERT. DEFL.(LL)= L/ 999 (0.17")
ALLOWABLE DEFL.(TL)= L/180 (3.35")
CALCULATED VERT. DEFL.(TL)= L/ 999 (0.25")

CANTILEVER DEFLECTION:
ALLOWABLE DEFL.(LL)= L/120 (0.19")
CALCULATED VERT. DEFL.(LL)= L/ 999 (0.01")
ALLOWABLE DEFL.(TL)= L/120 (0.19")
CALCULATED VERT. DEFL.(TL)= L/ 999 (0.01")

CSI: TC=0.44/1.00 (G-I:1) , BC=0.53/1.00 (Q-S:1) ,
WB=0.78/1.00 (B-W:1) , SSI=0.36/1.00 (L-Y:4)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10
COMP=1.10 SHEAR=1.10 TENS= 1.10

SNOW LOAD IMPORTANCE FACTOR = 1.00
WIND LOAD IMPORTANCE FACTOR = 1.00
LIVE LOAD IMPORTANCE FACTOR = 1.00
COMPANION LIVE LOAD FACTOR = 1.00

AUTOSOLVE RIGHT HEEL ONLY

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES
PLATE GRIP(DRY) SHEAR SECTION
(PSI) (PLI) (PLI)
MAX MIN MAX MIN MAX MIN
MT20 650 371 1747 788 1987 1873

PLATE PLACEMENT TOL. = 0.250 inches

PLATE ROTATION TOL. = 5.0 Deg.

JSI GRIP= 0.89 (W) (INPUT = 0.90)
JSI METAL= 0.79 (B) (INPUT = 1.00)

LATERAL BRACE(S) SHOWN SHALL BE 2X4 SPF#2



JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	H03E		1	JT 45147	E22075139

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:07:05 2022 Page 1
ID:AdsF8nx1Uq6zWc uLADACeywtAv-SMjE9pliJPTdN1QoohimplBwZqx3ZHfAb icyube

The structural drawing illustrates a symmetrical roof truss system. The top chord consists of horizontal members C-D, D-E, E-F, F-G, G-H, H-I, I-J, and J-K, along with end overhangs A-B and L-M. Vertical members connect the top chord to the bottom chord at joints D, E, F, G, H, I, and J. Diagonal bracing members are shown between various joints, including W1 through W11. The bottom chord includes a central section T-U and end sections V-W and X-Y. Dimensions are provided for all major spans and heights. A scale of 1/8" = 1'-0" is indicated.

TOTAL WEIGHT = 383 lb

LUMBER

N. L. G. A. RULES

CHORDS

SIZE

LUMBER

DESCR.

A - C

2x6

DRY

No.2

SPF

C - E

2x6

DRY

No.2

SPF

E - H

2x6

DRY

No.2

SPF

H - J

2x6

DRY

No.2

SPF

J - L

2x6

DRY

No.2

SPF

L - M

2x6

DRY

No.2

SPF

Z - A

2x6

DRY

No.2

SPF

O - M

2x6

DRY

No.2

SPF

AA- X

2x6

DRY

No.2

SPF

X - U

2x6

DRY

No.2

SPF

U - R

2x6

DRY

No.2

SPF

R - N

2x6

DRY

No.2

SPF

ALL WEBS EXCEPT

SPF

B - Y

2x3

DRY

No.2

SPF

Q - K

2x3

DRY

No.2

SPF

Q - L

2x3

DRY

No.2

SPF

P - L

2x3

DRY

No.2

SPF

DRY - SEASONED LUMBER.

PLATES (table is in inches)

JT

TYPE

PLATES

W

LEN

Y

X

A

TMV+p

MT20

2.0

4.0

B

TMWW-t

MT20

5.0

8.0

2.50

2.50

C

TTWW-h

MT20

8.0

9.0

2.00

4.50

D, F, I

D

TMWW-t

MT20

4.0

6.0

E

TS-t

MT20

5.0

6.0

G

TMW+w

MT20

2.0

4.0

H

TS-t

MT20

5.0

6.0

J

TTWW-h

MT20

8.0

9.0

2.00

4.50

K

TMW+w

MT20

2.0

4.0

L

TTWW-h

MT20

8.0

9.0

4.00

3.75

M

TMW-t

MT20

6.0

7.0

2.00

3.00

O

BMV1+t

MT20

6.0

10.0

Edge

0.50

P

BMWW-t

MT20

6.0

7.0

2.25

2.50

Q

BMWWW+t

MT20

5.0

6.0

2.00

2.50

R, U, X

R

BS-t

MT20

5.0

6.0

S

BMWWW+t

MT20

4.0

6.0

2.50

1.75

T

BMWWW-t

MT20

5.0

8.0

V

BMWW-t

MT20

4.0

6.0

W

BMWWW+t

MT20

4.0

6.0

2.25

1.75

Y

BMWW-t

MT20

4.0

6.0

Z

BMVW1-t

MT20

5.0

6.0

2.00

2.75

Edge - INDICATES REFERENCE CORNER OF PLATE TOUCHES EDGE OF CHORD.

BEARINGS

FACTORED

GROSS REACTION

DOWN

HORZ

UPLIFT

IN-SX

BRG

BRG

IN-SX

JT

VERT

HORZ

DOWN

HORZ

UPLIFT

IN-SX

BRG

BRG

IN-SX

Z

3634

0

3634

339

-562

5-8

4-0

O

3640

0

3640

0

-568

5-8

5-8

PROVIDE ANCHORAGE AT BEARING JOINT Z FOR 562 LBS. FACTORED UPLIFT

PROVIDE ANCHORAGE AT BEARING JOINT O FOR 568 LBS. FACTORED UPLIFT

PROVIDE FOR 339 LBS FACTORED HORIZONTAL REACTION AT JOINTZ

UNFACTORED REACTIONS

1ST LCASE

MAX./MIN. COMPONENT REACTIONS

JT

COMBINED

SNOW

LIVE

PERM.LIVE

WIND

DEAD

SOIL

Z

2732

1442 / 0

567 / 0

0 / 0

392 / -866

723 / 0

0 / 0

O

2737

1445 / 0

567 / 0

0 / 0

309 / -871

724 / 0

0 / 0

HORIZONTAL REACTIONS

Z

0 / 0

0 / 0

0 / 0

242 / -236

0 / 0

0 / 0

BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) Z, O

BEARING SIZE FACTOR = 1.15 AT JNT(S) O (BASED ON SUPPORT DEPTH = 1-8)

BRACING

MAX. UNBRACED TOP CHORD LENGTH = 3.96 FT.

MAX. UNBRACED BOTTOM CHORD LENGTH = 6.25 FT OR RIGID CEILING DIRECTLY APPLIED.

ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED.

1 LATERAL BRACE(S) AT 1/2 LENGTH OF C-Y, C-W, D-V, F-V, F-T, G-T, I-T, J-S, J-Q, B-Z.

2 LATERAL BRACE(S) AT 1/3 LENGTH OF D-W, I-S.

END VERTICAL(S) MUST BE SHEATHED OR HAVE BRACES AS INDICATED IN THE MAX. UNBRACED LENGTH COLUMN OF THE TABLE BELOW

LOADING

TOTAL LOAD CASES: (18)

CHORDS

MEMB.

MAX. FACTORED

FACTORED

VERT. LOAD

LC1

MAX

MAX.

WEBS

MEMB.

MAX. FACTORED

FACTORED

VERT. LOAD

LC1

MAX

MAX.

FR-TO

FROM

TO

LENGTH

FR-TO

FROM

TO

LENGTH

A-B

-44 / 169

-95.2

-95.2

0.12

(13)

6.25

B-Y

0 / 367

0.08

(3)

B-C

-3269 / 759

-95.2

-95.2

0.18

(13)

4.60

Y-C

-126 / 286

0.08

(13)

C-D

-3230 / 758

-95.2

-95.2

0.41

(1)

4.35

C-W

-461 / 2439

0.45

(14)

D-E

-3881 / 845

-95.2

-95.2

0.44

(1)

3.99

W-D

-1787 / 475

0.50

(3)

E-F

-3881 / 845

-95.2

-95.2

0.44

(1)

3.99

D-V

-235 / 1268

0.23

(14)

F-G

-3950 / 859

-95.2

-95.2

0.36

(1)

4.06

V-F

-817 / 292

0.52

(10)

G-H

-3950 / 859

-95.2

-95.2

0.45

(1)

3.96

F-T

-55 / 177

0.05

(14)

H-I

-3950 / 859

-95.2

-95.2

0.45

(1)

3.96

T-G

-687 / 241

0.43

(10)

I-J

-3448 / 795

-95.2

-95.2

0.42

(1)

4.22

T-I

-192 / 1012

0.19

(13)

J-K

-3886 / 869

-95.2

-95.2

0.18

(14)

4.28

S-I

-1572 / 441

0.44

(2)

K-L

-4017 / 710

-95.2

-95.2

0.16

(14)

4.24

S-J

-416 / 2193

0.41

(13)

L-M

-3189 / 515

-95.2

-95.2

0.08

(1)

4.71

Q-J

-255 / 879

0.16

(14)

Z-A

-179 / 179

0.0

0.0

0.02

(13)

7.81

Q-K

-364 / 331

0.32

(8)

O-M

-3249 / 519

0.0

0.0

0.24

(1)

5.88

Q-L

-941 / 194

0.91

(1)

AA-Z

0 / 0

-134.7

-134.7

0.11

(1)

10.00

P-L

-3274 / 605

0.50

(1)

Z-Y

-387 / 1822

-39.5

-39.5

0.36

(4)

6.25

P-M

-696 / 4554

0.73

(1)

Y-X

-236 / 1936

-39.5

-39.5

0.37

(4)

6.25

Z-B

-3653 / 465

0.80

(1)

X-W

-236 / 1936

-39.5

-39.5

0.37

(4)

6.25

W-V

-445 / 3230

-39.5

-39.5

0.48

(1)

6.25

V-U

-530 / 3881

-39.5

-39.5

0.55

(1)

6.25

U-T

-530 / 3881

-39.5

-39.5

0.55

(1)

6.25

T-S

-417 / 3448

-39.5

-39.5

0.51

(1)

6.25

S-R

-191 / 2302

-39.5

-39.5

0.41

(1)

6.25

R-Q

-191 / 2302

-39.5

-39.5

0.41

(1)

6.25

Q-P

-488 / 3351

-39.5

-39.5

0.55

(1)

6.25

P-O

-11 / 29

-39.5

-39.5

0.51

(3)

6.25

O-N

0 / 0

-134.7

-134.7

0.11

(1)

10.00

DESIGN CRITERIA

SPECIFIED LOADS:

TOP

CH.

LL

=

26.7

PSF

DL

=

6.0

PSF

BOT

CH.

LL

=

10.5

PSF

DL

=

7.4

PSF

TOTAL LOAD

=

50.6

PSF

SPACING = 24.0 IN. C/C

LOADING IN ALL FLAT SECTIONS BASED ON A SLOPE OF 12.00/12

THIS TRUSS IS DESIGNED FOR COMMERCIAL OR INDUSTRIAL BUILDING REQUIREMENTS OF PART 4, NBCC 2015

THIS DESIGN COMPLIES WITH:

- PART 4 OF BCBC 2018 , ABC 2019

- PART 4 OF OBC 2012 (2019 AMENDMENT)

- CSA 086-14

- TPIC 2014

DESIGN ASSUMPTIONS

- SLOPE REDUCTION FACTOR USED

- PERCENTAGE OF GROUND SNOW LOAD IS USER-DEFINED.

- OVERHANG NOT TO BE ALTERED OR CUT OFF.

(80 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) TIMES IMPORTANCE FACTOR EQUALS 26.7 P.S.F. SPECIFIED ROOF LIVE LOAD

ALLOWABLE DEFL.(LL)= L/360 (1.70")

CALCULATED VERT. DEFL.(LL) = L/ 999 (0.20")

ALLOWABLE DEFL.(TL)= L/180 (3.39")

CALCULATED VERT. DEFL.(TL) = L/ 999 (0.29")

CANTILEVER DEFLECTION:

ALLOWABLE DEFL.(LL)= L/120 (0.19")

CALCULATED VERT. DEFL.(LL) = L/ 518 (0.04")

ALLOWABLE DEFL.(TL)= L/120 (0.19")

CALCULATED VERT. DEFL.(TL) = L/ 355 (0.05")

CSI: TC=0.45/1.00 (G-I:1) , BC=0.55/1.00 (P-Q:1) , WB=0.91/1.00 (L-Q:1) , SSI=0.24/1.00 (I-J:3)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10

COMP=1.10 SHEAR=1.10 TENS= 1.10

SNOW LOAD IMPORTANCE FACTOR = 1.00

WIND LOAD IMPORTANCE FACTOR = 1.00

LIVE LOAD IMPORTANCE FACTOR = 1.00

COMPANION LIVE LOAD FACTOR = 1.00

AUTOSOLVE HEELS OFF

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES

PLATE GRIP(DRY) SHEAR SECTION

(PSI) (PLI) (PLI)

MAX MIN MAX MIN MAX MIN

MT20 650 371 1747 788 1987 1873

PLATE PLACEMENT TOL. = 0.250 inches

PLATE ROTATION TOL. = 5.0 Deg.

LATERAL BRACE(S) SHOWN SHALL BE
2X4 SPF#2



TRUSS HAS BEEN CHECKED FOR UNBALANCED LOADING
AS PER NBCC 4.1.6.2.(8)

WIND LOAD APPLIED IS DERIVED FROM REFERENCE VELOCITY PRESSURE OF (9.2) PSF AT (30-0.0) FT-IN-SX REFERENCE HEIGHT ABOVE GRADE AND USING EXTERNAL PEAK COEFFICIENTS, CpCg, BASED ON THE (MAIN WIND FORCE RESISTING SYSTEM); INTERNAL WIND PRESSURE IS BASED ON DESIGN (CATEGORY 2). BUILDING MAY BE LOCATED ON (ROUGH TERRAIN) AT MINIMUM (1.000) MILES DISTANCE FROM OPEN TERRAIN. AND TRUSS IS DESIGNED TO BE LOCATED AT LEAST (0-0) FT-IN-SX AWAY FROM EAVE. TRUSS UPLIFT IS BASED ON TOP AND BOTTOM CHORD DEAD LOADS OF 6.0 PSF AND 7.4 PSF RESPECTIVELY.

DESIGN CRITERIA

SPECIFIED LOADS:

TOP	CH.	LL	=	26.7	PSF
		DL	=	6.0	PSF
BOT	CH.	LL	=	10.5	PSF
		DL	=	7.4	PSF
TOTAL		LOAD	=	50.6	PSF

SPACING = 24.0 IN. C/C

LOADING IN ALL FLAT SECTIONS BASED ON A
SLOPE OF 12.00/12

THIS TRUSS IS DESIGNED FOR COMMERCIAL
OR INDUSTRIAL BUILDING REQUIREMENTS OF
PART 4, NBCC 2015

THIS DESIGN COMPLIES WITH:

- PART 4 OF BCBC 2018 , ABC 2019
- PART 4 OF OBC 2012 (2019 AMENDMENT)
- CSA 086-14
- TPIC 2014

DESIGN ASSUMPTIONS
- SLOPE REDUCTION FACTOR USED
- PERCENTAGE OF GROUND SNOW LOAD IS
USER-DEFINED.
- OVERHANG NOT TO BE ALTERED OR CUT OFF.

(80 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) TIMES IMPORTANCE FACTOR EQUALS 26.7 P.S.F. SPECIFIED ROOF LIVE LOAD

ALLOWABLE DEFL.(LL)= $L/360$ (1.70")
 CALCULATED VERT. DEFL.(LL) = $L/999$ (0.20")
 ALLOWABLE DEFL.(TL)= $L/180$ (3.39")
 CALCULATED VERT. DEFL.(TL) = $L/999$ (0.29")

CANTILEVER DEFLECTION:
ALLOWABLE DEFL.(LL)= $L/120$ (0.19")
CALCULATED VERT. DEFL.(LL)= $L/518$ (0.04")
ALLOWABLE DEFL.(TL)= $L/120$ (0.19")
CALCULATED VERT. DEFL.(TL)= $L/355$ (0.05")

CSI: TC=0.45/1.00 (G-I:1), BC=0.55/1.00 (P-Q:1),
WB=0.91/1.00 (L-Q:1), SSI=0.24/1.00 (I-J:3)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10
COMP=1.10 SHEAR=1.10 TENS= 1.10

SNOW LOAD IMPORTANCE FACTOR = 1.00
WIND LOAD IMPORTANCE FACTOR = 1.00
LIVE LOAD IMPORTANCE FACTOR = 1.00
COMPANION LIVE LOAD FACTOR = 1.00

AUTOSOLVE HEELS OFF

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES						
PLATE	GRIP(DRY)		SHEAR		SECTION	
	(PSI)		(PLI)		(PLI)	
	MAX	MIN	MAX	MIN	MAX	MIN
MT20	650	371	1747	788	1987	1873

PLATE PLACEMENT TOL. = 0.250 inches

PLATE ROTATION TOL. = 5.0 Deg.

JSI GRIP= 0.90 (C) (INPUT = 0.90)
JSI METAL= 0.75 (U) (INPUT = 1.00)

JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	H03T		1	TRUSS DESC.	E22075140

Alpa Roof Truss, Maple

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:07:10 2022 Page 1
 ID:AdsF8nx1Ug6zWc uLADACeywtAv-pJW7CXMq7x5vUoJIULIxWLuk8rdnEX4coSIIOPyube

Scale = 1:91.6

TOTAL WEIGHT = 437 lb

LUMBER				
N. L. G. A. RULES				
CHORDS		SIZE	LUMBER	DESCR.
A - B	2x6	DRY	No.2	SPF
B - D	2x6	DRY	No.2	SPF
D - H	2x6	DRY	No.2	SPF
H - K	2x6	DRY	No.2	SPF
K - L	2x6	DRY	No.2	SPF
L - M	2x6	DRY	No.2	SPF
M - N	2x6	DRY	No.2	SPF
AC- A	2x8	DRY	No.2	SPF
P - N	2x8	DRY	No.2	SPF
AD- AA	2x6	DRY	No.2	SPF
AA- Y	2x6	DRY	No.2	SPF
Y - X	2x6	DRY	No.2	SPF
X - V	2x6	DRY	No.2	SPF
V - U	2x6	DRY	No.2	SPF
U - R	2x6	DRY	No.2	SPF
R - O	2x6	DRY	No.2	SPF
ALL WEBS EXCEPT	2x4	DRY	No.2	SPF
E - X	2x3	DRY	No.2	SPF
X - F	2x3	DRY	No.2	SPF
W - G	2x3	DRY	No.2	SPF
V - I	2x3	DRY	No.2	SPF
V - J	2x3	DRY	No.2	SPF
T - L	2x3	DRY	No.2	SPF
A - AB	2x3	DRY	No.2	SPF
Q - N	2x3	DRY	No.2	SPF
DRY: SEASONED LUMBER.				

JT	TYPE	PLATES	W	LEN	Y	X
A	TMVW-t	MT20	6.0	10.0	3.00	2.75
B	TTWW-h	MT20	10.0	12.0	Edge	4.50
C, F, I						
D	TMWW-t	MT20	4.0	6.0		
D	TS-t	MT20	5.0	6.0		
E	TMWW+t	MT20	4.0	6.0	2.00	1.75
G	TMW+w	MT20	2.0	4.0		
H	TS-t	MT20	5.0	6.0		
J	TMWW+t	MT20	5.0	6.0	2.50	2.00
K	TTWW-h	MT20	8.0	9.0	2.00	4.50
L	TTWW-h	MT20	8.0	9.0	4.00	4.00
M	TTWW-h	MT20	10.0	12.0	Edge	4.75
N	TMVW-t	MT20	5.0	14.0	2.00	5.50
P	BMV1+p	MT20	4.0	6.0		
Q	BMWW-t	MT20	4.0	6.0	2.00	2.75
R	BS-t	MT20	5.0	6.0		
S	BMWW+t	MT20	4.0	6.0	2.00	1.75
T	BMWW-t	MT20	4.0	6.0		
U	BBWW-h	MT20	10.0	12.0	4.00	7.75
V	BBWW-I	MT20	10.0	12.0		
W	BMWWW-t	MT20	5.0	6.0	2.25	3.00
X	BBWW-I	MT20	8.0	9.0	4.50	4.50
Y	BBWW-h	MT20	10.0	12.0	4.25	8.25
Z	BMWW+t	MT20	4.0	6.0	2.25	1.75
AA	BS-t	MT20	5.0	6.0		
AB	BMWW-t	MT20	5.0	6.0	2.50	2.75
AC	BMV1+p	MT20	4.0	6.0		

Edge - INDICATES REFERENCE CORNER OF PLATE
TOUCHES EDGE OF CHORD.

LATERAL BRACE(S) SHOWN SHALL BE
2X4 SPF#2



DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER
BEARINGS

JT	FACTORED		MAXIMUM FACTORED			INPUT	REQRD
	GROSS	REACTION	GROSS REACTION		BRG	BRG	
AC	VERT	HORZ	DOWN	HORZ	UPLIFT	IN-SX	IN-SX
P	3637	0	3637	355	-562	5-8	4-5
	3637	0	3637	0	-567	5-8	4-5

PROVIDE ANCHORAGE AT BEARING JOINT AC FOR 562 LBS FACTORED UPLIFT
PROVIDE ANCHORAGE AT BEARING JOINT P FOR 567 LBS FACTORED UPLIFT

PROVIDE FOR 355 LBS FACTORED HORIZONTAL REACTION AT JOINT C

UNFACTORED REACTIONS							
1ST LCASE		MAX./MIN. COMPONENT REACTIONS					
JT	COMBINED	SNOW	LIVE	PERM.LIVE	WIND	DEAD	SOIL
AC	2734	1444 / 0	567 / 0	0 / 0	392 / -866	724 / 0	0 / 0
P	2734	1444 / 0	567 / 0	0 / 0	310 / -870	724 / 0	0 / 0

HORIZONTAL REACTIONS							
AC	---	0 / 0	0 / 0	0 / 0	253 / -238	0 / 0	0 / 0

BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) AC, P

BRACING
MAX. UNBRACED TOP CHORD LENGTH = 3.91 FT.
MAX. UNBRACED BOTTOM CHORD LENGTH = 6.25 FT OR RIGID CEILING DIRECTLY APPLIED.

ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE LATERALLY RESTRAINED.

1 LATERAL BRACE(S) AT 1/2 LENGTH OF B-AB, E-X, F-X, F-W, G-W, I-W, I-V, J-V, K-U, K-T, L-T, M-S, M-Q.
2 LATERAL BRACE(S) AT 1/3 LENGTH OF B-Z, C-Z, C-Y, E-Y, J-U, L-S.

END VERTICAL(S) MUST BE SHEATHED OR HAVE BRACES AS INDICATED IN THE MAX. UNBRACED LENGTH COLUMN OF THE TABLE BELOW

LOADING									
TOTAL LOAD CASES: (18)									
CHORDS					WEB S				
MEMB.	MAX. FACTORED FORCE (LBS)	FACTORED VERT. LOAD (PLF)	LC1	MAX. CSI (LC)	MAX. UNBRAC	MEMB.	MAX. FACTORED FORCE (LBS)	MAX. CSI (LC)	
FR-TO		FROM TO			LENGTH	FR-TO			
A-B	-3248 / 547	-95.2	-95.2	0.65 (1)	4.18	AB-B	-172 / 215	0.11 (7)	
B-C	-3281 / 763	-95.2	-95.2	0.46 (1)	4.25	B-Z	-461 / 2468	0.40 (3)	
C-D	-3912 / 853	-95.2	-95.2	0.50 (1)	3.91	Z-C	-1747 / 492	0.49 (3)	
D-E	-3912 / 853	-95.2	-95.2	0.50 (1)	3.91	C-Y	-235 / 1188	0.19 (3)	
E-F	-4332 / 902	-95.2	-95.2	0.32 (1)	3.91	Y-E	-2724 / 448	0.77 (1)	
F-G	-4310 / 892	-95.2	-95.2	0.33 (1)	3.94	E-X	-262 / 2174	0.49 (1)	
G-H	-4310 / 892	-95.2	-95.2	0.33 (1)	3.94	X-F	-107 / 91	0.07 (10)	
H-I	-4310 / 892	-95.2	-95.2	0.33 (1)	3.94	F-W	-122 / 76	0.08 (2)	
I-J	-3844 / 835	-95.2	-95.2	0.36 (1)	4.06	W-G	-679 / 216	0.47 (7)	
J-K	-3313 / 778	-95.2	-95.2	0.36 (1)	4.35	W-I	-198 / 1083	0.17 (2)	
K-L	-3829 / 992	-95.2	-95.2	0.11 (14)	4.38	V-I	-968 / 233	0.68 (2)	
L-M	-2315 / 590	-95.2	-95.2	0.11 (1)	5.30	V-J	-398 / 2739	0.62 (1)	
M-N	-3023 / 548	-95.2	-95.2	0.36 (14)	4.63	U-J	-3343 / 604	0.94 (1)	
AC-A	-3314 / 583	0.0	0.0	0.18 (1)	6.53	U-K	-420 / 2213	0.36 (13)	
P-N	-3357 / 581	0.0	0.0	0.21 (1)	6.50	T-K	-387 / 903	0.24 (14)	
						T-L	-911 / 402	0.66 (1)	
AD-AC	0 / 0	-134.7	-134.7	0.11 (1)	10.00	S-L	-2319 / 458	0.56 (1)	
AC-AB	-336 / 324	-39.5	-39.5	0.18 (17)	6.25	S-M	-429 / 2614	0.42 (1)	
AB-AA	-236 / 1938	-39.5	-39.5	0.37 (4)	6.25	Q-M	-350 / 81	0.18 (7)	
AA-Z	-236 / 1938	-39.5	-39.5	0.37 (4)	6.25	A-AB	-162 / 1973	0.44 (1)	
Z-Y	-449 / 3281	-39.5	-39.5	0.52 (1)	6.25	Q-N	-103 / 1626	0.37 (1)	
Y-X	-593 / 4334	-39.5	-39.5	0.52 (1)	6.25				
X-W	-586 / 4332	-39.5	-39.5	0.58 (1)	6.25				
W-V	-469 / 3853	-39.5	-39.5	0.52 (1)	6.25				
V-U	-429 / 3656	-39.5	-39.5	0.44 (1)	6.25				
U-T	-190 / 2290	-39.5	-39.5	0.40 (1)	6.25				
T-S	-207 / 2348	-39.5	-39.5	0.33 (2)	6.25				
S-R	-74 / 1536	-39.5	-39.5	0.28 (1)	6.25				
R-Q	-74 / 1536	-39.5	-39.5	0.28 (1)	6.25				
Q-P	-11 / 23	-39.5	-39.5	0.10 (4)	6.25				
P-O	0 / 0	-134.7	-134.7	0.11 (1)	10.00				

TRUSS HAS BEEN CHECKED FOR UNBALANCED LOADING
AS PER NBCC 4.1.6.2.(8)

WIND LOAD APPLIED IS DERIVED FROM REFERENCE VELOCITY PRESSURE OF { 9.2} PSF AT { 30-0.0} FT-IN-SX REFERENCE HEIGHT ABOVE GRADE AND USING EXTERNAL PEAK COEFFICIENTS, CpCg, BASED ON THE {MAIN WIND FORCE RESISTING SYSTEM}. INTERNAL WIND PRESSURE IS BASED ON DESIGN {CATEGORY 2}. BUILDING MAY BE LOCATED ON {ROUGH TERRAIN} AT MINIMUM {1.000} MILES DISTANCE FROM OPEN TERRAIN,, AND TRUSS IS DESIGNED TO BE LOCATED AT LEAST {0-0} FT-IN-SX AWAY FROM EAVE. TRUSS UPLIFT IS BASED ON TOP AND BOTTOM CHORD DEAD LOADS OF 6.0 PSF AND 7.4 PSF RESPECTIVELY.

DESIGN CRITERIA

DESIGN CRITERIA

SPECIFIED LOADS:

TOP	CH.	LL	=	26.7	PSF
		DL	=	6.0	PSF
BOT	CH.	LL	=	10.5	PSF
		DL	=	7.4	PSF
TOTAL LOAD				=	50.6 PSF

SPACING = 24.0 IN. C/C

LOADING IN ALL FLAT SECTIONS BASED ON A
SLOPE OF 12.00/12

THIS TRUSS IS DESIGNED FOR COMMERCIAL
OR INDUSTRIAL BUILDING REQUIREMENTS OF
PART 4, NBCC 2015

THIS DESIGN COMPLIES WITH:

- PART 4 OF BCBC 2018 , ABC 2019
- PART 4 OF OBC 2012 (2019 AMENDMENT)
- CSA 086-14
- TPIC 2014

DESIGN ASSUMPTIONS

- SLOPE REDUCTION FACTOR USED
- PERCENTAGE OF GROUND SNOW LOAD IS USER-DEFINED.

(80 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) TIMES IMPORTANCE FACTOR EQUALS 26.7 P.S.F. SPECIFIED ROOF LIVE LOAD

ALLOWABLE DEFL.(LL)= L/360 (1.70")
CALCULATED VERT. DEFL.(LL) = L/ 999 (0.29")
ALLOWABLE DEFL.(TL)= L/180 (3.39")
CALCULATED VERT. DEFL.(TL) = L/ 999 (0.42")

CANTILEVER DEFLECTION:
ALLOWABLE DEFL.(LL)= $L/120$ (0.19")
CALCULATED VERT. DEFL.(LL) = $L/999$ (0.00")
ALLOWABLE DEFL.(TL)= $L/120$ (0.19")
CALCULATED VERT. DEFL.(TL) = $L/999$ (0.00")

CSI: TC=0.65/1.00 (A-B:1) , BC=0.58/1.00 (W-X:1) ,
WB=0.94/1.00 (J-U:1) , SSI=0.25/1.00 (B-C:2)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10
COMP=1.10 SHEAR=1.10 TENS= 1.10

SNOW LOAD IMPORTANCE FACTOR = 1.00
WIND LOAD IMPORTANCE FACTOR = 1.00
LIVE LOAD IMPORTANCE FACTOR = 1.00
COMPANION LIVE LOAD FACTOR = 1.00

AUTOSOLVE HEELS OFF

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES						
PLATE	GRIP(DRY)		SHEAR		SECTION	
	(PSI)		(PLI)		(PLI)	
	MAX	MIN	MAX	MIN	MAX	MIN
MT20	650	371	1747	788	1987	1873

PLATE PLACEMENT TOL. = 0.250 inches

PLATE ROTATION TOL. = 5.0 Deg.

JSI GRIP= 0.87 (A) (INPUT = 0.90)
JSI METAL= 0.64 (K) (INPUT = 1.00)

JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	H03TC		1	JT 45147	E22075143

Alpa Roof Truss, Maple

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:07:24 2022 Page 1

ID:AdsF8nx1Uq6zWc uLADACeywtAv-P0NQ8JXcqEswyqNSJHYD5IU7?UPCWsqg0ehUu?yube

Scale = 1:91.2

LUMBER										DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER										DESIGN CRITERIA									
N. L. G. A. RULES										BEARINGS										SPECIFIED LOADS:									
CHORDS	SIZE	LUMBER	DESCR.	FACTORED						GROSS REACTION						INPUT		REQRD		TOP CH. LL = 26.7 PSF									
A - B	2x6	DRY	No.2	SPF	GROSS REACTION						DOWN		HORZ		UPLIFT		IN-SX		DL = 6.0 PSF										
B - D	2x6	DRY	No.2	SPF	GROSS REACTION						DOWN		HORZ		UPLIFT		IN-SX		LL = 10.5 PSF										
D - H	2x6	DRY	No.2	SPF	GROSS REACTION						DOWN		HORZ		UPLIFT		IN-SX		DL = 7.4 PSF										
H - K	2x6	DRY	No.2	SPF	GROSS REACTION						DOWN		HORZ		UPLIFT		IN-SX		TOTAL LOAD = 50.6 PSF										
K - L	2x6	DRY	No.2	SPF	GROSS REACTION						DOWN		HORZ		UPLIFT		IN-SX												
L - M	2x6	DRY	No.2	SPF	GROSS REACTION						DOWN		HORZ		UPLIFT		IN-SX												
M - N	2x6	DRY	No.2	SPF	GROSS REACTION						DOWN		HORZ		UPLIFT		IN-SX												
AC- A	2x6	DRY	No.2	SPF	GROSS REACTION						DOWN		HORZ		UPLIFT		IN-SX												
P - N	2x6	DRY	No.2	SPF	GROSS REACTION						DOWN		HORZ		UPLIFT		IN-SX												
AD- AA	2x6	DRY	No.2	SPF	GROSS REACTION						DOWN		HORZ		UPLIFT		IN-SX												
AA- Y	2x6	DRY	No.2	SPF	GROSS REACTION						DOWN		HORZ		UPLIFT		IN-SX												



JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	H04A	2		JT 45147	E22075144

Alpa Roof Truss, Maple

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:07:29 2022 Page 1
ID:AdsF8nx1Uq6zWc uLADACeywtAv-lzAJB1blfnUDGjGP5q8OoMBvKV1vB6yP9vPFYDyubc

Scale = 1:84.3

TOTAL WEIGHT = 2 X 277 = 555 LBS

NUMBER N L G A. RULES CHORDS SIZE LUMBER DESCR. A - B 2x6 DRY No.2 SPF B - F 2x6 DRY No.2 SPF F - J 2x6 DRY No.2 SPF J - M 2x6 DRY No.2 SPF M - N 2x6 DRY No.2 SPF AC- A 2x6 DRY No.2 SPF O - N 2x6 DRY No.2 SPF AD- Y 2x6 DRY 1650F 1.5E SPF Y - U 2x6 DRY 1650F 1.5E SPF U - R 2x6 DRY 1650F 1.5E SPF R - O 2x6 DRY 1650F 1.5E SPF ALL WEBS 2x3 DRY No.2 SPF EXCEPT DRY: SEASONED LUMBER. DESIGN CONSISTS OF 2 TRUSSES BUILT SEPARATELY THEN FASTENED TOGETHER AS FOLLOWS: CHORDS #ROWS SURFACE SPACING (IN) LOAD(PLF) TOP CHORDS : (0.122"x3") SPIRAL NAILS A- B 2 12 SIDE(140.3) B- F 2 12 SIDE(66.9) F- J 2 12 SIDE(48.0) J- M 2 12 TOP M- N 2 12 TOP AC- A 2 12 TOP O- N 2 12 TOP BOTTOM CHORDS : (0.122"x3") SPIRAL NAILS AD- Y 2 12 SIDE(24.2) Y- U 2 12 SIDE(203.9) U- R 2 12 TOP R- O 2 12 TOP WEBS : (0.122"x3") SPIRAL NAILS 2x3 1 6 E- X 1 6 SIDE(357.0) G- W 1 6 SIDE(410.5) NAILS TO BE DRIVEN FROM ONE SIDE ONLY. GIRDER NAILING ASSUMES NAILED HANGERS ARE FASTENED WITH MIN. 3-0 INCH NAILS. TOP - COMPONENTS ARE LOADED FROM THE TOP AND MUST BE PLACED ON TOP EDGE OF ALL PLIES FOR THE LOAD TO BE TRANSFERRED TO EACH PLY. SIDE - PLF SHOWN IS THE EQUIVALENT UDL APPLIED TO ONE SIDE THAT THE CORRESPONDING NAILING PATTERN SHALL BE CAPABLE OF TRANSFERING. REMAINING PLF MUST BE APPLIED ON THE OPPOSITE SIDE OR ON THE TOP. PLATES (table is in inches) JT TYPE PLATES W LEN Y X A TMVW-t MT20 6.0 10.0 2.00 4.00 B TTWW-I MT20 8.0 9.0 2.75 7.00 C TMVWV-t MT20 6.0 7.0 2.50 2.25 D TMVWV-t MT20 6.0 7.0 2.75 3.00 E TMVWV-t MT20 4.0 6.0 F TS-t MT20 5.0 8.0 G TMVWV-t MT20 4.0 6.0 H TMVW-w MT20 2.0 4.0 I TMVWV-t MT20 5.0 6.0 J TS-t MT20 5.0 6.0 K TMVWV-t MT20 5.0 6.0 2.50 1.75 L TMVWV-t MT20 5.0 6.0 2.75 1.75	STRENGTH, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER BEARINGS <table> <tr> <th></th><th>FACTORED</th><th>GROSS REACTION</th><th>MAXIMUM FACTORED</th><th>INPUT</th><th>REQRD</th></tr> <tr> <th>JT</th><th>VERT</th><th>HORZ</th><th>DOWN</th><th>HORZ</th><th>UPLIFT</th></tr> <tr> <td>AC</td><td>8693</td><td>0</td><td>8853</td><td>-149</td><td>0</td></tr> <tr> <td>O</td><td>5229</td><td>0</td><td>5388</td><td>0</td><td>-110</td></tr> </table> A SUITABLE HANGER/MECHANICAL CONNECTION IS REQUIRED AT JOINT O. MINIMUM BEARING LENGTH AT JOINT O = 4-0. PROVIDE ANCHORAGE AT BEARING JOINT O FOR 150 LBS. FACTORED UPLIFT PROVIDE FOR 149 LBS. FACTORED HORIZONTAL REACTION AT JOINTAC UNFACTORED REACTIONS <table> <tr> <th></th><th>1ST LCASE</th><th>MAX./MIN.</th><th>COMPONENT REACTIONS</th><th></th><th></th><th></th><th></th></tr> <tr> <th>JT</th><th>COMBINED</th><th>SNOW</th><th>LIVE</th><th>PERM.LIVE</th><th>WIND</th><th>DEAD</th><th>SOIL</th></tr> <tr> <td>AC</td><td>6362</td><td>3725 / 0</td><td>659 / 0</td><td>0 / 0</td><td>570 / -1015</td><td>2085 / 0</td><td>0 / 0</td></tr> <tr> <td>O</td><td>3865</td><td>2247 / 0</td><td>551 / 0</td><td>0 / 0</td><td>409 / -832</td><td>1173 / 0</td><td>0 / 0</td></tr> </table> HORIZONTAL REACTIONS AC --- 0 / 0 0 / 0 0 / 0 103 / -108 0 / 0 0 / 0 BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) AC BEARING SIZE FACTOR = 1.15 AT JNT(S) AC (BASED ON SUPPORT DEPTH = 1-8) BRACING MAX. UNBRACED TOP CHORD LENGTH = 2.03 FT. MAX. UNBRACED BOTTOM CHORD LENGTH = 6.25 FT. OR RIGID CEILING DIRECTLY APPLIED. ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED. 2x4 DRY SPF No.2 T-BRACE AT G-V FASTEN T AND I-BRACES TO NARROW EDGE OF WEB WITH ONE ROW PER PLY OF 3" COMMON WIRE NAILS @ 6" O.C. WITH 3" MINIMUM END DISTANCE. BRACE MUST COVER 90% OF WEB LENGTH. END VERTICAL(S) MUST BE SHEATHED OR HAVE BRACES AS INDICATED IN THE MAX. UNBRACED LENGTH COLUMN OF THE TABLE BELOW LOADING TOTAL LOAD CASES: (18) <table> <tr> <th colspan="4">CHORDS</th><th colspan="4">WEBS</th></tr> <tr> <th>MEMB.</th><th>MAX. FACTORED FORCE (LBS)</th><th>FACTORED VERT. LOAD (PLF)</th><th>MAX. CSI (LC)</th><th>MAX. UNBRAC LENGTH</th><th>MEMB.</th><th>MAX. FACTORED FORCE (LBS)</th><th>MAX. CSI (LC)</th></tr> <tr> <td>FR-TO</td><td></td><td>FROM TO</td><td></td><td></td><td>FR-TO</td><td></td><td></td></tr> <tr> <td>A- B</td><td>-7621 / 0</td><td>-95.2</td><td>-95.2 0.10 (2)</td><td>4.32</td><td>AB- B</td><td>-161 / 394</td><td>0.04 (14)</td></tr> <tr> <td>B-AE</td><td>-10242 / 0</td><td>-198.6</td><td>-198.6 0.30 (2)</td><td>3.68</td><td>B-AA</td><td>0 / 8031</td><td>0.99 (3)</td></tr> <tr> <td>AE- C</td><td>-10242 / 0</td><td>-95.2</td><td>-95.2 0.30 (2)</td><td>3.68</td><td>AA- C</td><td>-5311 / 0</td><td>0.94 (3)</td></tr> <tr> <td>C- D</td><td>-15218 / 0</td><td>-95.2</td><td>-95.2 0.53 (2)</td><td>2.89</td><td>C- Z</td><td>0 / 7019</td><td>0.87 (3)</td></tr> <tr> <td>D-E</td><td>-19526 / 0</td><td>-95.2</td><td>-95.2 0.88 (2)</td><td>2.25</td><td>Z- D</td><td>-4766 / 0</td><td>0.84 (3)</td></tr> <tr> <td>E- F</td><td>-20729 / 0</td><td>-191.2</td><td>-191.2 0.97 (2)</td><td>2.03</td><td>D- X</td><td>0 / 6077</td><td>0.75 (3)</td></tr> <tr> <td>F-G</td><td>-20729 / 0</td><td>-191.2</td><td>-191.2 0.97 (2)</td><td>2.03</td><td>X- E</td><td>-2055 / 135</td><td>0.36 (3)</td></tr> <tr> <td>G- H</td><td>-18908 / 0</td><td>-95.2</td><td>-95.2 0.85 (3)</td><td>2.34</td><td>E- W</td><td>0 / 1917</td><td>0.24 (3)</td></tr> <tr> <td>H- I</td><td>-18908 / 0</td><td>-95.2</td><td>-95.2 0.84 (3)</td><td>2.35</td><td>W- G</td><td>0 / 1001</td><td>0.12 (1)</td></tr> <tr> <td>I- J</td><td>-16208 / 0</td><td>-95.2</td><td>-95.2 0.64 (3)</td><td>2.73</td><td>G- V</td><td>-2466 / 0</td><td>0.57 (1)</td></tr> <tr> <td>J- K</td><td>-16208 / 0</td><td>-95.2</td><td>-95.2 0.64 (3)</td><td>2.73</td><td>V- H</td><td>-588 / 191</td><td>0.10 (10)</td></tr> <tr> <td>K- L</td><td>-12667 / 0</td><td>-95.2</td><td>-95.2 0.41 (3)</td><td>3.27</td><td>V- I</td><td>0 / 3621</td><td>0.45 (2)</td></tr> <tr> <td>L- M</td><td>-8293 / 152</td><td>-95.2</td><td>-95.2 0.24 (3)</td><td>4.08</td><td>T- I</td><td>-2940 / 0</td><td>0.52 (2)</td></tr> <tr> </tr></table>		FACTORED	GROSS REACTION	MAXIMUM FACTORED	INPUT	REQRD	JT	VERT	HORZ	DOWN	HORZ	UPLIFT	AC	8693	0	8853	-149	0	O	5229	0	5388	0	-110		1ST LCASE	MAX./MIN.	COMPONENT REACTIONS					JT	COMBINED	SNOW	LIVE	PERM.LIVE	WIND	DEAD	SOIL	AC	6362	3725 / 0	659 / 0	0 / 0	570 / -1015	2085 / 0	0 / 0	O	3865	2247 / 0	551 / 0	0 / 0	409 / -832	1173 / 0	0 / 0	CHORDS				WEBS				MEMB.	MAX. FACTORED FORCE (LBS)	FACTORED VERT. LOAD (PLF)	MAX. CSI (LC)	MAX. UNBRAC LENGTH	MEMB.	MAX. FACTORED FORCE (LBS)	MAX. CSI (LC)	FR-TO		FROM TO			FR-TO			A- B	-7621 / 0	-95.2	-95.2 0.10 (2)	4.32	AB- B	-161 / 394	0.04 (14)	B-AE	-10242 / 0	-198.6	-198.6 0.30 (2)	3.68	B-AA	0 / 8031	0.99 (3)	AE- C	-10242 / 0	-95.2	-95.2 0.30 (2)	3.68	AA- C	-5311 / 0	0.94 (3)	C- D	-15218 / 0	-95.2	-95.2 0.53 (2)	2.89	C- Z	0 / 7019	0.87 (3)	D-E	-19526 / 0	-95.2	-95.2 0.88 (2)	2.25	Z- D	-4766 / 0	0.84 (3)	E- F	-20729 / 0	-191.2	-191.2 0.97 (2)	2.03	D- X	0 / 6077	0.75 (3)	F-G	-20729 / 0	-191.2	-191.2 0.97 (2)	2.03	X- E	-2055 / 135	0.36 (3)	G- H	-18908 / 0	-95.2	-95.2 0.85 (3)	2.34	E- W	0 / 1917	0.24 (3)	H- I	-18908 / 0	-95.2	-95.2 0.84 (3)	2.35	W- G	0 / 1001	0.12 (1)	I- J	-16208 / 0	-95.2	-95.2 0.64 (3)	2.73	G- V	-2466 / 0	0.57 (1)	J- K	-16208 / 0	-95.2	-95.2 0.64 (3)	2.73	V- H	-588 / 191	0.10 (10)	K- L	-12667 / 0	-95.2	-95.2 0.41 (3)	3.27	V- I	0 / 3621	0.45 (2)	L- M	-8293 / 152	-95.2	-95.2 0.24 (3)	4.08	T- I	-2940 / 0	0.52 (2)
	FACTORED	GROSS REACTION	MAXIMUM FACTORED	INPUT	REQRD																																																																																																																																																																																				
JT	VERT	HORZ	DOWN	HORZ	UPLIFT																																																																																																																																																																																				
AC	8693	0	8853	-149	0																																																																																																																																																																																				
O	5229	0	5388	0	-110																																																																																																																																																																																				
	1ST LCASE	MAX./MIN.	COMPONENT REACTIONS																																																																																																																																																																																						
JT	COMBINED	SNOW	LIVE	PERM.LIVE	WIND	DEAD	SOIL																																																																																																																																																																																		
AC	6362	3725 / 0	659 / 0	0 / 0	570 / -1015	2085 / 0	0 / 0																																																																																																																																																																																		
O	3865	2247 / 0	551 / 0	0 / 0	409 / -832	1173 / 0	0 / 0																																																																																																																																																																																		
CHORDS				WEBS																																																																																																																																																																																					
MEMB.	MAX. FACTORED FORCE (LBS)	FACTORED VERT. LOAD (PLF)	MAX. CSI (LC)	MAX. UNBRAC LENGTH	MEMB.	MAX. FACTORED FORCE (LBS)	MAX. CSI (LC)																																																																																																																																																																																		
FR-TO		FROM TO			FR-TO																																																																																																																																																																																				
A- B	-7621 / 0	-95.2	-95.2 0.10 (2)	4.32	AB- B	-161 / 394	0.04 (14)																																																																																																																																																																																		
B-AE	-10242 / 0	-198.6	-198.6 0.30 (2)	3.68	B-AA	0 / 8031	0.99 (3)																																																																																																																																																																																		
AE- C	-10242 / 0	-95.2	-95.2 0.30 (2)	3.68	AA- C	-5311 / 0	0.94 (3)																																																																																																																																																																																		
C- D	-15218 / 0	-95.2	-95.2 0.53 (2)	2.89	C- Z	0 / 7019	0.87 (3)																																																																																																																																																																																		
D-E	-19526 / 0	-95.2	-95.2 0.88 (2)	2.25	Z- D	-4766 / 0	0.84 (3)																																																																																																																																																																																		
E- F	-20729 / 0	-191.2	-191.2 0.97 (2)	2.03	D- X	0 / 6077	0.75 (3)																																																																																																																																																																																		
F-G	-20729 / 0	-191.2	-191.2 0.97 (2)	2.03	X- E	-2055 / 135	0.36 (3)																																																																																																																																																																																		
G- H	-18908 / 0	-95.2	-95.2 0.85 (3)	2.34	E- W	0 / 1917	0.24 (3)																																																																																																																																																																																		
H- I	-18908 / 0	-95.2	-95.2 0.84 (3)	2.35	W- G	0 / 1001	0.12 (1)																																																																																																																																																																																		
I- J	-16208 / 0	-95.2	-95.2 0.64 (3)	2.73	G- V	-2466 / 0	0.57 (1)																																																																																																																																																																																		
J- K	-16208 / 0	-95.2	-95.2 0.64 (3)	2.73	V- H	-588 / 191	0.10 (10)																																																																																																																																																																																		
K- L	-12667 / 0	-95.2	-95.2 0.41 (3)	3.27	V- I	0 / 3621	0.45 (2)																																																																																																																																																																																		
L- M	-8293 / 152	-95.2	-95.2 0.24 (3)	4.08	T- I	-2940 / 0	0.52 (2)																																																																																																																																																																																		

JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	H04A		2	JT 45147	E22075144(2)

Alpa Roof Truss, Maple

ID:AdsF8nx1Ug6zWc_uLADACeywtAv-IzAJB1blfnUDGjGP5q8OoMBvKV1vB6yP9vPFYDyubdy

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:07:29 2022 Page 2

PLATES (table is in inches)							JSI GRIP= 0.90 (D) (INPUT = 0.90)	
JT	TYPE	PLATES	W	LEN	Y	X	JSI METAL= 0.79 (U) (INPUT = 1.00)	
M	TTWW-h	MT20	10.0	12.0	2.50	7.00		
N	TMVW-t	MT20	5.0	8.0	2.25	2.00		
O	BMV1+t	MT20	4.0	10.0	Edge	1.50		
P	BMWW-t	MT20	4.0	6.0	2.00	2.75		
Q	BMWW-t	MT20	6.0	7.0	2.75	2.00		
R	BS-t	MT20	5.0	6.0				
S	BMWW-t	MT20	5.0	6.0	2.00	1.75		
T	BMWW-t	MT20	5.0	6.0	2.50	1.75		
U	BS-t	MT18HS	6.0	14.0				
V	BMWWWW-t	MT20	5.0	8.0	2.50	2.50		
W	BMWW+t	MT20	5.0	6.0	4.25	2.25		
X	BMWW-t	MT20	6.0	7.0	2.75	3.00		
Y	BS-t	MT18HS	6.0	14.0				
Z	BMWW-t	MT20	6.0	7.0	2.50	2.25		
AA	BMWW-t	MT20	6.0	7.0	2.00	2.25		
AB	BMWW+t	MT20	6.0	7.0	3.75	2.50		
AC	BMV1+t	MT20	6.0	10.0	Edge			

Edge - INDICATES REFERENCE CORNER OF PLATE TOUCHES EDGE OF CHORD.

CONNECTION REQUIREMENTS

1) C1: A SUITABLE HANGER/MECHANICAL CONNECTION IS REQUIRED.

TRUSS HAS BEEN CHECKED FOR UNBALANCED LOADING AS PER NBCC 4.1.6.2.(8)

WIND LOAD APPLIED IS DERIVED FROM REFERENCE VELOCITY PRESSURE OF { 9.2} PSF AT {30-0-0} FT-IN-SX REFERENCE HEIGHT ABOVE GRADE AND USING EXTERNAL PEAK COEFFICIENTS, CpCg, BASED ON THE {MAIN WIND FORCE RESISTING SYSTEM}.INTERNAL WIND PRESSURE IS BASED ON DESIGN {CATEGORY 2}. BUILDING MAY BE LOCATED ON {ROUGH TERRAIN} AT MINIMUM {1.000} MILES DISTANCE FROM OPEN TERRAIN., AND TRUSS IS DESIGNED TO BE LOCATED AT LEAST {0-0} FT-IN-SX AWAY FROM EAVE.TRUSS UPLIFT IS BASED ON TOP AND BOTTOM CHORD DEAD LOADS OF 6.0 PSF AND 7.4 PSF RESPECTIVELY.

LATERAL BRACE(S) SHOWN SHALL BE 2X4 SPF#2



JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	H05	1		TRUSS DESC.	E22075145

Alpa Roof Truss, Maple

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:07:33 2022 Page 1

ID:AdsF8nx1Uq6zWc uLADACeywtAv-elPq1OeGi? ekKZAKqDKyCLfi7PD7yX?4XNSH yubc

Scale = 1:87.5

10x20 MT18HS//

16.00 [12

6x7 ||

6x10 ||

4x6 =

6x7 =

5x6 =

5x6 =

5x6 =

2x4 ||

4x6 =

5x6 =

5x6 =

6x14 MT18HS=

5x6 =

5x6 =

4x6 =

5x6 =

6x10 ||

4x6 =

4x10 ||

6x7 =

5x6 =

4x6 =

4x10 ||

1-6-8 0-0 3-4-5 7-0-14 10-5-3 7-0-14 17-6-2 7-0-14 24-7-0 7-0-14 31-7-14 7-0-14 38-8-13 7-0-14 45-9-11 3-8-5 49-6-0

1-6-8 0-0 3-4-5 7-0-14 10-5-3 7-0-14 17-6-2 7-0-14 24-7-0 7-0-14 31-7-14 7-0-14 38-8-13 7-0-14 45-9-11 3-8-5 49-6-0

TOTAL WEIGHT = 275 lb

[illegible]

LATERAL BRACE(S) SHOWN SHALL BE 2X4 SPF#2 	TRUSS HAS BEEN CHECKED FOR UNBALANCED LOADING <u>AS PER NBCC 4.1.6.2.(8)</u> WIND LOAD APPLIED IS DERIVED FROM REFERENCE VELOCITY PRESSURE OF { 9.2} PSF AT {30-0-0} FT-IN-SX REFERENCE HEIGHT ABOVE GRADE AND USING EXTERNAL PEAK COEFFICIENTS, CpCg, BASED ON THE {MAIN WIND FORCE RESISTING SYSTEM}. INTERNAL WIND PRESSURE IS BASED ON DESIGN {CATEGORY 2}. BUILDING MAY BE LOCATED ON {ROUGH TERRAIN} AT MINIMUM {1.000} MILES DISTANCE FROM OPEN TERRAIN, AND TRUSS IS DESIGNED TO BE LOCATED AT LEAST {0-0} FT-IN-SX AWAY FROM EAVE. TRUSS UPLIFT IS BASED ON TOP AND BOTTOM CHORD DEAD LOADS OF 6.0 PSF AND 7.4 PSF RESPECTIVELY.	JSI GRIP= 0.90 (O) (INPUT = 0.90) JSI METAL= 0.95 (T) (INPUT = 1.00)
--	---	---

[illegible]

NUMBER				DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER				DESIGN CRITERIA				
N. L. G. A. RULES				BEARINGS				SPECIFIED LOADS:				
CHORDS	SIZE	LUMBER		DESCR.	FACTORED	MAXIMUM FACTORED	INPUT	REQRD	TOP	CH.	LL	
A - B	2x6	DRY	No.2	SPF	GROSS REACTION	GROSS REACTION	BRG	BRG	DL	=	26.7 PSF	
B - E	2x6	DRY	No.2	SPF	VERT	HORZ	DOWN	HORZ	DL	=	6.0 PSF	
E - H	2x6	DRY	No.2	SPF	W	3541	0	3675	-228	-567	5-8	
H - J	2x6	DRY	No.2	SPF	L	3334	0	3468	0	-549	MECHANICAL	
J - K	2x6	DRY	No.2	SPF	A SUITABLE HANGER/MECHANICAL CONNECTION IS REQUIRED AT JOINT L. MINIMUM BEARING LENGTH AT JOINT L = 3-8.							
W - A	2x6	DRY	No.2	SPF	PROVIDE ANCHORAGE AT BEARING JOINT W FOR 567 LBS FACTORED UPLIFT							
L - K	2x6	DRY	No.2	SPF	PROVIDE ANCHORAGE AT BEARING JOINT L FOR 549 LBS FACTORED UPLIFT							
X - T	2x6	DRY	No.2	SPF	PROVIDE FOR 228 LBS FACTORED HORIZONTAL REACTION AT JOINTW							
T - Q	2x6	DRY	No.2	SPF	UNFACTORED REACTIONS							
Q - N	2x6	DRY	No.2	SPF	1ST LCASE	MAX./MIN. COMPONENT REACTIONS						
N - L	2x6	DRY	No.2	SPF	JT	COMBINED	SNOW	LIVE	PERM.LIVE	WIND	DEAD	
ALL WEBS EXCEPT				SPF	W	2666	1495 / 0	552 / 0	0 / 0	398 / -858	705 / 0	
DRY: SEASONED LUMBER.					L	2562	1412 / 0	520 / 0	0 / 0	372 / -819	663 / 0	
					HORIZONTAL REACTIONS							
					W	---	0 / 0	0 / 0	0 / 0	159 / -163	0 / 0	
					BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) W							
					BEARING SIZE FACTOR = 1.15 AT JNT(S) W (BASED ON SUPPORT DEPTH = 1-8)							
					BRACING							
					MAX. UNBRACED TOP CHORD LENGTH = 3.30 FT.							
					MAX. UNBRACED BOTTOM CHORD LENGTH = 6.25 FT OR RIGID CEILING DIRECTLY APPLIED.							
					ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED.							
					1 LATERAL BRACE(S) AT 1/2 LENGTH OF B-U, C-U, C-S, D-S, D-R, G-R, G-P, I-P, I-O, J-O.							
					END VERTICAL(S) MUST BE SHEATHED OR HAVE BRACES AS INDICATED IN THE MAX. UNBRACED LENGTH COLUMN OF THE TABLE BELOW							
					LOADING							
					TOTAL LOAD CASES: (18)							
					CHORDS				WEBS			
					MEMB.	MAX. FACTORED	FACTORED	VERT. LOAD	MAX. UNBRAC	MEMB.	MAX. FACTORED	
						FORCE (LBS)	(PLF)	LC1	MAX. (LC)		FORCE (LBS)	
					FR-TO		FROM TO		LENGTH	FR-TO		
					A-B	-3246 / 548	-95.2	-95.2	0.23 (2)	4.54	V-B	-376 / 140
					B-C	-4161 / 821	-95.2	-95.2	0.45 (2)	3.88	B-U	-562 / 3333

LATERAL BRACE(S) SHOWN SHALL BE
2X4 SPF#2



DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER

BEARINGS		FACTORED GROSS REACTION		MAXIMUM FACTORED GROSS REACTION		INPUT BRG	REQRD BRG
	VERT	HORZ	DOWN	HORZ	UPLIFT	IN-SX	IN-SX
JT							
W	3541	0	3675	-228	-567	5-8	5-8
L	3334	0	3468	0	-549	MECHANICAL	

A SUITABLE HANGER/MECHANICAL CONNECTION IS REQUIRED AT JOINT L. MINIMUM BEARING LENGTH AT JOINT L = 3-8.

PROVIDE ANCHORAGE AT BEARING JOINT W FOR 567 LBS FACTORED UPLIFT
PROVIDE ANCHORAGE AT BEARING JOINT L FOR 549 LBS FACTORED UPLIFT

UNFACTORED REACTIONS							
JT	1ST LCASE	MAX./MIN. COMPONENT REACTIONS					
	COMBINED	SNOW	LIVE	PERM.LIVE	WIND	DEAD	SOIL
W	2662	1495 / 0	552 / 0	0 / 0	398 / -858	705 / 0	0 / 0
L	2506	1412 / 0	520 / 0	0 / 0	372 / -819	663 / 0	0 / 0

HORIZONTAL REACTIONS							
W	---	0 / 0	0 / 0	0 / 0	159 / -163	0 / 0	0 / 0

BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) W
BEARING SIZE FACTOR = 1.15 AT JNT(S) W (BASED ON SUPPORT DEPTH = 1-8)

BRACING
MAX. UNBRACED TOP CHORD LENGTH = 3.30 FT.
MAX. UNBRACED BOTTOM CHORD LENGTH = 6.25 FT OR RIGID CEILING DIRECTLY APPLIED.

ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE LATERALLY RESTRAINED.

1 LATERAL BRACE(S) AT 1/ 2 LENGTH OF B-U, C-U, C-S, D-S, D-R, G-R, G-P, I-P, I-O, J-O.

END VERTICAL(S) MUST BE SHEATHED OR HAVE BRACES AS INDICATED IN THE MAX. UNBRACED LENGTH COLUMN OF THE TABLE BELOW

LOADING
TOTAL LOAD CASES: (18)

CHORDS					WEBS				
MAX. FACTORED	FACTORED				MAX. FACTORED	FACTORED			
MEMB.	FORCE	VERT. LOAD	LC1	MAX	MAX.	MEMB.	FORCE	MAX.	FACTORED
	(LBS)	(PLF)	(CS)	(LC)	UNBRAC		(LBS)	(LBS)	MAX
FR-TO		FROM	TO		LENGTH	FR-TO			CSI (LC)
A-B	-3246 / 548	-95.2	-95.2	0.23 (2)	4.54	V-B	-376 / 140		0.37 (9)
B-C	-4161 / 821	-95.2	-95.2	0.45 (2)	3.88	B-U	-562 / 3333		0.75 (3)
C-D	-5466 / 1019	-95.2	-95.2	0.55 (2)	3.36	C-U	-2184 / 505		0.77 (3)
D-E	-5919 / 1082	-95.2	-95.2	0.52 (3)	3.30	C-S	-326 / 1975		0.44 (3)
E-F	-5919 / 1082	-95.2	-95.2	0.52 (3)	3.30	S-D	-1190 / 329		0.42 (3)
F-G	-5919 / 1082	-95.2	-95.2	0.52 (3)	3.30	D-R	-126 / 704		0.16 (3)
G-H	-5514 / 1028	-95.2	-95.2	0.55 (3)	3.34	R-F	-748 / 245		0.74 (10)
H-I	-5514 / 1028	-95.2	-95.2	0.55 (3)	3.34	R-G	-117 / 644		0.14 (2)
I-J	-4250 / 836	-95.2	-95.2	0.45 (3)	3.84	P-G	-1145 / 321		0.40 (2)
J-K	-3458 / 566	-95.2	-95.2	0.27 (3)	4.39	P-I	-316 / 1915		0.43 (2)
W-A	-3415 / 571	0.0	0.0	0.24 (2)	5.76	O-I	-2138 / 498		0.75 (2)
L-K	-3405 / 574	0.0	0.0	0.22 (3)	5.77	O-J	-552 / 3273		0.74 (2)
						M-J	-231 / 136		0.23 (10)
X-W	0 / 0	-134.7	-134.7	0.11 (1)	10.00	A-V	-214 / 2022		0.45 (2)
W-V	-203 / 219	-39.5	-39.5	0.12 (6)	6.25	M-K	-220 / 2098		0.47 (3)
V-U	-254 / 1926	-39.5	-39.5	0.33 (2)	6.25				
U-T	-611 / 4161	-39.5	-39.5	0.57 (2)	6.25				
T-S	-611 / 4161	-39.5	-39.5	0.57 (2)	6.25				
S-R	-807 / 5466	-39.5	-39.5	0.73 (2)	6.25				
R-Q	-790 / 5514	-39.5	-39.5	0.74 (3)	6.25				
Q-P	-790 / 5514	-39.5	-39.5	0.74 (3)	6.25				
P-O	-576 / 4251	-39.5	-39.5	0.58 (3)	6.25				
O-N	-201 / 2057	-39.5	-39.5	0.35 (3)	6.25				
N-M	-201 / 2057	-39.5	-39.5	0.35 (3)	6.25				
M-L	-6 / 13	-39.5	-39.5	0.12 (5)	10.00				

TRUSS HAS BEEN CHECKED FOR UNBALANCED LOADING
AS PER NBCC 4.1.6.2.(8)

WIND LOAD APPLIED IS DERIVED FROM REFERENCE VELOCITY PRESSURE OF (9.2) PSF AT (30-0.0) FT-IN-SX REFERENCE HEIGHT ABOVE GRADE AND USING EXTERNAL PEAK COEFFICIENTS, CpCg, BASED ON THE (MAIN WIND FORCE RESISTING SYSTEM); INTERNAL WIND PRESSURE IS BASED ON DESIGN (CATEGORY 2). BUILDING MAY BE LOCATED ON (ROUGH TERRAIN) AT MINIMUM (1.000) MILES DISTANCE FROM OPEN TERRAIN. AND TRUSS IS DESIGNED TO BE LOCATED AT LEAST (0-0) FT-IN-SX AWAY FROM EAVE. TRUSS UPLIFT IS BASED ON TOP AND BOTTOM CHORD DEAD LOADS OF 6.0 PSF AND 7.4 PSF RESPECTIVELY.

DESIGN CRITERIA

SPECIFIED LOADS:

TOP	CH.	LL =	26.7	PSF
		DL =	6.0	PSF
BOT	CH.	LL =	10.5	PSF
		DL =	7.4	PSF
TOTAL LOAD		=	50.6	PSF

SPACING = 24.0 IN. C/C

LOADING IN FLAT SECTION BASED ON A SLOPE
OF 8.00/12

THIS TRUSS IS DESIGNED FOR COMMERCIAL
OR INDUSTRIAL BUILDING REQUIREMENTS OF
PART 4, NBCC 2015

THIS DESIGN COMPLIES WITH:

- PART 4 OF BCBC 2018 , ABC 2019
- PART 4 OF OBC 2012 (2019 AMENDMENT)
- CSA 086-14
- TPIC 2014

DESIGN ASSUMPTIONS

- SLOPE REDUCTION FACTOR USED
- PERCENTAGE OF GROUND SNOW LOAD IS USER-DEFINED.

(80 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) TIMES IMPORTANCE FACTOR EQUALS 26.7 P.S.F. SPECIFIED ROOF LIVE LOAD

ALLOWABLE DEFL.(LL)= $L/360$ (1.65")
 CALCULATED VERT. DEFL.(LL) = $L/999$ (0.32")
 ALLOWABLE DEFL.(TL)= $L/180$ (3.30")
 CALCULATED VERT. DEFL.(TL) = $L/999$ (0.46")

CANTILEVER DEFLECTION:
ALLOWABLE DEFL.(LL)= $L/120$ (0.19")
CALCULATED VERT. DEFL.(LL) = $L/999$ (0.00")
ALLOWABLE DEFL.(TL)= $L/120$ (0.19")
CALCULATED VERT. DEFL.(TL) = $L/999$ (0.00")

CSI: TC=0.55/1.00 (G-I:3) , BC=0.74/1.00 (P-R:3) ,
WB=0.77/1.00 (C-U:3) , SSI=0.25/1.00 (B-C:3)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10
COMP=1.10 SHEAR=1.10 TENS= 1.10

SNOW LOAD IMPORTANCE FACTOR = 1.00
WIND LOAD IMPORTANCE FACTOR = 1.00
LIVE LOAD IMPORTANCE FACTOR = 1.00
COMPANION LIVE LOAD FACTOR = 1.00

AUTOSOLVE HEELS OFF

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES						
PLATE	GRIP(DRY)		SHEAR		SECTION	
	(PSI)		(PLI)		(PLI)	
	MAX	MIN	MAX	MIN	MAX	MIN
MT20	650	371	1747	788	1987	1873

PLATE PLACEMENT TOL. = 0.250 inches

PLATE ROTATION TOL. = 5.0 Deg.

JSI GRIP= 0.90 (S) (INPUT = 0.90)
JSI METAL= 1.00 (Q) (INPUT = 1.00)

JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	H09TA	1		JT 45147	E22075149

Alpa Roof Truss, Maple

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:07:45 2022 Page 1
 ID:AdsF8nx1Uq6zWc uLADACeywtAv-H28MYVnnuhVxB4UU1BQ8RkrkyXvXLnmrPH57Hyub

Scale = 1:51.8

[illegible]

JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	H10S	1		JT 45147	E22075150

Alpa Roof Truss, Maple

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:07:47 2022 Page 1
 ID:AdsF8nx1Uq6zWc uLADACeywtAv-ERG6zAp2QJlfQUet9cTcW9x4HmKnPQj2ljmCBAyubd

0-0 4-8-4 4-8-4 7-0-11 11-8-15 6-11-7 18-8-6 7-0-11 25-9-2 3-2-14 29-0-0

Scale = 1:49.7

29-0-0

0-0 4-8-4 4-8-4 7-0-11 11-8-15 6-11-7 18-8-6 7-0-11 25-9-2 3-2-14 29-0-0

TOTAL WEIGHT = 148 lb

[illegible]

LATERAL BRACE(S) SHOWN SHALL BE
2X4 SPF#2



[illegible]

LUMBER				
N. L. G. A. RULES				
CHORDS	SIZE		LUMBER	DESCR.
A - B	2x6	DRY	No.2	SPF
B - D	2x4	DRY	No.2	SPF
D - F	2x4	DRY	No.2	SPF
F - G	2x4	DRY	No.2	SPF
N - A	2x4	DRY	No.2	SPF
H - G	2x4	DRY	No.2	SPF
N - K	2x4	DRY	No.2	SPF
K - H	2x4	DRY	No.2	SPF
ALL WEBS EXCEPT	2x3	DRY	No.2	SPF
B - L	2x4	DRY	No.2	SPF
L - E	2x4	DRY	No.2	SPF
J - F	2x4	DRY	No.2	SPF

DRY: SEASONED LUMBER.

PLATES (table is in inches)					
JT	TYPE	PLATES	W	LEN	Y X
A	TMVW+p	MT20	4.0	6.0	2.00 2.00
B	TTWW-h	MT20	6.0	7.0	Edge 2.75
C	TMW+w	MT20	2.0	4.0	
D	TS-t	MT20	3.0	8.0	
E	TMWW-t	MT20	4.0	6.0	
F	TTWW-h	MT20	6.0	7.0	Edge 3.00
G	TMVW+p	MT20	4.0	6.0	1.50 2.00
H	BMV1+p	MT20	2.0	4.0	
I, J, M					
I	BMWW-t	MT20	4.0	6.0	
K	BS-t	MT20	3.0	8.0	
L	BMWWWW-t	MT20	5.0	6.0	
N	BMV1+p	MT20	2.0	4.0	

Edge - INDICATES REFERENCE CORNER OF PLATE
TOUCHES EDGE OF CHORD.

DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER						
<u>BEARINGS</u>						
	FACTORED GROSS REACTION		MAXIMUM FACTORED GROSS REACTION		INPUT BRG	REQRD BRG
	VERT	HORZ	DOWN	HORZ	UPLIFT	IN-SX
JT						
N	1399	0	1399	0	0	MECHANICAL
H	1399	0	1399	0	0	MECHANICAL

A SUITABLE HANGER/MECHANICAL CONNECTION IS REQUIRED AT JOINT N, H. MINIMUM BEARING LENGTH AT JOINT N = 1-8, JOINT H = 1-8.

UNFACTORED REACTIONS							
1ST LCASE		MAX./MIN. COMPONENT REACTIONS					
JT	COMBINED	SNOW	LIVE	PERM.LIVE	WIND	DEAD	SOIL
N	997	609 / 0	0 / 0	0 / 0	0 / 0	389 / 0	0 / 0
H	997	609 / 0	0 / 0	0 / 0	0 / 0	389 / 0	0 / 0

BRACING
TOP CHORD TO BE SHEATHED OR MAX. PURLIN SPACING = 5.62 FT.
MAX. UNBRACED BOTTOM CHORD LENGTH = 10.00 FT OR RIGID CEILING DIRECTLY APPLIED.

1 LATERAL BRACE(S) AT 1/2 LENGTH OF B-M, C-L, E-J, F-I.

END VERTICAL(S) MUST BE SHEATHED OR HAVE BRACES AS INDICATED IN THE MAX. UNBRACED LENGTH COLUMN OF THE TABLE BELOW

LOADING									
TOTAL LOAD CASES: (4)									
CHORDS					WEBS				
MEMB.	MAX. FACTORED FORCE (LBS)	FACTORED VERT. LOAD (PLF)	LC1 MAX CSI (LC)	MAX. UNBRAC LENGTH	MEMB.	MAX. FACTORED FORCE (LBS)	MAX CSI (LC)		
FR-TO		FROM TO			FR-TO				
A-B	-1151 / 0	-78.0	-78.0 0.28 (1)	6.25	M-B	-55 / 72	0.04 (1)		
B-C	-1004 / 0	-78.0	-78.0 0.43 (1)	5.63	B-L	0 / 616	0.10 (1)		
C-D	-1005 / 0	-78.0	-78.0 0.44 (1)	5.62	L-C	-502 / 0	0.39 (1)		
D-E	-1005 / 0	-78.0	-78.0 0.44 (1)	5.62	L-E	0 / 94	0.02 (1)		
E-F	-956 / 0	-78.0	-78.0 0.44 (1)	5.73	J-E	-594 / 0	0.46 (1)		
F-G	-1032 / 0	-78.0	-78.0 0.35 (1)	5.80	J-F	0 / 831	0.13 (1)		
N-A	-1353 / 0	0.0	0.0 0.15 (1)	6.97	I-F	-200 / 0	0.15 (1)		
H-G	-1368 / 0	0.0	0.0 0.24 (1)	6.94	A-M	0 / 709	0.16 (1)		
					I-G	0 / 611	0.14 (1)		
N-M	0 / 0	-18.5	-18.5 0.18 (4)	10.00					
M-L	0 / 684	-18.5	-18.5 0.24 (4)	10.00					
L-K	0 / 957	-18.5	-18.5 0.23 (1)	10.00					
K-J	0 / 957	-18.5	-18.5 0.23 (1)	10.00					
J-I	0 / 525	-18.5	-18.5 0.19 (4)	10.00					
I-H	0 / 0	-18.5	-18.5 0.12 (4)	10.00					

DESIGN CRITERIA

SPECIFIED LOADS:

TOP CH.	LL =	21.0	PSF
	DL =	6.0	PSF
BOT CH.	LL =	0.0	PSF
	DL =	7.4	PSF
TOTAL LOAD	=	34.4	PSF

LOADING IN FLAT SECTION BASED ON A SLOPE
OF 2.00/12 MINIMUM

THIS TRUSS IS DESIGNED FOR RESIDENTIAL
OR SMALL BUILDING REQUIREMENTS OF PART
9, NBCC 2015

THIS DESIGN COMPLIES WITH:

- PART 9 OF BCBC 2018 , ABC 2019
- PART 9 OF OBC 2012 (2019 AMENDMENT)
- CSA 086-14
- TPIC 2014

(55 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) EQUALS 21.0 P.S.F. SPECIFIED ROOF LIVE LOAD

ALLOWABLE DEFL.(LL)= $L/360$ (0.97")
 CALCULATED VERT. DEFL.(LL) = $L/999$ (0.03")
 ALLOWABLE DEFL.(TL)= $L/360$ (0.97")
 CALCULATED VERT. DEFL.(TL) = $L/999$ (0.07")

CSI: TC=0.44/1.00 (C-E:1), BC=0.24/1.00 (L-M:4),
WB=0.46/1.00 (E-J:1), SSI=0.22/1.00 (E-F:1)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10
COMP=1.10 SHEAR=1.10 TENS= 1.10

COMPANION LIVE LOAD FACTOR = 1.00

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES					
PLATE	GRIP(DRY)		SHEAR		SECTION
	(PSI)		(PLI)		(PLI)
	MAX	MIN	MAX	MIN	MAX MIN
MT20	650	371	1747	788	1987 1873


PLATE PLACEMENT TOL. = 0.250 inches

PLATE ROTATION TOL. = 5.0 Deg.

JSI GRIP= 0.84 (B) (INPUT = 0.90)
JSI METAL= 0.42 (A) (INPUT = 1.00)

LATERAL BRACE(S) SHOWN SHALL BE
2X4 SPF#2



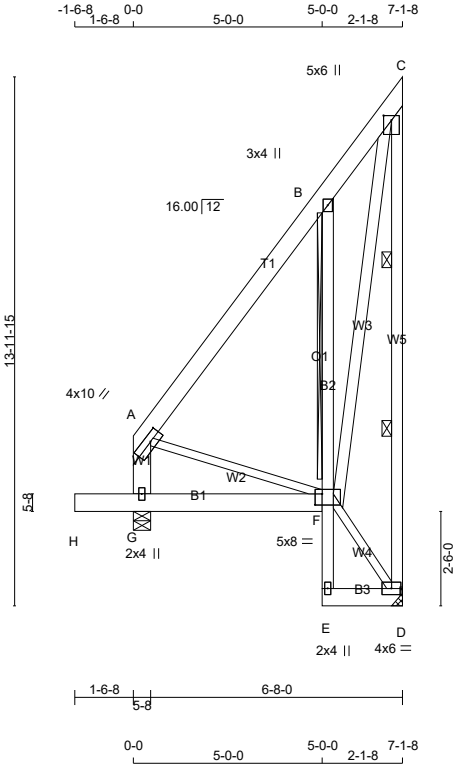

TOTAL WEIGHT = 85 lb

LUMBER				
N. L. G. A. RULES				
CHORDS	SIZE	LUMBER	DESCR.	
G - A	2x6	DRY	No.2	SPF
A - C	2x6	DRY	No.2	SPF
D - C	2x4	DRY	No.2	SPF
H - F	2x6	DRY	No.2	SPF
E - B	2x4	DRY	No.2	SPF
E - D	2x6	DRY	No.2	SPF
ALL WEBS EXCEPT	2x3	DRY	No.2	SPF
F - C	2x4	DRY	No.2	SPF
DRY: SEASONED LUMBER.				

PLATES (table is in inches)					
JT	TYPE	PLATES	W	LEN	Y X
A	TMVW-t	MT20	4.0	10.0	2.00 4.00
B	TMV+p	MT20	3.0	4.0	
C	TMVW+p	MT20	5.0	6.0	1.50 2.50
D	BMVW1-t	MT20	4.0	6.0	
E	BMV+p	MT20	2.0	4.0	
F	BVMWWW-I	MT20	5.0	8.0	3.50 2.25
G	BMV1+p	MT20	2.0	4.0	

DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER

JT	FACTORED GROSS REACTION		MAXIMUM FACTORED GROSS REACTION		INPUT BRG		REQRD BRG	
	VERT	HORZ	DOWN	HORZ	IN-SX	IN-SX	IN-SX	IN-SX
G	1545	0	1545	0	0	5-8	1-10	
D	1396	0	1396	0	0	MECHANICAL		

A SUITABLE HANGER/MECHANICAL CONNECTION IS REQUIRED AT JOINT D. MINIMUM BEARING LENGTH AT JOINT D = 1-8.

UNFACTORED REACTIONS	
1ST LCASE	MAX./MIN. COMPONENT REACTIONS
JT	COMBINED
G	1101
D	995

BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) G

BRACING
TOP CHORD TO BE SHEATHED OR MAX. PURLIN SPACING = 6.25 FT.
MAX. UNBRACED BOTTOM CHORD LENGTH = 7.81 FT OR RIGID CEILING DIRECTLY APPLIED.

ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED.

2 LATERAL BRACE(S) AT 1/ 3 LENGTH OF C-D.
2x4 DRY SPF No.2 T-BRACE AT B-F

FASTEN T AND I-BRACES TO NARROW EDGE OF WEB WITH ONE ROW PER PLY OF 3" COMMON WIRE NAILS @ 6" O.C. WITH 3" MINIMUM END DISTANCE. BRACE MUST COVER 90% OF WEB LENGTH.

END VERTICAL(S) MUST BE SHEATHED OR HAVE BRACES AS INDICATED IN THE MAX. UNBRACED LENGTH COLUMN OF THE TABLE BELOW

LOADING				
TOTAL LOAD CASES: (4)				
CHORDS		FACTORED		WEBS
MEMB.	MAX. FORCE (LBS)	VERT. LOAD (PLF)	LC1 MAX CSI (LC)	MAX. UNBRACED LENGTH
FR-TO		FROM	TO	FR-TO
G- A	-1203 / 0	0.0	0.0	0.09 (1)
A- B	-462 / 0	-316.7	-316.7	0.53 (1)
B- C	-712 / 0	-316.7	-316.7	0.44 (1)
D- C	-1298 / 0	0.0	0.0	0.56 (1)
H- G	0 / 0	-96.5	-96.5	0.08 (1)
G- F	0 / 0	-75.2	-75.2	0.32 (4)
E- F	0 / 83	0.0	0.0	0.08 (1)
F- B	-1471 / 0	0.0	0.0	0.50 (1)
E- D	0 / 19	-75.2	-75.2	0.05 (4)

DESIGN CRITERIA

SPECIFIED LOADS:
TOP CH. LL = 21.0 PSF
DL = 6.0 PSF
BOT CH. LL = 0.0 PSF
DL = 7.4 PSF
TOTAL LOAD = 34.4 PSF

SPACING = 24.0 IN. C/C

GIRDER TYPE: CPrimeHip
SIDE SETBACK = 0-0
END SETBACK = 14-3-0
END WALL WIDTH = 0-0
CORNER FRAMING TYPE: CONVENTIONAL
END JACK TYPE: CONVENTIONAL
APPLIED TO FRONT SIDE
- ADDTL LOADS BASED ON 55 % OF GSL.

THIS TRUSS IS DESIGNED FOR RESIDENTIAL OR SMALL BUILDING REQUIREMENTS OF PART 9, NBCC 2015

THIS DESIGN COMPLIES WITH:
- PART 9 OF BCBC 2018 , ABC 2019
- PART 9 OF OBC 2012 (2019 AMENDMENT)
- CSA 086-14
- TPIC 2014

(55 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) EQUALS 21.0 P.S.F. SPECIFIED ROOF LIVE LOAD

ALLOWABLE DEFL.(LL)= L/360 (0.24")
CALCULATED VERT. DEFL.(LL) = L/ 999 (0.03")
ALLOWABLE DEFL.(TL)= L/360 (0.24")
CALCULATED VERT. DEFL.(TL) = L/ 999 (0.06")

CANTILEVER DEFLECTION:
ALLOWABLE DEFL.(LL)= L/120 (0.19")
CALCULATED VERT. DEFL.(LL) = L/ 999 (0.00")
ALLOWABLE DEFL.(TL)= L/120 (0.19")
CALCULATED VERT. DEFL.(TL) = L/ 999 (0.00")

CSI: TC=0.56/1.00 (C-D:1) , BC=0.50/1.00 (B-F:1) , WB=0.29/1.00 (C-F:1) , SSI=0.36/1.00 (A-B:1)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.00
COMP=1.00 SHEAR=1.00 TENS= 1.00

COMPANION LIVE LOAD FACTOR = 1.00

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES			
PLATE	GRIP(DRY)	SHEAR	SECTION
(PSI)	(PLI)	(PLI)	(PLI)
MAX MIN	MAX MIN	MAX MIN	MAX MIN
MT20	650	371	1747 788 1987 1873

PLATE PLACEMENT TOL. = 0.250 inches

PLATE ROTATION TOL. = 5.0 Deg.

JSI GRIP= 0.89 (C) (INPUT = 0.90)
JSI METAL= 0.54 (F) (INPUT = 1.00)

LATERAL BRACE(S) SHOWN SHALL BE 2X4 SPF#2




JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	J01T		1	TRUSS DESC. JT 45147	E22075161

Alpa Roof Truss, Maple

ID:AdsF8nx1Ug6zWc uLADACeywtAv-ivLwIK1KAq06aF0KCONrFyqlj0VEdcHiRW79q7yubdO

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:08:05 2022 Page 1

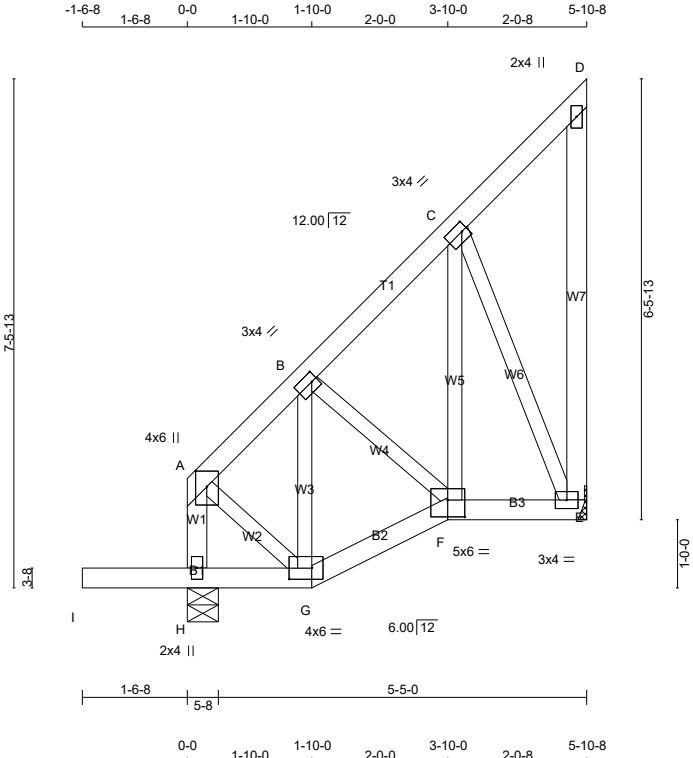

TOTAL WEIGHT = 7 X 39 = 274 lb

LUMBER					
N. L. G. A. RULES					
CHORDS	SIZE	LUMBER	DESCR.		
H - A	2x4	DRY	No.2	SPF	
A - D	2x4	DRY	No.2	SPF	
E - D	2x4	DRY	No.2	SPF	
I - G	2x4	DRY	No.2	SPF	
G - F	2x4	DRY	No.2	SPF	
F - E	2x4	DRY	No.2	SPF	
ALL WEBS	2x3	DRY	No.2	SPF	
DRY: SEASONED LUMBER.					

PLATES (table is in inches)						
JT	TYPE	PLATES	W	LEN	Y	X
A	TMVW+p	MT20	4.0	6.0	2.75	2.00
B	TMWW-t	MT20	3.0	4.0	1.50	1.00
C	TMWW-t	MT20	3.0	4.0	1.50	1.00
D	TMV+p	MT20	2.0	4.0		
E	BMVW1-t	MT20	3.0	4.0		
F	BBWW-l	MT20	5.0	6.0	3.00	3.00
G	BBWW-l	MT20	4.0	6.0	2.00	4.00
H	BMV1+p	MT20	2.0	4.0		

DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER

JT	FACTORED GROSS REACTION		MAXIMUM FACTORED GROSS REACTION		INPUT BRG		REQRD BRG	
	VERT	HORZ	DOWN	HORZ	IN-SX	IN-SX		
H	452	0	452	0	0	5-8	1-8	
E	264	0	264	0	0	MECHANICAL		

A SUITABLE HANGER/MECHANICAL CONNECTION IS REQUIRED AT JOINT E. MINIMUM BEARING LENGTH AT JOINT E = 1-8.

UNFACTORED REACTIONS		1ST LCASE MAX./MIN. COMPONENT REACTIONS					
JT	COMBINED	SNOW	LIVE	PERM.LIVE	WIND	DEAD	SOIL
H	322	197 / 0	0 / 0	0 / 0	0 / 0	125 / 0	0 / 0
E	188	115 / 0	0 / 0	0 / 0	0 / 0	73 / 0	0 / 0

BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) H

BRACING
TOP CHORD TO BE SHEATHED OR MAX. PURLIN SPACING = 6.25 FT.
MAX. UNBRACED BOTTOM CHORD LENGTH = 10.00 FT OR RIGID CEILING DIRECTLY APPLIED.

ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED.

LOADING
TOTAL LOAD CASES: (4)

CHORDS				WEBS			
MEMB.	MAX. FACTORED FORCE (LBS)	FACTORED VERT. LOAD (PLF)	LC1 MAX CSI (LC)	MAX. UNBRAC LENGTH	MEMB.	MAX. FACTORED FORCE (LBS)	MAX CSI (LC)
FR-TO		FROM TO			FR-TO		
H- A	-223 / 0	0.0	0.0 0.02 (1)	7.81	A- G	0 / 123	0.03 (1)
A- B	-133 / 0	-78.0	-78.0 0.04 (1)	6.25	G- B	-145 / 0	0.03 (1)
B- C	-123 / 0	-78.0	-78.0 0.05 (1)	6.25	B- F	-11 / 0	0.00 (1)
C- D	-12 / 0	-78.0	-78.0 0.05 (1)	6.25	F- C	0 / 94	0.02 (4)
E- D	-58 / 0	0.0	0.0 0.05 (1)	7.81	C- E	-206 / 0	0.07 (1)
I- H	0 / 0	-96.5	-96.5 0.16 (1)	10.00			
H- G	0 / 0	-18.5	-18.5 0.16 (1)	10.00			
G- F	0 / 108	-18.5	-18.5 0.03 (4)	10.00			
F- E	0 / 86	-18.5	-18.5 0.03 (4)	10.00			

DESIGN CRITERIA

SPECIFIED LOADS:			
TOP CH.	LL	=	21.0 PSF
	DL	=	6.0 PSF
BOT CH.	LL	=	0.0 PSF
	DL	=	7.4 PSF
TOTAL LOAD	=	34.4	PSF

SPACING = 24.0 IN. C/C

THIS TRUSS IS DESIGNED FOR RESIDENTIAL OR SMALL BUILDING REQUIREMENTS OF PART 9, NBC 2015

THIS DESIGN COMPLIES WITH:
- PART 9 OF BCBC 2018 , ABC 2019
- PART 9 OF OBC 2012 (2019 AMENDMENT)
- CSA 086-14
- TPIC 2014

DESIGN ASSUMPTIONS
-OVERHANG NOT TO BE ALTERED OR CUT OFF.

(55 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) EQUALS 21.0 P.S.F. SPECIFIED ROOF LIVE LOAD

ALLOWABLE DEFL.(LL)= L/360 (0.20")
CALCULATED VERT. DEFL.(LL) = L/ 999 (0.00")
ALLOWABLE DEFL.(TL)= L/360 (0.20")
CALCULATED VERT. DEFL.(TL) = L/ 999 (0.00")

CANTILEVER DEFLECTION:
ALLOWABLE DEFL.(LL)= L/120 (0.19")
CALCULATED VERT. DEFL.(LL) = L/ 999 (0.02")
ALLOWABLE DEFL.(TL)= L/120 (0.19")
CALCULATED VERT. DEFL.(TL) = L/ 569 (0.03")

CSI: TC=0.05/1.00 (D-E:1) , BC=0.16/1.00 (G-H:1) , WB=0.07/1.00 (C-E:1) , SSI=0.12/1.00 (H-I:1)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10
COMP=1.10 SHEAR=1.10 TENS= 1.10

COMPANION LIVE LOAD FACTOR = 1.00

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES					
PLATE	GRIP(DRY)	SHEAR	SECTION		
	(PSI)	(PLI)	(PLI)		
	MAX	MIN	MAX	MIN	MAX
MT20	650	371	1747	788	1987

PLATE PLACEMENT TOL. = 0.250 inches

PLATE ROTATION TOL. = 5.0 Deg.

JSI GRIP= 0.31 (C) (INPUT = 0.90)
JSI METAL= 0.07 (G) (INPUT = 1.00)

LATERAL BRACE(S) SHOWN SHALL BE 2X4 SPF#2



JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	P03A	1		JT 45147	E22075165

Alpa Roof Truss, Maple

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:08:10 2022 Page 1
 ID:AdsF8nx1Uq6zWc uLADACeywtAv-3s9po25T?NfOq0uH?xN0y?O1?1DRItMRboqwVLyubd

0-0 1-6-0 1-6-0 6-5-6 7-11-6 6-4-2 14-3-8 6-4-2 20-7-11 6-4-2 26-11-13 6-5-6 33-5-3 34-11-3

Scale = 1:59.1

16.00 12 2.00 1=10.7 6.1 6x7 6x7 6x1 1.9 6.1

33-11-11

0-0 1-6-0 1-6-0 6-5-6 7-11-6 6-4-2 14-3-8 6-4-2 20-7-11 6-4-2 26-11-13 6-5-6 33-5-3 34-11-3

TOTAL WEIGHT = 113 lb

NUMBER		N. L. G. A. RULES		CHORDS		SIZE	LUMBER		DESCR.	DIMENSIONS, SUPPORTS AND LOADS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER		BEARINGS		DESIGN CRITERIA				
A - C	2x4	DRY	No.2	SPF	FACTORED		MAXIMUM FACTORED		INPUT	REQRD	SPECIFIED LOADS:							
C - E	2x4	DRY	No.2	SPF	GROSS REACTION		GROSS REACTION		BRG	BRG	TOP CH. LL = 21.0 PSF	DL = 6.0 PSF						
E - H	2x4	DRY	No.2	SPF	JT	VERT	HORZ	DOWN	HORZ	UPLIFT	IN-SX	IN-SX						
H - J	2x4	DRY	No.2	SPF	B	95	0	95	0	-12	33-11-11 (10-14811)		BOT CH. LL = 0.0 PSF					
J - L	2x4	DRY	No.2	SPF	T	287	0	287	0	0	33-11-11 (10-14811)		DL = 7.4 PSF					
B - R	2x4	DRY	No.2	SPF	S	684	0	684	0	0	33-11-11 (10-14811)		TOTAL LOAD = 34.4 PSF					
R - O	2x4	DRY	No.2	SPF	Q	598	0	598	0	0	33-11-11 (10-14811)		SPACING = 24.0 IN. C/C					
O - K	2x4	DRY	No.2	SPF	P	607	0	607	0	0	33-11-11 (10-14811)							
ALL WEBS DRY: SEASONED LUMBER.	2x3	DRY	No.2	SPF	N	683	0	683	0	0	33-11-11 (10-14811)		LOADING IN FLAT SECTION BASED ON A SLOPE OF 2.00/12 MINIMUM					
					M	289	0	289	0	0	33-11-11 (10-14811)							
					K	92	0	92	0	-13	33-11-11 (10-14811)							
VALUE IN PARENTHESIS INDICATES EFFECTIVE BEARING LENGTH												THIS TRUSS IS DESIGNED FOR RESIDENTIAL OR SMALL BUILDING REQUIREMENTS OF PART 9, NBCC 2015						
PROVIDE ANCHORAGE AT BEARING JOINT B FOR 150 LBS. FACTORED UPLIFT												THIS DESIGN COMPLIES WITH:						
PROVIDE ANCHORAGE AT BEARING JOINT K FOR 150 LBS. FACTORED UPLIFT												- PART 9 OF BCBC 2018 , ABC 2019						
UNFACTORED REACTIONS												- PART 9 OF OBC 2012 (2019 AMENDMENT)						
JT	TYPE	PLATES	W	LEN	Y	X	1ST LCASE		MAX./MIN. COMPONENT REACTIONS				- CSA 086-14					
B	TMB1-I	MT20	3.0	4.0	1.50	2.75	COMBINED		SNOW	LIVE	PERM.LIVE	WIND	DEAD	SOIL				
C	TTWW-h	MT20	6.0	7.0	1.75	4.00	D	62	70 / 0	0 / 0	0 / 0	0 / 0	0 / -9	0 / 0				
D, F, I							E	211	93 / 0	0 / 0	0 / 0	0 / 0	117 / 0	0 / 0				
E	TMWW-t	MT20	4.0	6.0			S	487	304 / 0	0 / 0	0 / 0	0 / 0	183 / 0	0 / 0				
H	TS-t	MT20	3.0	8.0			Q	427	259 / 0	0 / 0	0 / 0	0 / 0	168 / 0	0 / 0				
G	TMW+w	MT20	2.0	4.0			P	433	264 / 0	0 / 0	0 / 0	0 / 0	169 / 0	0 / 0				
H	TS-t	MT20	3.0	8.0			N	486	303 / 0	0 / 0	0 / 0	0 / 0	183 / 0	0 / 0				
J	TTWW-h	MT20	6.0	7.0	1.75	4.00	M	212	94 / 0	0 / 0	0 / 0	0 / 0	118 / 0	0 / 0				
K	TMB1-I	MT20	3.0	4.0	1.50	2.75	K	60	69 / 0	0 / 0	0 / 0	0 / 0	0 / -9	0 / 0				
M	BMW1+w	MT20	2.0	4.0			BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) B, T, S, Q, P, N, M, K											
N, Q, S							BRACING											
N	BMWW1-t	MT20	4.0	6.0														

LATERAL BRACE(S) SHOWN SHALL BE
2X4 SPF#2



JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	P03B	1		JT 45147	E22075166

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:08:12 2022 Page 1
ID:AdsF8nx1Uq6zWc uLADACeywtAv-?FGZDK6jX v6wK2g7MPU1QTLDr8mmvk25J1aDyubd

0-0 3-0-0 3-0-0 7-3-7 10-3-7 7-2-3 17-5-9 7-2-3 24-7-12 7-3-7 31-11-3 3-0-0 34-11-3

Scale = 1:57.0

6x7 // 16'-0" 4'-0" 3'-10" 7'-3" 10'-3" 7'-2" 17'-5" 7'-2" 24'-7" 7'-3" 31'-11" 3'-0" 34'-11"

3x4 = 2x4 || 4x6 = 3x8 = 4x6 = 3x4 =

Q P O N M L K

33-11-11

0-0 3-0-0 3-0-0 7-3-7 10-3-7 7-2-3 17-5-9 7-2-3 24-7-12 7-3-7 31-11-3 3-0-0 34-11-3

TOTAL WEIGHT = 122 LB

[illegible]

LATERAL BRACE(S) SHOWN SHALL BE
2X4 SPF#2



JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	P03C	1		JT 45147	E22075167

Alpa Roof Truss, Maple

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:08:13 2022 Page 1
ID:AdsF8nx1Uq6zWc uLADACeywtAv-TRqxQ37MII1zYUdsq4xae?YIFE1VCStHI3a6fyubd

0-0 4-6-0 4-6-0 6-6-7 11-0-7 6-5-3 17-5-9 6-5-3 23-10-12 6-6-7 30-5-3 4-6-0 34-11-3

Scale = 1:57.0

6x7 // 6x7 //

16.00' 12

6-10-7 5-10-7 6-1

T1 W1 W2 W1 W2 W1 W2 W1 W1 T1

A B C D E F G H I J

3x4 = 2x4 || 4x6 = 3x8 = 5x6 = 3x8 = 4x6 = 2x4 || 3x4 =


Q P O N M L K


33-11-11


0-0 4-6-0 4-6-0 6-6-7 11-0-7 6-5-3 17-5-9 6-5-3 23-10-12 6-6-7 30-5-3 4-6-0 34-11-3

TOTAL WEIGHT = 134 lb

NUMBER N. L. G. A. RULES CHORDS SIZE LUMBER DESCR. A - C 2x4 DRY No.2 SPF C - F 2x4 DRY No.2 SPF F - H 2x4 DRY No.2 SPF H - J 2x4 DRY No.2 SPF B - O 2x4 DRY No.2 SPF O - M 2x4 DRY No.2 SPF M - I 2x4 DRY No.2 SPF ALL WEBS 2x3 DRY No.2 SPF DRY: SEASONED LUMBER.	DIMENSIONS, SUPPORTS AND LOADINGS BUILDING DESIGNER BEARINGS FACTORED GROSS REACTION DOWN HORZ UPLIFT IN-SX IN-SX MAXIMUM FACTORED GROSS REACTION DOWN HORZ UPLIFT IN-SX IN-SX INPUT BRG BRG REQRD BRG BRG JT B Q P N L K I 322 0 312 0 636 0 794 0 322 0 312 0 636 0 794 0 0 0 0 0 0 0 0 0 33-11-11 (14-0-8) 33-11-11 (14-0-8) 33-11-11 (14-0-8) 33-11-11 (14-0-8) 33-11-11 (14-0-8) 33-11-11 (14-0-8) 33-11-11 (14-0-8) 33-11-11 (14-0-8)	DESIGN CRITERIA SPECIFIED LOADS: TOP CH. LL = 21.0 PSF DL = 6.0 PSF BOT CH. LL = 0.0 PSF DL = 7.4 PSF TOTAL LOAD = 34.4 PSF SPACING = 24.0 IN. C/C LOADING IN FLAT SECTION BASED ON A SLOPE OF 2.00/12 MINIMUM THIS TRUSS IS DESIGNED FOR RESIDENTIAL OR SMALL BUILDING REQUIREMENTS OF PART 9, NBCC 2015 THIS DESIGN COMPLIES WITH: - PART 9 OF BCBC 2018 , ABC 2019 - PART 9 OF OBC 2012 (2019 AMENDMENT) - CSA 086-14 - TPIC 2014 (55 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) EQUALS 21.0 P.S.F. SPECIFIED ROOF LIVE LOAD CSI: TC=0.50/1.00 (D-E:1) , BC=0.16/1.00 (K-L:4) , WB=0.25/1.00 (G-L:1) , SSI=0.24/1.00 (G-H:1) DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10 COMP=1.10 SHEAR=1.10 TENS= 1.10 COMPANION LIVE LOAD FACTOR = 1.00 TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT . NAIL VALUES PLATE GRIP(DRY) SHEAR SECTION (PSI) (PLI) (PLI) MAX MIN MAX MIN MAX MIN MT20 650 371 1747 788 1987 1873 PLATE PLACEMENT TOL. = 0.250 inches PLATE ROTATION TOL. = 5.0 Deg. JSI GRIP= 0.72 (C) (INPUT = 0.90) JSI METAL= 0.34 (F) (INPUT = 1.00)	PLATES (table is in inches) JT TYPE PLATES W LEN Y X B TMB1-I MT20 3.0 4.0 1.50 2.75 C TTWW-h MT20 6.0 7.0 Edge 2.75 D TMWW-t MT20 4.0 6.0 E TMW+w MT20 2.0 4.0 F TS-t MT20 3.0 8.0 G TMWW-t MT20 4.0 6.0 H TTWW-h MT20 6.0 7.0 Edge 2.75 I TMB1-I MT20 3.0 4.0 1.50 2.75 K BMW1+w MT20 2.0 4.0 L BMWW1-t MT20 4.0 6.0 M BS-t MT20 3.0 8.0 N BMWW1-t MT20 5.0 6.0 O BS-t MT20 3.0 8.0 P BMWW1-t MT20 4.0 6.0 Q BMW1+w MT20 2.0 4.0 Edge - INDICATES REFERENCE CORNER OF PLATE TOUCHES EDGE OF CHORD.	UNFACTORED REACTIONS 1ST LCASE MAX./MIN. COMPONENT REACTIONS JT COMBINED SNOW LIVE PERM.LIVE WIND DEAD SOIL B 226 160 / 0 0 / 0 0 / 0 66 / 0 0 / 0 Q 227 109 / 0 0 / 0 0 / 0 118 / 0 0 / 0 P 454 277 / 0 0 / 0 0 / 0 0 / 0 177 / 0 0 / 0 N 562 364 / 0 0 / 0 0 / 0 0 / 0 198 / 0 0 / 0 L 454 277 / 0 0 / 0 0 / 0 0 / 0 177 / 0 0 / 0 K 227 109 / 0 0 / 0 0 / 0 0 / 0 118 / 0 0 / 0 I 226 160 / 0 0 / 0 0 / 0 0 / 0 66 / 0 0 / 0 BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) B, Q, P, N, L, K, I BRACING TOP CHORD TO BE SHEATHED OR MAX. PURLIN SPACING = 6.25 FT. MAX. UNBRACED BOTTOM CHORD LENGTH = 10.00 FT OR RIGID CEILING DIRECTLY APPLIED. ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED. 1 LATERAL BRACE(S) AT 1/ 2 LENGTH OF C-P, D-N, G-N, H-L. LOADING TOTAL LOAD CASES: (4) CHORDS WEBS MAX. FACTORED MAX. FACTORED MAX. FACTORED MEMB. FORCE VERT. LOAD LC1 MAX. MAX. MEMB. FORCE MAX (LBS) (PLF) CSI (LC) UNBRAC LENGTH FR-TO (LBS) CSI (LC) FR-TO FROM TO A- B 0 / 10 -78.0 -78.0 0.01 (1) 10.00 Q- C -203 / 0 0.11 (1) B- C -138 / 0 -78.0 -78.0 0.22 (1) 6.25 C- P -66 / 0 0.03 (1) C- D -27 / 0 -78.0 -78.0 0.48 (1) 6.25 P- D -472 / 0 0.25 (1) D- E 0 / 96 -78.0 -78.0 0.50 (1) 10.00 D- N -163 / 0 0.08 (1) E- F 0 / 96 -78.0 -78.0 0.50 (1) 10.00 N- E -462 / 0 0.25 (1) F- G 0 / 96 -78.0 -78.0 0.50 (1) 10.00 N- G -163 / 0 0.08 (1) G- H -27 / 0 -78.0 -78.0 0.48 (1) 6.25 L- G -472 / 0 0.25 (1) H- I -138 / 0 -78.0 -78.0 0.22 (1) 6.25 L- H -66 / 0 0.03 (1) I- J 0 / 10 -78.0 -78.0 0.01 (1) 10.00 K- H -203 / 0 0.11 (1) B- Q 0 / 81 -18.5 -18.5 0.13 (4) 10.00 Q- P 0 / 78 -18.5 -18.5 0.16 (4) 10.00 P- O 0 / 27 -18.5 -18.5 0.16 (4) 10.00 O- N 0 / 27 -18.5 -18.5 0.16 (4) 10.00 N- M 0 / 27 -18.5 -18.5 0.16 (4) 10.00 M- L 0 / 27 -18.5 -18.5 0.16 (4) 10.00 L- K 0 / 78 -18.5 -18.5 0.16 (4) 10.00 K- I 0 / 81 -18.5 -18.5 0.13 (4) 10.00	LATERAL BRACE(S) SHOWN SHALL BE 2X4 SPF#2
---	---	---	--	--	--

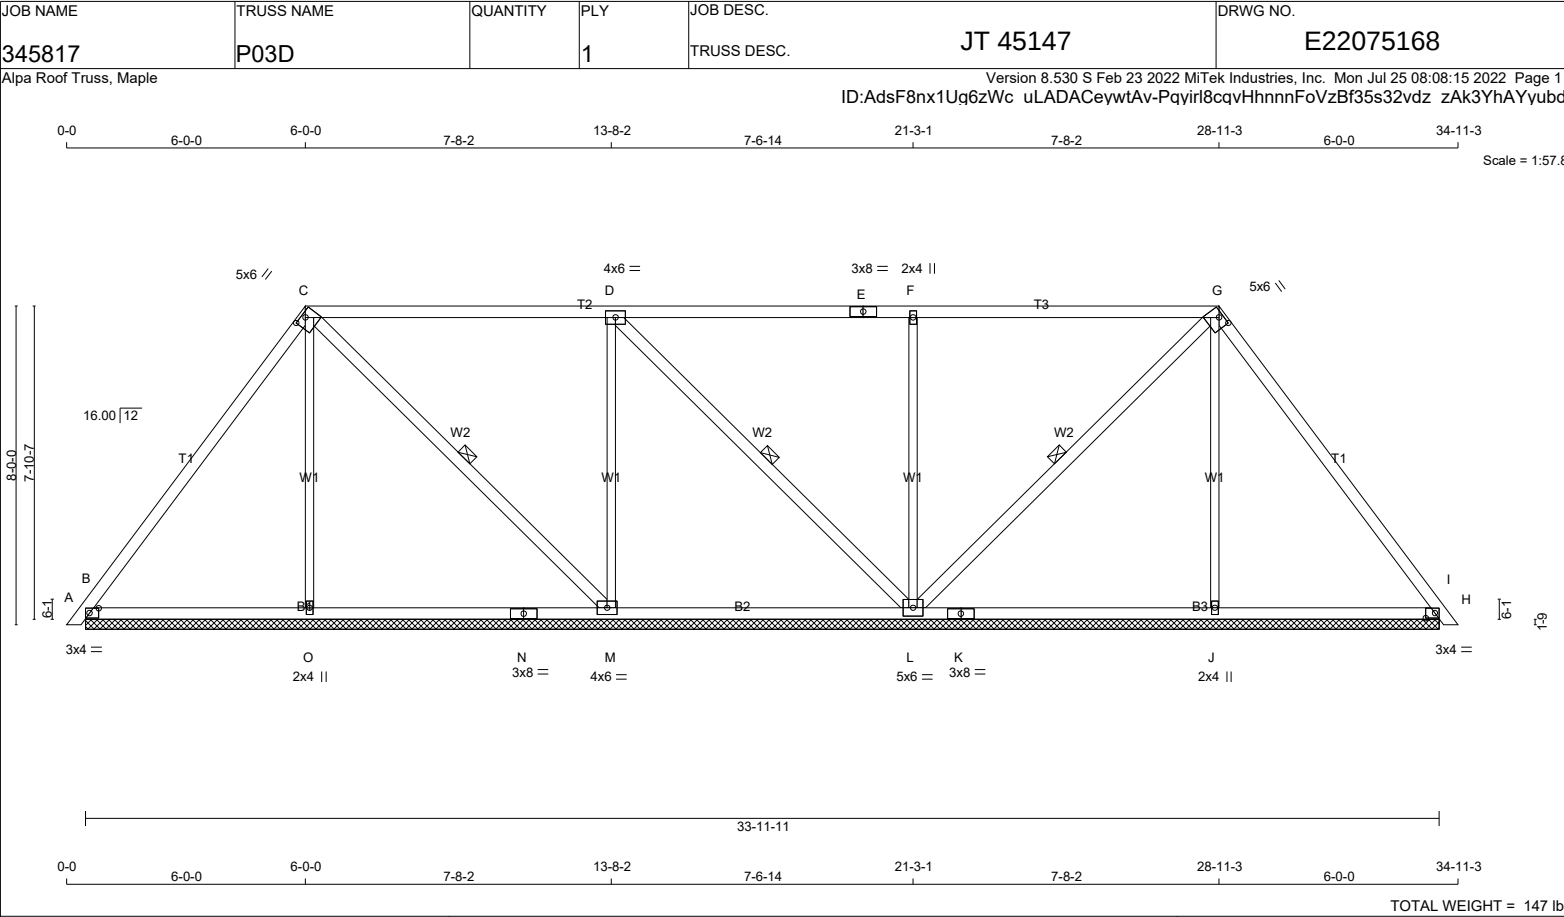

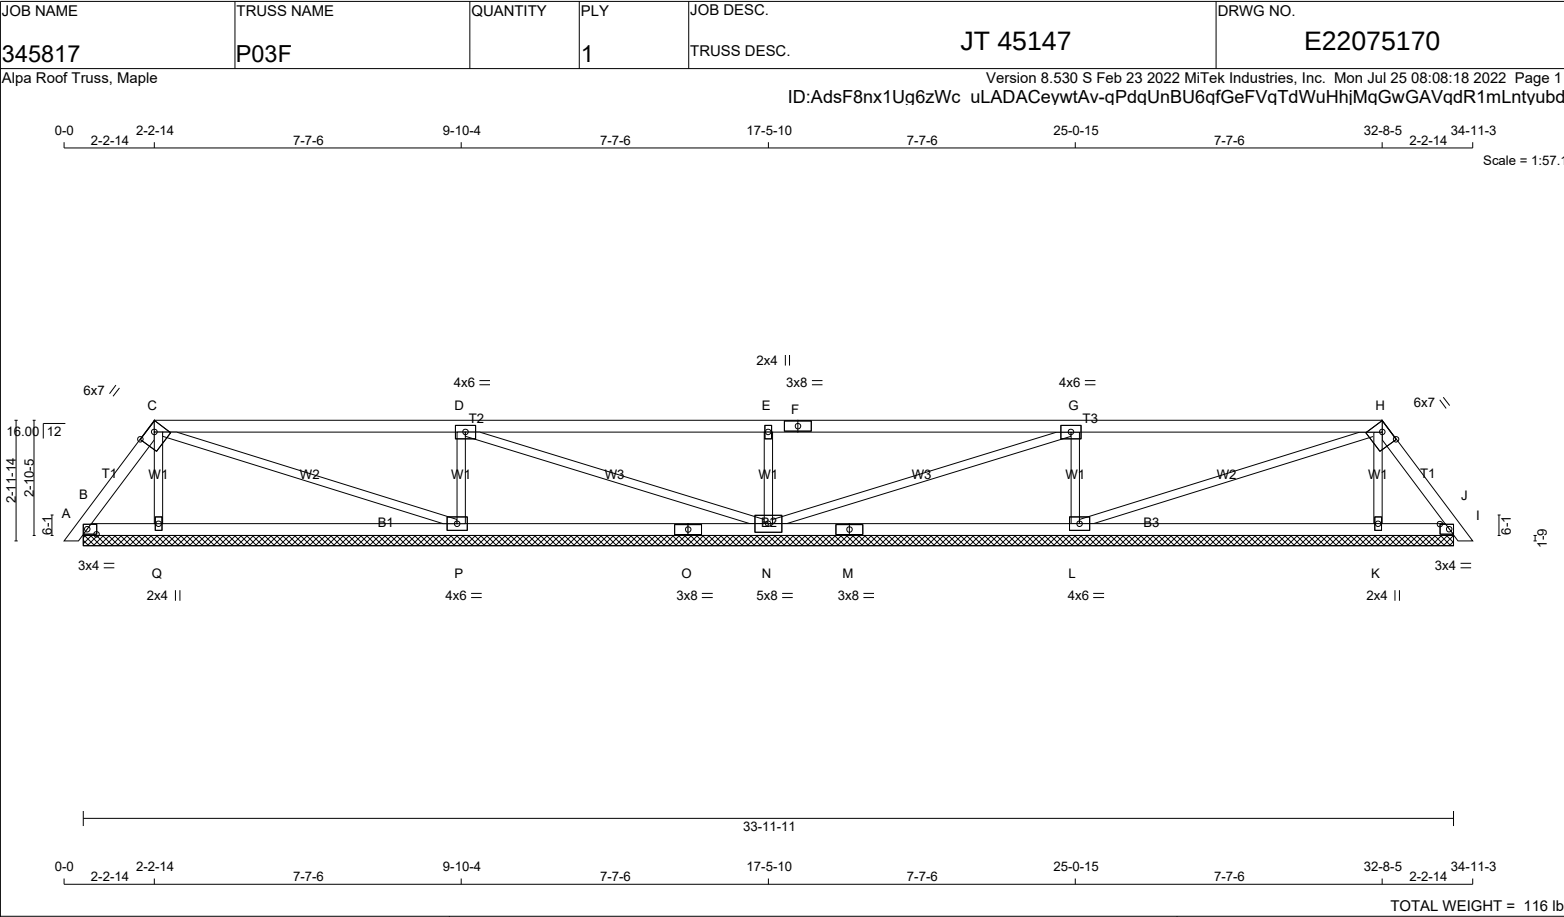

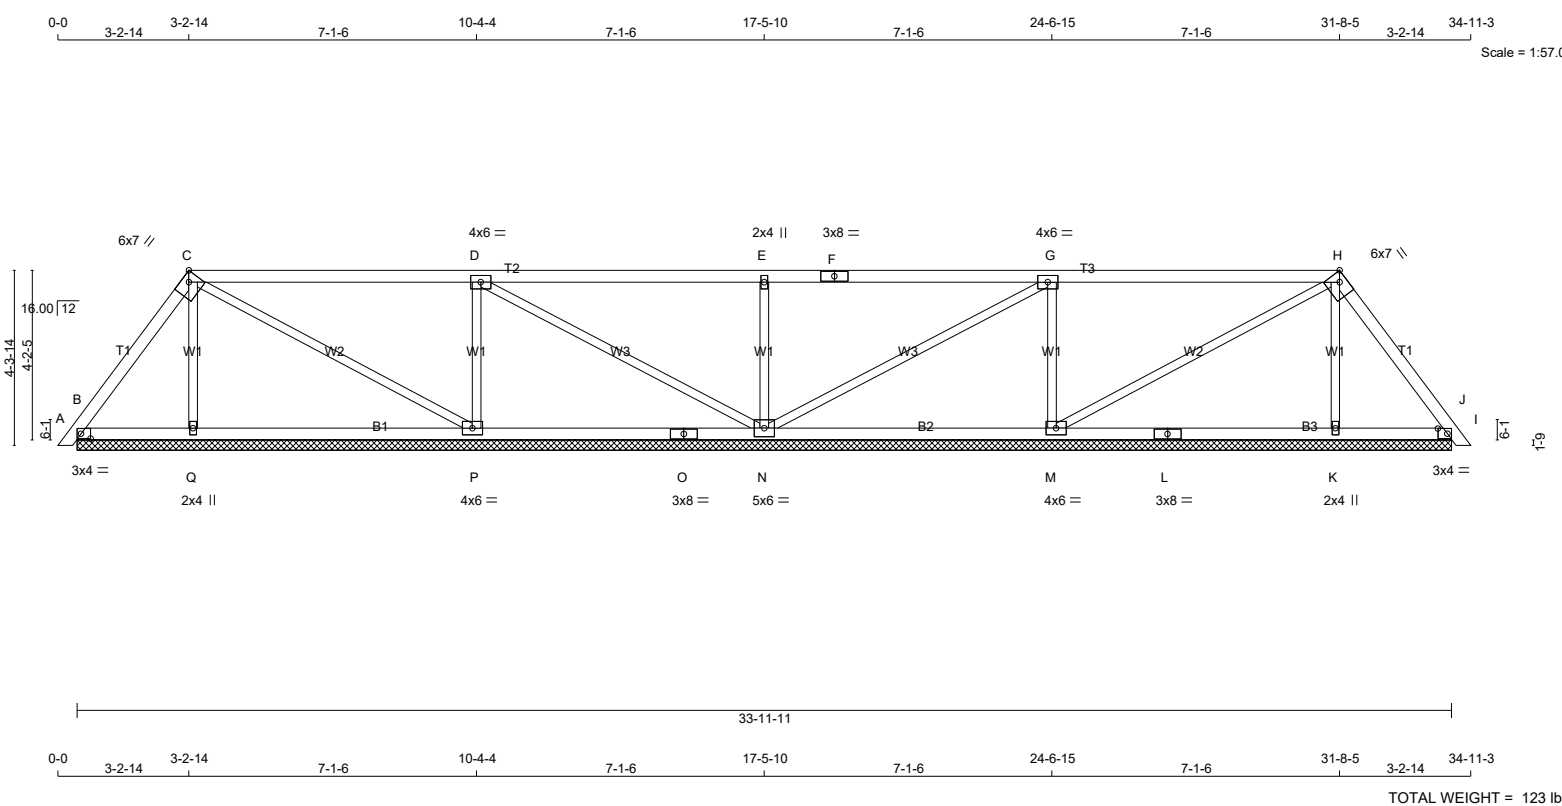

LUMBER					DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER					DESIGN CRITERIA				
N. L. G. A. RULES					BEARINGS					SPECIFIED LOADS:				
CHORDS	SIZE		LUMBER	DESCR.						TOP CH.	LL	=	21.0	PSF
A - C	2x4	DRY	No.2	SPF							DL	=	6.0	PSF
C - F	2x4	DRY	No.2	SPF						BOT CH.	LL	=	0.0	PSF
F - H	2x4	DRY	No.2	SPF							DL	=	7.4	PSF
H - J	2x4	DRY	No.2	SPF						TOTAL LOAD = 34.4 PSF				
B - O	2x4	DRY	No.2	SPF										
O - L	2x4	DRY	No.2	SPF										
L - I	2x4	DRY	No.2	SPF										
ALL WEBS	2x3	DRY	No.2	SPF										
DRY: SEASONED LUMBER.														

PLATES (table is in inches)						
JT	TYPE	PLATES	W	LEN	Y	X
B	TMB1-I	MT20	3.0	4.0	1.50	2.75
C	TTWW-h	MT20	6.0	7.0	Edge	2.75
D	TMWW-t	MT20	4.0	6.0		
E	TMW+w	MT20	2.0	4.0		
F	TS-t	MT20	3.0	8.0		
G	TMWW-t	MT20	4.0	6.0		
H	TTWW-h	MT20	6.0	7.0	Edge	2.75
I	TMB1-I	MT20	3.0	4.0	1.50	2.75
K	BMW1+w	MT20	2.0	4.0		
L	BS-t	MT20	3.0	8.0		
M	BMWW1-t	MT20	4.0	6.0		
N	BMWWW1-t	MT20	5.0	6.0		
O	BS-t	MT20	3.0	8.0		
P	BMWW1-t	MT20	4.0	6.0		
Q	BMW1+w	MT20	2.0	4.0		

Edge - INDICATES REFERENCE CORNER OF PLATE TOUCHES EDGE OF CHORD.

UNFACTORED REACTIONS						
JT	1ST LCASE	MAX./MIN. COMPONENT REACTIONS				
	COMBINED	SNOW	LIVE	PERM.LIVE	WIND	DEAD
B	167	126 / 0	0 / 0	0 / 0	0 / 0	41 / 0
Q	231	112 / 0	0 / 0	0 / 0	0 / 0	118 / 0
P	527	325 / 0	0 / 0	0 / 0	0 / 0	201 / 0
N	528	330 / 0	0 / 0	0 / 0	0 / 0	198 / 0
M	527	325 / 0	0 / 0	0 / 0	0 / 0	201 / 0
K	231	112 / 0	0 / 0	0 / 0	0 / 0	118 / 0
I	167	126 / 0	0 / 0	0 / 0	0 / 0	41 / 0

BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) B, Q, P, N, M, K, I

BRACING
TOP CHORD TO BE SHEATHED OR MAX. PURLIN SPACING = 6.25 FT.
MAX. UNBRACED BOTTOM CHORD LENGTH = 10.00 FT OR RIGID CEILING DIRECTLY APPLIED.

ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED.

LOADING					TOTAL LOAD CASES: (4)				
C H O R D S					W E B S				
MEMB.	MAX. FACTORED FORCE (LBS)	FACTORED VERT. LOAD (PLF)	LC1	MAX CSI (LC)	MAX. UNBRAC LENGTH	MEMB.	MAX. FACTORED FORCE (LBS)	MAX CSI (LC)	
FR-TO		FROM	TO			FR-TO			
A-B	0 / 10	-78.0	-78.0	0.01 (1)	10.00	Q-C	-209 / 0	0.06 (1)	
B-C	-120 / 0	-78.0	-78.0	0.10 (1)	6.25	C-P	-42 / 0	0.06 (1)	
C-D	-27 / 0	-78.0	-78.0	0.58 (1)	6.25	P-D	-585 / 0	0.15 (1)	
D-E	0 / 62	-78.0	-78.0	0.58 (1)	10.00	D-N	-101 / 0	0.14 (1)	
E-F	0 / 62	-78.0	-78.0	0.58 (1)	10.00	N-E	-515 / 0	0.14 (1)	
F-G	0 / 62	-78.0	-78.0	0.58 (1)	10.00	N-G	-101 / 0	0.14 (1)	
G-H	-27 / 0	-78.0	-78.0	0.58 (1)	6.25	M-G	-585 / 0	0.15 (1)	
H-I	-120 / 0	-78.0	-78.0	0.10 (1)	6.25	M-H	-42 / 0	0.06 (1)	
I-J	0 / 10	-78.0	-78.0	0.01 (1)	10.00	K-H	-209 / 0	0.06 (1)	
B-Q	0 / 70	-18.5	-18.5	0.14 (4)	10.00				
Q-P	0 / 64	-18.5	-18.5	0.20 (4)	10.00				
P-O	0 / 27	-18.5	-18.5	0.19 (4)	10.00				
O-N	0 / 27	-18.5	-18.5	0.19 (4)	10.00				
N-M	0 / 27	-18.5	-18.5	0.19 (4)	10.00				
M-L	0 / 64	-18.5	-18.5	0.20 (4)	10.00				
L-K	0 / 64	-18.5	-18.5	0.20 (4)	10.00				
K-I	0 / 70	-18.5	-18.5	0.14 (4)	10.00				

LATERAL BRACE(S) SHOWN SHALL BE 2X4 SPF#2



JOB NAME	TRUSS NAME	QUANTITY	PLY	JOB DESC.	DRWG NO.
345817	P03H	1		JT 45147	E22075172

Version 8.530 S Feb 23 2022 MiTek Industries, Inc. Mon Jul 25 08:08:22 2022 Page 1
ID:AdsF8nx1Ug6zWc uLADACeywtAv-iAtLJ8E?A39h7spbiTbqRXi5CtJ16G2CLfkYweyubd

0-0 4-2-14 4-2-14 6-7-6 10-10-4 6-7-6 17-5-10 6-7-6 24-0-15 6-7-6 30-8-5 4-2-14 34-11-3
Scale = 1:57.0

6x7 // C
16-00 12
5-7-14
5-6-5
6-1
A B
T1
W1
W2
T2
D
4x6 =
2x4 || E
3x8 = F
4x6 = G
T3
H
6x7 // J
T1
W1
W2
W3
W1
W3
W1
B1
B2
Q
P
O
N
M
L
K
3x4 =
2x4 ||
4x6 =
3x8 = 5x6 =
4x6 =
3x8 =
2x4 ||
3x4 =
6-1
1-9
33-11-11
0-0 4-2-14 4-2-14 6-7-6 10-10-4 6-7-6 17-5-10 6-7-6 24-0-15 6-7-6 30-8-5 4-2-14 34-11-3
TOTAL WEIGHT = 131 lb

NUMBER N. L. G. A. RULES CHORDS SIZE LUMBER DESCR. A - C 2x4 DRY No.2 SPF C - F 2x4 DRY No.2 SPF F - H 2x4 DRY No.2 SPF H - J 2x4 DRY No.2 SPF B - O 2x4 DRY No.2 SPF O - L 2x4 DRY No.2 SPF L - I 2x4 DRY No.2 SPF ALL WEBS 2x3 DRY No.2 SPF DRY: SEASONED LUMBER.

PLATES (table is in inches)

JT	TYPE	PLATES	W	LEN	Y	X
B	TMB1-I	MT20	3.0	4.0	1.50	2.75
C	TTWW-h	MT20	6.0	7.0	Edge 2.75	
D	TMWW-t	MT20	4.0	6.0		
E	TMW+w	MT20	2.0	4.0		
F	TS-t	MT20	3.0	8.0		
G	TMWW-t	MT20	4.0	6.0		
H	TTWW-h	MT20	6.0	7.0	Edge 2.75	
I	TMB1-I	MT20	3.0	4.0	1.50	2.75
K	BMW1+w	MT20	2.0	4.0		
L	BS-t	MT20	3.0	8.0		
M	BMWW1-t	MT20	4.0	6.0		
N	BMWWV1-t	MT20	5.0	6.0		
O	BS-t	MT20	3.0	8.0		
P	BMWW1-t	MT20	4.0	6.0		
Q	BMW1+w	MT20	2.0	4.0		

Edge - INDICATES REFERENCE CORNER OF PLATE TOUCHES EDGE OF CHORD.

 DIMENSIONS, SUPPORTS AND LOADINGS FACTORED REACTIONS BEARINGS | JT | FACTORED GROSS REACTION | | MAXIMUM FACTORED GROSS REACTION | | INPUT BRG | | REQRD BRG | | |----|-------------------------|------|---------------------------------|------|-----------|------------------|-----------|--| | | VERT | HORZ | DOWN | HORZ | UPLIFT | IN-SX | IN-SX | | | B | 307 | 0 | 307 | 0 | 0 | 33-11-11 (8-0)33 | | | | Q | 310 | 0 | 310 | 0 | 0 | 33-11-11 (8-0)33 | | | | P | 657 | 0 | 657 | 0 | 0 | 33-11-11 (8-0)33 | | | | N | 788 | 0 | 788 | 0 | 0 | 33-11-11 (8-0)33 | | | | M | 657 | 0 | 657 | 0 | 0 | 33-11-11 (8-0)33 | | | | K | 310 | 0 | 310 | 0 | 0 | 33-11-11 (8-0)33 | | | | I | 307 | 0 | 307 | 0 | 0 | 33-11-11 (8-0)33 | | | VALUE IN PARENTHESIS INDICATES EFFECTIVE BEARING LENGTH UNFACTORED REACTIONS | JT | 1ST LCASE | | MAX./MIN. COMPONENT REACTIONS | | WIND | DEAD | SOIL | |----|-----------|---------|-------------------------------|-----------|-------|---------|-------| | | COMBINED | SNOW | LIVE | PERM.LIVE | | | | | B | 215 | 153 / 0 | 0 / 0 | 0 / 0 | 0 / 0 | 62 / 0 | 0 / 0 | | Q | 226 | 109 / 0 | 0 / 0 | 0 / 0 | 0 / 0 | 117 / 0 | 0 / 0 | | P | 468 | 287 / 0 | 0 / 0 | 0 / 0 | 0 / 0 | 182 / 0 | 0 / 0 | | N | 558 | 359 / 0 | 0 / 0 | 0 / 0 | 0 / 0 | 200 / 0 | 0 / 0 | | M | 468 | 287 / 0 | 0 / 0 | 0 / 0 | 0 / 0 | 182 / 0 | 0 / 0 | | K | 226 | 109 / 0 | 0 / 0 | 0 / 0 | 0 / 0 | 117 / 0 | 0 / 0 | | I | 215 | 153 / 0 | 0 / 0 | 0 / 0 | 0 / 0 | 62 / 0 | 0 / 0 | BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) B, Q, P, N, M, K, I BRACING TOP CHORD TO BE SHEATHED OR MAX. PURLIN SPACING = 6.25 FT. MAX. UNBRACED BOTTOM CHORD LENGTH = 10.00 FT OR RIGID CEILING DIRECTLY APPLIED. ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED. 1 LATERAL BRACE(S) AT 1/ 2 LENGTH OF C-P, D-N, G-N, H-M. LOADING TOTAL LOAD CASES: (4) | CHORDS | | | | WEBS | | | | |--------|---------------------------|---------------------------|----------------|-------|---------------------------|---------------------------|----------| | MEMB. | MAX. FACTORED FORCE (LBS) | FACTORED VERT. LOAD (PLF) | | MEMB. | MAX. FACTORED FORCE (LBS) | MAX. UNBRACED LENGTH (LC) | | | | | FROM | TO | | | FR-TO | | | A- B | 0 / 10 | -78.0 | -78.0 0.01 (1) | 10.00 | Q- C | -203 / 0 | 0.09 (1) | | B- C | -135 / 0 | -78.0 | -78.0 0.19 (1) | 6.25 | C- P | -60 / 0 | 0.03 (1) | | C- D | -27 / 0 | -78.0 | -78.0 0.50 (1) | 6.25 | P- D | -495 / 0 | 0.23 (1) | | D- E | 0 / 91 | -78.0 | -78.0 0.51 (1) | 10.00 | D- N | -151 / 0 | 0.07 (1) | | E- F | 0 / 91 | -78.0 | -78.0 0.51 (1) | 10.00 | N- E | - | | |

[illegible]

NUMBER

N. L. G. A. RULES

CHORDS

SIZE

LUMBER

DESCR.

A - C

2x4

DRY

No.2

SPF

C - F

2x4

DRY

No.2

SPF

F - H

2x4

DRY

No.2

SPF

H - J

2x4

DRY

No.2

SPF

B - O

2x4

DRY

No.2

SPF

O - L

2x4

DRY

No.2

SPF

L - I

2x4

DRY

No.2

SPF

ALL WEBS

2x3

DRY

No.2

SPF

DRY: SEASONED LUMBER.

PLATES (table is in inches)

JT

TYPE

PLATES

W

LEN

Y

X

B

TMB1-I

MT20

3.0

4.0

1.50

2.75

C

TTWW-h

MT20

5.0

6.0

1.25

3.00

D

TMWW-t

MT20

4.0

6.0

E

TMW+w

MT20

2.0

4.0

F

TS-t

MT20

3.0

8.0

G

TMWW-t

MT20

4.0

6.0

H

TTWW-h

MT20

5.0

6.0

1.25

3.00

I

TMB1-I

MT20

3.0

4.0

1.50

2.75

K

BMW1+w

MT20

2.0

4.0

L

BS-t

MT20

3.0

8.0

M

BMWW1-t

MT20

4.0

6.0

N

BMWWWW1-t

MT20

5.0

6.0

O

BS-t

MT20

3.0

8.0

P

BMWW1-t

MT20

4.0

6.0

Q

BMW1+w

MT20

2.0

4.0

DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER

BEARINGS

FACTORED

MAXIMUM FACTORED

INPUT

REQRD

GROSS REACTION

GROSS REACTION

BRG

BRG

DOWN

HORZ

UPLIFT

IN-SX

IN-SX

JT

VERT

HORZ

DOWN

HORZ

UPLIFT

IN-SX

IN-SX

B

362

0

362

0

0

33-11-11 (9-0)39

33-11-11 (9-0)39

Q

309

0

309

0

0

33-11-11 (9-0)39

33-11-11 (9-0)39

P

583

0

583

0

0

33-11-11 (9-0)39

33-11-11 (9-0)39

N

827

0

827

0

0

33-11-11 (9-0)39

33-11-11 (9-0)39

M

583

0

583

0

0

33-11-11 (9-0)39

33-11-11 (9-0)39

K

309

0

309

0

0

33-11-11 (9-0)39

33-11-11 (9-0)39

I

362

0

362

0

0

33-11-11 (9-0)39

33-11-11 (9-0)39

VALUE IN PARENTHESIS INDICATES EFFECTIVE BEARING LENGTH

UNFACTORED REACTIONS

1ST LCASE

MAX./MIN. COMPONENT REACTIONS

JT

COMBINED

SNOW

LIVE

PERM.LIVE

WIND

DEAD

SOIL

B

254

177 / 0

0 / 0

0 / 0

0 / 0

78 / 0

0 / 0

Q

226

106 / 0

0 / 0

0 / 0

0 / 0

120 / 0

0 / 0

P

416

253 / 0

0 / 0

0 / 0

0 / 0

162 / 0

0 / 0

N

585

384 / 0

0 / 0

0 / 0

0 / 0

201 / 0

0 / 0

M

416

253 / 0

0 / 0

0 / 0

0 / 0

162 / 0

0 / 0

K

226

106 / 0

0 / 0

0 / 0

0 / 0

120 / 0

0 / 0

I

254

177 / 0

0 / 0

0 / 0

0 / 0

78 / 0

0 / 0

BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) B, Q, P, N, M, K, I

BRACING

TOP CHORD TO BE SHEATHED OR MAX. PURLIN SPACING = 6.25 FT.

MAX. UNBRACED BOTTOM CHORD LENGTH = 10.00 FT. OR RIGID CEILING DIRECTLY APPLIED.

ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE LATERALLY RESTRAINED.

1 LATERAL BRACE(S) AT 1/2 LENGTH OF C-P, D-N, G-N, H-M.

LOADING

TOTAL LOAD CASES: (4)

CHORDS

WEBS

MEMB.

MAX. FACTORED

FACTORED

MAX. FACTORED

MEMB.

MAX. FACTORED

FORCE

VERT. LOAD

LC1

MAX

MAX.

FORCE

MAX

(LBS)

(PLF)

CSI (LC)

UNBRAC

(LBS)

CSI (LC)

FR-TO

FROM

TO

LENGTH

FR-TO

A- B

0 / 10

-78.0

-78.0

0.01 (1)

10.00

Q- C

-197 / 0

0.16 (1)

B- C

-142 / 0

-78.0

-78.0

0.31 (1)

6.25

C- P

-85 / 0

0.05 (1)

C- D

-22 / 0

-78.0

-78.0

0.42 (1)

6.25

P- D

-409 / 0

0.32 (1)

D- E

0 / 103

-78.0

-78.0

0.44 (1)

10.00

D- N

-185 / 0

0.10 (1)

E- F

0 / 103

-78.0

-78.0

0.44 (1)

10.00

N- E

-443 / 0

0.35 (1)

F- G

0 / 103

-78.0

-78.0

0.44 (1)

10.00

N- G

-185 / 0

0.10 (1)

G- H

-22 / 0

-78.0

-78.0

0.42 (1)

6.25

M- G

-409 / 0

0.32 (1)

H- I

-142 / 0

-78.0

-78.0

0.31 (1)

6.25

M- H

-85 / 0

0.05 (1)

I- J

0 / 10

-78.0

-78.0

0.01 (1)

10.00

K- H

-197 / 0

0.16 (1)

B- Q

0 / 84

-18.5

-18.5

0.13 (4)

10.00

Q- P

0 / 81

-18.5

-18.5

0.14 (4)

10.00

P- O

0 / 23

-18.5

-18.5

0.14 (4)

10.00

O- N

0 / 23

-18.5

-18.5

0.14 (4)

10.00

N- M

0 / 23

-18.5

-18.5

0.14 (4)

10.00

M- L

0 / 81

-18.5

-18.5

0.14 (4)

10.00

L- K

0 / 81

-18.5

-18.5

0.14 (4)

10.00

K- I

0 / 84

-18.5

-18.5

0.13 (4)

10.00

DESIGN CRITERIA

SPECIFIED LOADS:

TOP CH.

LL =

21.0

PSF

DL =

6.0

PSF

BOT CH.

LL =

0.0

PSF

DL =

7.4

PSF

TOTAL LOAD

=

34.4

PSF

SPACING =

24.0

IN. C/C

LOADING IN FLAT SECTION BASED ON A SLOPE OF 2.00/12 MINIMUM

THIS TRUSS IS DESIGNED FOR RESIDENTIAL OR SMALL BUILDING REQUIREMENTS OF PART 9, NBCC 2015

THIS DESIGN COMPLIES WITH:

- PART 9 OF BCBC 2018 , ABC 2019

- PART 9 OF OBC 2012 (2019 AMENDMENT)

- CSA 086-14

- TPIC 2014

(55 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) EQUALS 21.0 P.S.F. SPECIFIED ROOF LIVE LOAD

CSI: TC=0.44/1.00 (E-G:1) , BC=0.14/1.00 (M-N:4) , WB=0.35/1.00 (E-N:1) , SSI=0.23/1.00 (C-D:1)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10 COMP=1.10 SHEAR=1.10 TENS= 1.10

COMPANION LIVE LOAD FACTOR = 1.00

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES

PLATE

GRIP(DRY)

SHEAR

SECTION

(PSI)

(PLI)

(PLI)

MAX MIN

MAX MIN

MAX MIN

MT20

650

371

1747

788

1987

1873

PLATE PLACEMENT TOL. = 0.250 inches


PLATE ROTATION TOL. = 5.0 Deg.

JSI GRIP= 0.84 (C) (INPUT = 0.90)

JSI METAL= 0.23 (F) (INPUT = 1.00)

LATERAL BRACE(S) SHOWN SHALL BE
2X4 SPF#2



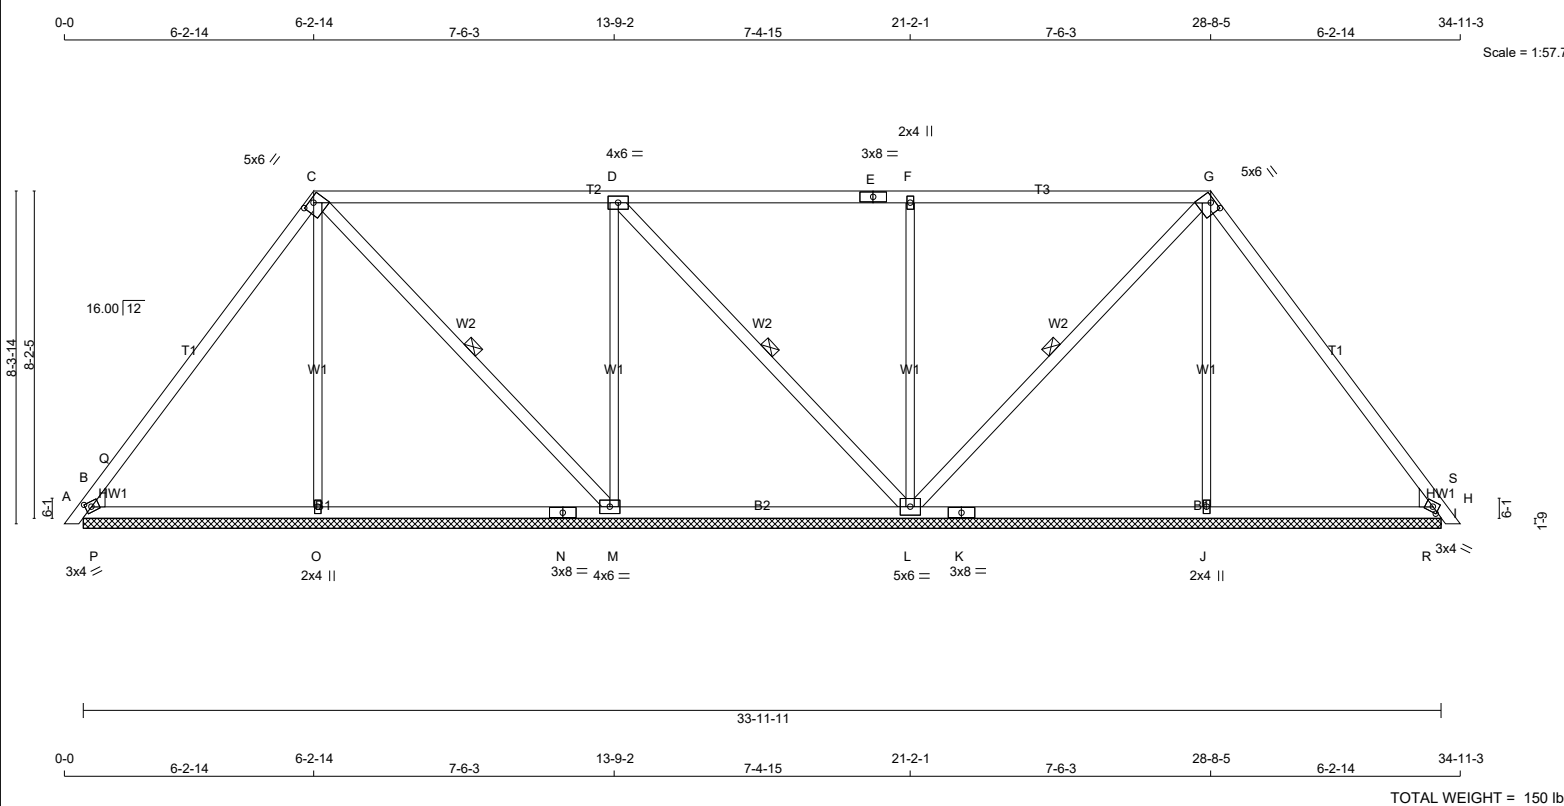

TOTAL WEIGHT = 150 lb

LUMBER				
N. L. G. A. RULES				
CHORDS	SIZE	LUMBER	DESCR.	
A - C	2x4	DRY	No.2	SPF
C - E	2x4	DRY	No.2	SPF
E - G	2x4	DRY	No.2	SPF
G - I	2x4	DRY	No.2	SPF
B - N	2x4	DRY	No.2	SPF
N - K	2x4	DRY	No.2	SPF
K - H	2x4	DRY	No.2	SPF
ALL WEBS	2x3	DRY	No.2	SPF
EXCEPT				
C - M	2x4	DRY	No.2	SPF
D - L	2x4	DRY	No.2	SPF
L - G	2x4	DRY	No.2	SPF
DRY: SEASONED LUMBER.				

PLATES (table is in inches)						
JT	TYPE	PLATES	W	LEN	Y	X
B	TMBH1-m	MT20	3.0	4.0	1.50	1.75
C	TTWW-h	MT20	5.0	6.0	1.25	3.00
D	TMWW-t	MT20	4.0	6.0		
E	TS-t	MT20	3.0	8.0		
F	TMW+w	MT20	2.0	4.0		
G	TTWW-h	MT20	5.0	6.0	1.25	3.00
H	TMBH1-m	MT20	3.0	4.0	1.50	1.75
J	BMW1+w	MT20	2.0	4.0		
K	BS-t	MT20	3.0	8.0		
L	BMWWW1-t	MT20	5.0	6.0		
M	BMWW1-t	MT20	4.0	6.0		
N	BS-t	MT20	3.0	8.0		
O	BMW1+w	MT20	2.0	4.0		

DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER

BEARINGS		FACTORED GROSS REACTION		MAXIMUM FACTORED GROSS REACTION		INPUT BRG		REQRD BRG		HEEL WEDGE	
JT	VERT	HORZ	DOWN	HORZ	UPLIFT	IN-SX	BRG	IN-SX	BRG	IN-SX	WEDGE
B	554	0	554	0	0	33-11-11 (12-0-0)		33-11-11 (12-0-0)		2x6 L	
O	293	0	293	0	0	33-11-11 (12-0-0)		33-11-11 (12-0-0)		2x6 L	
M	663	0	663	0	0	33-11-11 (12-0-0)		33-11-11 (12-0-0)		2x6 L	
L	1073	0	1073	0	0	33-11-11 (12-0-0)		33-11-11 (12-0-0)		2x6 L	
J	278	0	278	0	0	33-11-11 (12-0-0)		33-11-11 (12-0-0)		2x6 L	
H	474	0	474	0	0	33-11-11 (12-0-0)		33-11-11 (12-0-0)		2x6 L	

VALUE IN PARENTHESIS INDICATES EFFECTIVE BEARING LENGTH

UNFACTORED REACTIONS		MAX./MIN. COMPONENT REACTIONS					
JT	1ST LCASE COMBINED	SNOW	LIVE	PERM.LIVE	WIND	DEAD	SOIL
B	389	268 / 0	0 / 0	0 / 0	0 / 0	121 / 0	0 / 0
O	216	93 / 0	0 / 0	0 / 0	0 / 0	123 / 0	0 / 0
M	474	282 / 0	0 / 0	0 / 0	0 / 0	192 / 0	0 / 0
L	758	503 / 0	0 / 0	0 / 0	0 / 0	255 / 0	0 / 0
J	206	85 / 0	0 / 0	0 / 0	0 / 0	121 / 0	0 / 0
H	334	225 / 0	0 / 0	0 / 0	0 / 0	108 / 0	0 / 0

BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) B, O, M, L, J, H

BRACING
TOP CHORD TO BE SHEATHED OR MAX. PURLIN SPACING = 6.25 FT.
MAX. UNBRACED BOTTOM CHORD LENGTH = 10.00 FT OR RIGID CEILING DIRECTLY APPLIED.

ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED.

1 LATERAL BRACE(S) AT 1/ 2 LENGTH OF C-M, D-L, G-L.

LOADING				TOTAL LOAD CASES: (4)			
C H O R D S				W E B S			
MEMB.	MAX. FACTORED FORCE (LBS)	FACTORED VERT. LOAD (PLF)	MAX LC1 CSI (LC)	MAX. UNBRAC LENGTH	MEMB.	MAX. FACTORED FORCE (LBS)	MAX CSI (LC)
FR-TO		FROM TO			FR-TO		
A-B	0 / 10	-78.0 -78.0	0.01 (1)	10.00	O-C	-107 / 0	0.14 (1)
B-Q	-56 / 3	-78.0 -78.0	0.20 (1)	6.25	C-M	-71 / 0	0.04 (1)
Q-C	-350 / 0	-78.0 -78.0	0.32 (1)	6.25	M-D	-481 / 0	0.63 (1)
C-D	-146 / 0	-78.0 -78.0	0.60 (1)	6.25	D-L	-217 / 0	0.14 (1)
D-E	-9 / 2	-78.0 -78.0	0.59 (1)	10.00	L-F	-640 / 0	0.84 (1)
E-F	-9 / 2	-78.0 -78.0	0.59 (1)	10.00	L-G	-201 / 0	0.13 (1)
F-G	-8 / 3	-78.0 -78.0	0.59 (1)	10.00	J-G	-91 / 0	0.12 (1)
G-S	-252 / 0	-78.0 -78.0	0.32 (1)	6.25	P-Q	-634 / 0	0.00 (1)
S-H	-32 / 112	-78.0 -78.0	0.21 (1)	6.25	R-S	-647 / 0	0.00 (1)
H-I	0 / 10	-78.0 -78.0	0.01 (1)	10.00			
B-P	0 / 197	-18.5 -18.5	0.30 (1)	10.00			
P-O	0 / 197	-18.5 -18.5	0.30 (1)	10.00			
O-N	0 / 195	-18.5 -18.5	0.22 (4)	10.00			
N-M	0 / 195	-18.5 -18.5	0.22 (4)	10.00			
M-L	0 / 146	-18.5 -18.5	0.21 (4)	10.00			
L-K	0 / 137	-18.5 -18.5	0.22 (4)	10.00			
K-J	0 / 137	-18.5 -18.5	0.22 (4)	10.00			
J-R	0 / 138	-18.5 -18.5	0.30 (1)	10.00			
R-H	0 / 138	-18.5 -18.5	0.30 (1)	10.00			

DESIGN CRITERIA

SPECIFIED LOADS:
TOP CH. LL = 21.0 PSF
DL = 6.0 PSF
BOT CH. LL = 0.0 PSF
DL = 7.4 PSF
TOTAL LOAD = 34.4 PSF

SPACING = 24.0 IN. C/C

LOADING IN FLAT SECTION BASED ON A SLOPE OF 2.00/12 MINIMUM

THIS TRUSS IS DESIGNED FOR RESIDENTIAL OR SMALL BUILDING REQUIREMENTS OF PART 9, NBCC 2015

THIS DESIGN COMPLIES WITH:
- PART 9 OF CBC 2018 , ABC 2019
- PART 9 OF OBC 2012 (2019 AMENDMENT)
- CSA 086-14
- TPIC 2014

(55 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) EQUALS 21.0 P.S.F. SPECIFIED ROOF LIVE LOAD

CSI: TC=0.60/1.00 (C-D:1) , BC=0.30/1.00 (B-P:1) , WB=0.84/1.00 (F-L:1) , SSI=0.50/1.00 (H-R:1)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10 COMP=1.10 SHEAR=1.10 TENS= 1.10

COMPANION LIVE LOAD FACTOR = 1.00

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES
PLATE GRIP(DRY) SHEAR SECTION (PSI) (PLI) (PLI)
MAX MIN MAX MIN MAX MIN
MT20 650 371 1747 788 1987 1873


PLATE PLACEMENT TOL. = 0.250 inches

PLATE ROTATION TOL. = 5.0 Deg.

JSI GRIP= 0.67 (E) (INPUT = 0.90)
JSI METAL= 0.53 (E) (INPUT = 1.00)

LATERAL BRACE(S) SHOWN SHALL BE 2X4 SPF#2



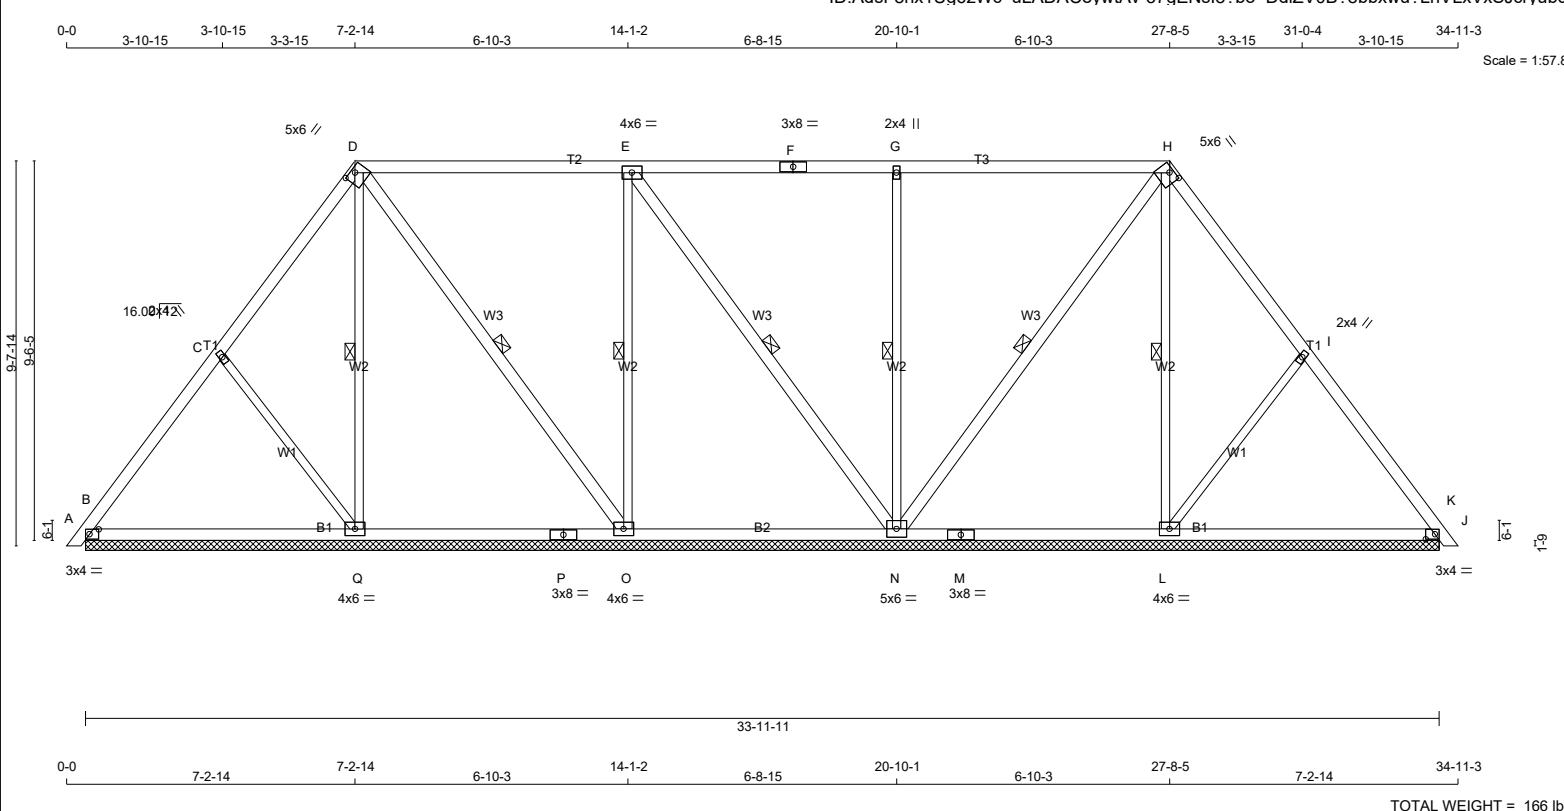

TOTAL WEIGHT = 166 lb

LUMBER				
N. L. G. A. RULES				
CHORDS	SIZE	LUMBER	DESCR.	
A - D	2x4	DRY	No.2	SPF
D - F	2x4	DRY	No.2	SPF
F - H	2x4	DRY	No.2	SPF
H - K	2x4	DRY	No.2	SPF
B - P	2x4	DRY	No.2	SPF
P - M	2x4	DRY	No.2	SPF
M - J	2x4	DRY	No.2	SPF
ALL WEBS	2x3	DRY	No.2	SPF
EXCEPT				
D - O	2x4	DRY	No.2	SPF
E - N	2x4	DRY	No.2	SPF
N - H	2x4	DRY	No.2	SPF
DRY: SEASONED LUMBER.				

PLATES (table is in inches)					
JT	TYPE	PLATES	W	LEN	Y X
B	TMB1-I	MT20	3.0	4.0	1.50 2.75
C, G, I					
D	TMW+w	MT20	2.0	4.0	
E	TTWW-h	MT20	5.0	6.0	1.25 3.00
D	TMWW-t	MT20	4.0	6.0	
F	TS-t	MT20	3.0	8.0	
H	TTWW-h	MT20	5.0	6.0	1.25 3.00
J	TMB1-I	MT20	3.0	4.0	1.50 2.75
L, O, Q					
L	BMWW1-t	MT20	4.0	6.0	
M	BS-t	MT20	3.0	8.0	
N	BMWWW1-t	MT20	5.0	6.0	
P	BS-t	MT20	3.0	8.0	

DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER									
BEARINGS									
JT	FACTORED GROSS REACTION		MAXIMUM FACTORED GROSS REACTION		INPUT BRG		REQRD BRG		
	VERT	HORZ	DOWN	HORZ	UPLIFT	IN-SX	IN-SX		
B	422	0	422	0	0	33-11-11 (12-0-0)			
Q	491	0	491	0	0	33-11-11 (12-0-0)			
O	562	0	562	0	0	33-11-11 (12-0-0)			
N	1047	0	1047	0	0	33-11-11 (12-0-0)			
L	478	0	478	0	0	33-11-11 (12-0-0)			
J	334	0	334	0	0	33-11-11 (12-0-0)			

VALUE IN PARENTHESIS INDICATES EFFECTIVE BEARING LENGTH

UNFACTORED REACTIONS						
JT	1ST LCASE COMBINED	MAX./MIN. COMPONENT REACTIONS				
		SNOW	LIVE	PERM.LIVE	WIND	DEAD
B	298	200 / 0	0 / 0	0 / 0	0 / 0	97 / 0
Q	355	187 / 0	0 / 0	0 / 0	0 / 0	168 / 0
O	402	238 / 0	0 / 0	0 / 0	0 / 0	165 / 0
N	738	499 / 0	0 / 0	0 / 0	0 / 0	239 / 0
L	346	180 / 0	0 / 0	0 / 0	0 / 0	166 / 0
J	236	153 / 0	0 / 0	0 / 0	0 / 0	84 / 0

BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) B, Q, O, N, L, J

BRACING
TOP CHORD TO BE SHEATHED OR MAX. PURLIN SPACING = 6.25 FT.
MAX. UNBRACED BOTTOM CHORD LENGTH = 6.25 FT OR RIGID CEILING DIRECTLY APPLIED.
ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED.

1 LATERAL BRACE(S) AT 1/ 2 LENGTH OF D-Q, D-O, E-O, E-N, G-N, H-N, H-L.

LOADING							
TOTAL LOAD CASES: (4)							
CHORDS				WEBS			
MEMB.	MAX. FACTORED FORCE (LBS)	FACTORED VERT. LOAD (PLF)	LC1 MAX CSI (LC)	MAX. UNBRAC LENGTH	MEMB.	MAX. FACTORED FORCE (LBS)	MAX. CSI (LC)
FR-TO		FROM	TO		FR-TO		
A-B	0 / 10	-78.0	-78.0	0.01 (1)	10.00	C-Q	-201 / 0
B-C	-280 / 0	-78.0	-78.0	0.15 (1)	6.25	Q-D	-190 / 0
C-D	-121 / 0	-78.0	-78.0	0.15 (1)	6.25	D-O	-63 / 0
D-E	-17 / 0	-78.0	-78.0	0.49 (1)	6.25	O-E	-391 / 0
E-F	0 / 123	-78.0	-78.0	0.51 (1)	10.00	E-N	-238 / 0
F-G	0 / 123	-78.0	-78.0	0.51 (1)	10.00	N-G	-583 / 0
G-H	0 / 123	-78.0	-78.0	0.51 (1)	10.00	N-H	-189 / 0
H-I	-12 / 0	-78.0	-78.0	0.15 (1)	6.25	L-H	-175 / 0
I-J	-170 / 0	-78.0	-78.0	0.15 (1)	6.25	L-I	-202 / 0
J-K	0 / 10	-78.0	-78.0	0.01 (1)	10.00		
B-Q	0 / 181	-18.5	-18.5	0.22 (4)	10.00		
Q-P	0 / 55	-18.5	-18.5	0.22 (4)	10.00		
P-O	0 / 55	-18.5	-18.5	0.22 (4)	10.00		
O-N	0 / 17	-18.5	-18.5	0.16 (4)	10.00		
N-M	-10 / 0	-18.5	-18.5	0.21 (4)	6.25		
M-L	-10 / 0	-18.5	-18.5	0.21 (4)	6.25		
L-J	0 / 116	-18.5	-18.5	0.22 (4)	10.00		

DESIGN CRITERIA			
SPECIFIED LOADS:			
TOP	CH.	LL	= 21.0 PSF
		DL	= 6.0 PSF
BOT	CH.	LL	= 0.0 PSF
		DL	= 7.4 PSF
TOTAL LOAD		=	34.4 PSF

SPACING = 24.0 IN. C/C

LOADING IN FLAT SECTION BASED ON A SLOPE OF 2.00/12 MINIMUM

THIS TRUSS IS DESIGNED FOR RESIDENTIAL OR SMALL BUILDING REQUIREMENTS OF PART 9, NBCC 2015

THIS DESIGN COMPLIES WITH:
- PART 9 OF BCBC 2018 , ABC 2019
- PART 9 OF OBC 2012 (2019 AMENDMENT)
- CSA 086-14
- TPIC 2014

(55 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) EQUALS 21.0 P.S.F. SPECIFIED ROOF LIVE LOAD

CSI: TC=0.51/1.00 (E-G:1) , BC=0.22/1.00 (B-Q:4) , WB=0.35/1.00 (G-N:1) , SSI=0.25/1.00 (D-E:1)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10 COMP=1.10 SHEAR=1.10 TENS= 1.10

COMPANION LIVE LOAD FACTOR = 1.00

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES					
PLATE	GRIP(DRY)	SHEAR	SECTION		
	(PSI)	(PLI)	(PLI)		
MT20	650	371	1747	788	1987 1873


PLATE PLACEMENT TOL. = 0.250 inches


PLATE ROTATION TOL. = 5.0 Deg.

JSI GRIP= 0.72 (D) (INPUT = 0.90)
JSI METAL= 0.21 (B) (INPUT = 1.00)

LATERAL BRACE(S) SHOWN SHALL BE 2X4 SPF#2



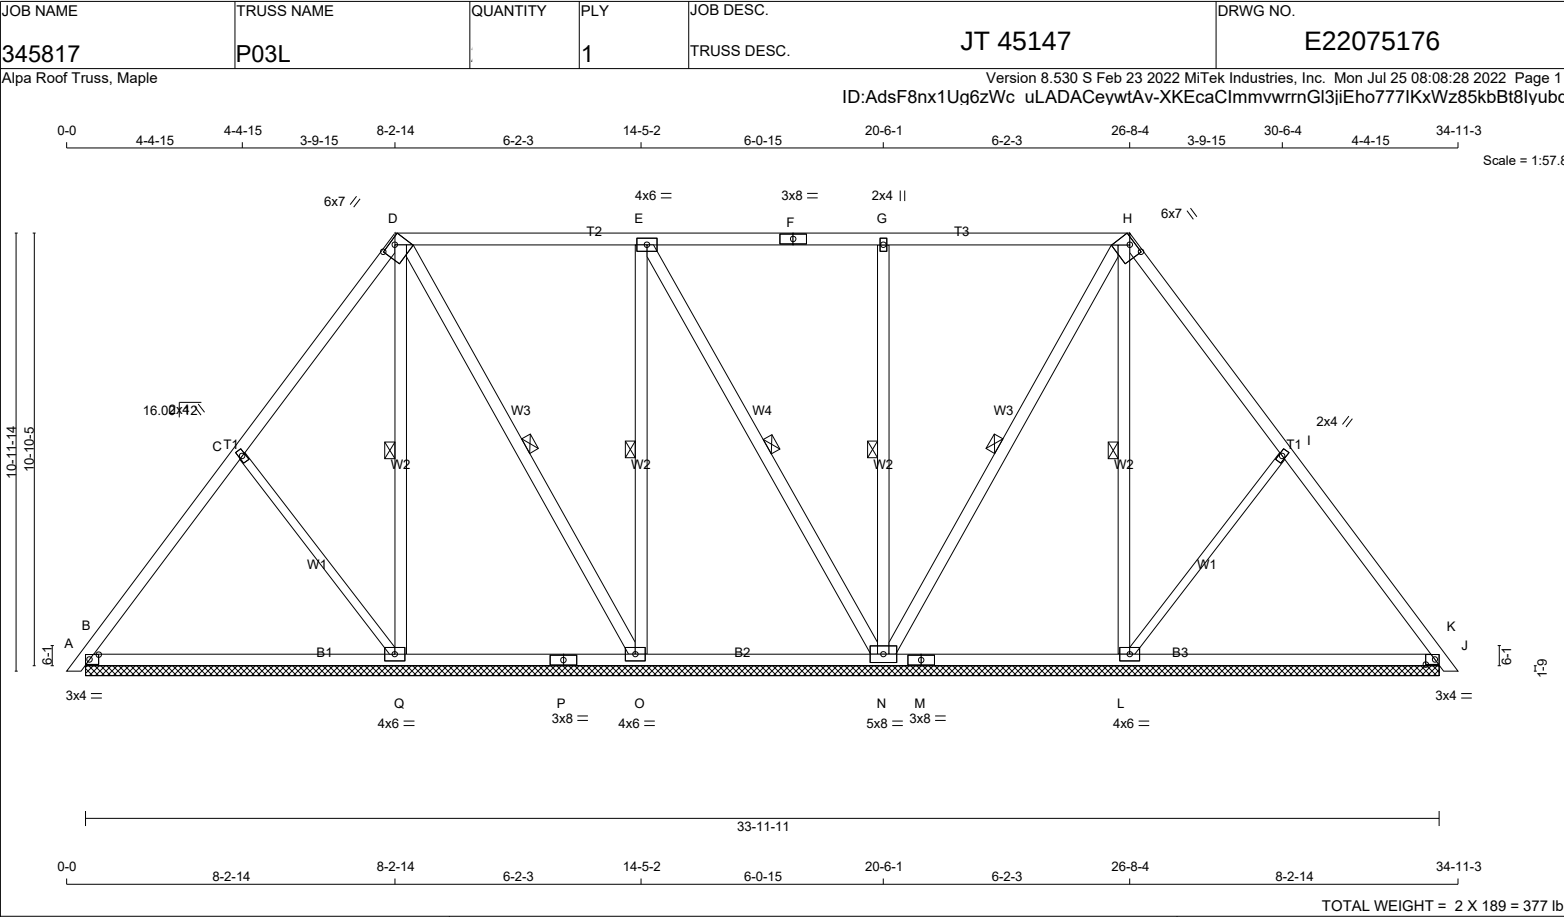

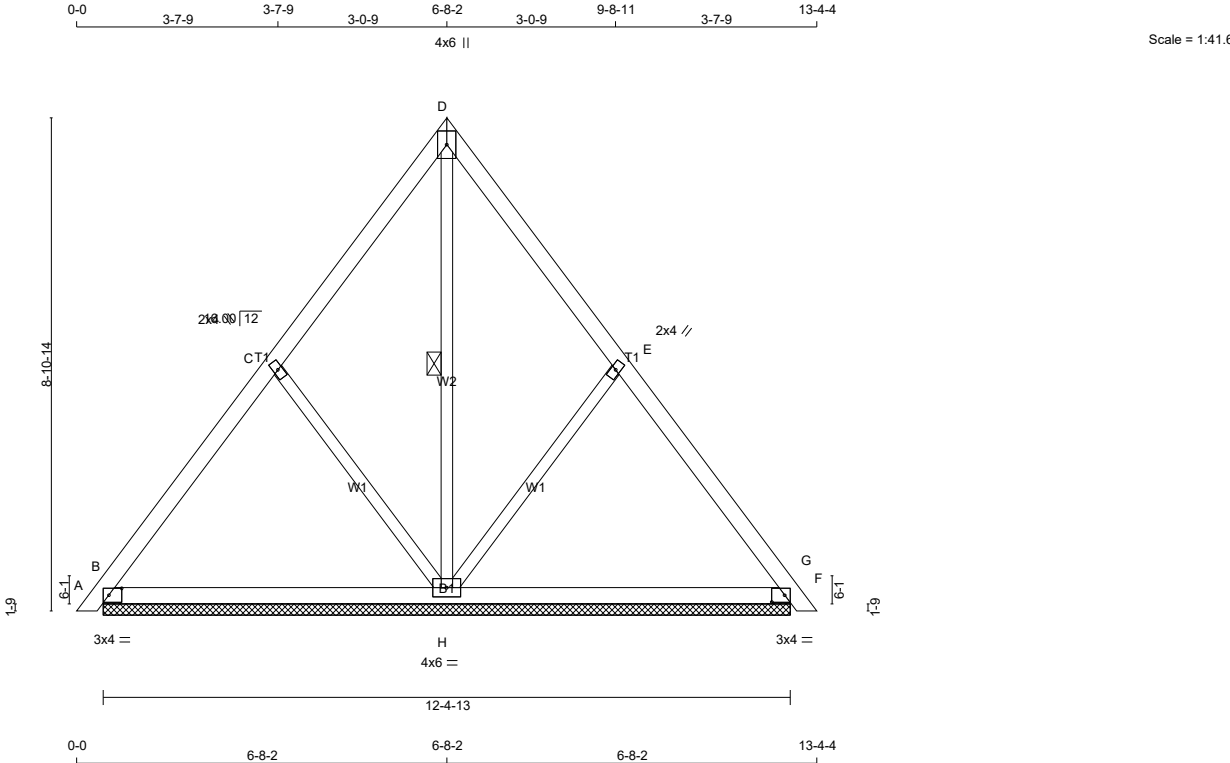

TOTAL WEIGHT = 3 X 54 = 162 lb

LUMBER				
N. L. G. A. RULES				
CHORDS		SIZE	LUMBER	DESCR.
A - D	2x4	DRY	No.2	SPF
D - G	2x4	DRY	No.2	SPF
B - F	2x4	DRY	No.2	SPF
ALL WEBS		2x3	DRY	SPF
DRY: SEASONED LUMBER.				

PLATES (table is in inches)						
JT	TYPE	PLATES	W	LEN	Y	X
B	TMB1-I	MT20	3.0	4.0	1.50	2.75
C	TMW+w	MT20	2.0	4.0		
D	TTW+p	MT20	4.0	6.0		
E	TMW+w	MT20	2.0	4.0		
F	TMB1-I	MT20	3.0	4.0	1.50	2.75
H	BMWW1-I	MT20	4.0	6.0		

DIMENSIONS, SUPPORTS AND LOADINGS SPECIFIED BY FABRICATOR TO BE VERIFIED BY BUILDING DESIGNER

JT	FACTORED GROSS REACTION		MAXIMUM FACTORED GROSS REACTION		INPUT BRG		REQRD BRG	
	VERT	HORZ	DOWN	HORZ	IN-SX	IN-SX	IN-SX	IN-SX
B	324	0	324	0	0	12-4-13	1-8	
F	324	0	324	0	0	12-4-13	1-8	
H	604	0	604	0	0	12-4-13	1-8	

UNFACTORED REACTIONS							
1ST LCASE		MAX / MIN. COMPONENT REACTIONS					
JT	COMBINED	SNOW	LIVE	PERM. LIVE	WIND	DEAD	SOIL
B	229	151 / 0	0 / 0	0 / 0	0 / 0	78 / 0	0 / 0
F	229	151 / 0	0 / 0	0 / 0	0 / 0	78 / 0	0 / 0
H	434	248 / 0	0 / 0	0 / 0	0 / 0	186 / 0	0 / 0

BEARING MATERIAL TO BE SPF NO.2 OR BETTER AT JOINT(S) B, F, H

BRACING
TOP CHORD TO BE SHEATHED OR MAX. PURLIN SPACING = 6.25 FT.
MAX. UNBRACED BOTTOM CHORD LENGTH = 10.00 FT OR RIGID CEILING DIRECTLY APPLIED.

ALL PITCH BREAKS AND PERIMETER CORNER JOINTS MUST BE Laterally RESTRAINED.

1 LATERAL BRACE(S) AT 1/ 2 LENGTH OF D-H.

LOADING
TOTAL LOAD CASES: (4)

CHORDS				WEBS			
MEMB.	MAX. FACTORED FORCE (LBS)	FACTORED VERT. LOAD (PLF)	MAX LC1 CSI (LC)	MAX. UNBRAC LENGTH	MEMB.	MAX. FACTORED FORCE (LBS)	MAX CSI (LC)
FR-TO		FROM TO			FR-TO		
A- B	0 / 10	-78.0 -78.0	0.01 (1)	10.00	H- D	-165 / 0	0.08 (1)
B- C	-180 / 0	-78.0 -78.0	0.13 (1)	6.25	H- E	-185 / 0	0.09 (1)
C- D	-38 / 0	-78.0 -78.0	0.13 (1)	6.25	C- H	-185 / 0	0.09 (1)
D- E	-38 / 0	-78.0 -78.0	0.13 (1)	6.25			
E- F	-180 / 0	-78.0 -78.0	0.13 (1)	6.25			
F- G	0 / 10	-78.0 -78.0	0.01 (1)	10.00			
B- H	0 / 121	-18.5 -18.5	0.21 (4)	10.00			
H- F	0 / 121	-18.5 -18.5	0.21 (4)	10.00			

DESIGN CRITERIA

SPECIFIED LOADS:
TOP CH. LL = 21.0 PSF
DL = 6.0 PSF
BOT CH. LL = 0.0 PSF
DL = 7.4 PSF
TOTAL LOAD = 34.4 PSF

SPACING = 24.0 IN. C/C

THIS TRUSS IS DESIGNED FOR RESIDENTIAL OR SMALL BUILDING REQUIREMENTS OF PART 9, NBCC 2015

THIS DESIGN COMPLIES WITH:
- PART 9 OF BCBC 2018 , ABC 2019
- PART 9 OF OBC 2012 (2019 AMENDMENT)
- CSA 086-14
- TPIC 2014

(55 % OF 23.0 P.S.F. G.S.L. PLUS 8.4 P.S.F. RAIN LOAD) EQUALS 21.0 P.S.F. SPECIFIED ROOF LIVE LOAD

CSI: TC=0.13/1.00 (E-F:1) , BC=0.21/1.00 (F-H:4) , WB=0.09/1.00 (E-H:1) , SSI=0.10/1.00 (F-H:4)

DOL LUMBER=1.00 NAIL=1.00 LS BEND=1.10
COMP=1.10 SHEAR=1.10 TENS= 1.10

COMPANION LIVE LOAD FACTOR = 1.00

TRUSS PLATE MANUFACTURER IS NOT RESPONSIBLE FOR QUALITY CONTROL IN THE TRUSS MANUFACTURING PLANT .

NAIL VALUES
PLATE GRIP(DRY) SHEAR SECTION
(PSI) (PLI) (PLI)
MAX MIN MAX MIN MAX MIN
MT20 650 371 1747 788 1987 1873

PLATE PLACEMENT TOL. = 0.250 inches

PLATE ROTATION TOL. = 5.0 Deg.

JSI GRIP= 0.37 (B) (INPUT = 0.90)
JSI METAL= 0.16 (F) (INPUT = 1.00)

LATERAL BRACE(S) SHOWN SHALL BE 2X4 SPF#2



LUS — Double-Shear Joist Hangers

SIMPSON
Strong-Tie

All LUS hangers have double-shear nailing. This patented innovation distributes the load through two points on each joist nail for greater strength. It also allows the use of fewer nails, faster installation and the use of common nails for all connections.

Material: 18 gauge

Finish: G90 galvanized

Design:


- Factored resistances are in accordance with CSA O86-14 and CSA O86:19.
- Uplift resistances have been increased 15%. No further increase is permitted.
- Wood shear is not considered in the factored resistances given. The specifier must ensure that the joist and header capacities are capable of withstanding these loads.

Installation:


- Use all specified fasteners
- Nails: 16d = 0.162" dia. x 3½" long common wire,
10d = 0.148" x 3" long common wire
- Double-shear nails must be driven at an angle through the joist or truss into the header to achieve the table loads
- Not designed for welded or nailer applications

Options:

- These hangers cannot be modified

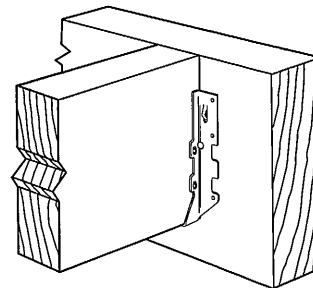


Typical LUS
Installation

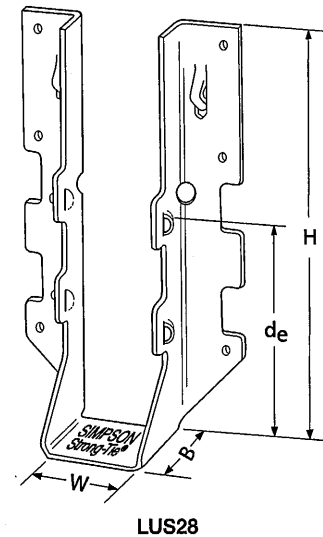


Model No.	Ga.	Dimensions (in.)				Fasteners		Factored Resistance (lb.)			
								D-Fir-L		S-P-F	
		W	H	B	d _o ¹	Face	Joist	Uplift (K _o =1.15)	Normal (K _o =1.00)	Uplift (K _o =1.15)	Normal (K _o =1.00)
LUS24	18	1⅞	3⅞	1¼	1⅝	(4) 10d	(2) 10d	710	1630	645	1155
LUS24-2	18	3⅞	3⅞	2	1⅝	(4) 16d	(2) 16d	835	2020	590	1435
LUS26	18	1⅞	4¾	1¼	3⅝	(4) 10d	(4) 10d	1420	2170	1290	1630
LUS26-2	18	3⅞	4¾	2	4	(4) 16d	(4) 16d	1720	2595	1545	1920
LUS26-3	18	4⅝	4¾	2	3¼	(4) 16d	(4) 16d	1720	2595	1545	2340
LUS28	18	1⅞	6⅝	1¼	3¾	(6) 10d	(6) 10d	1420	2520	1290	1790
LUS28-2	18	3⅞	7	2	4	(6) 16d	(4) 16d	1720	3325	1545	2575
LUS28-3	18	4⅝	6¼	2	3¼	(6) 16d	(4) 16d	1720	3325	1545	2375
LUS210	18	1⅞	7⅞	1¼	3⅞	(8) 10d	(4) 10d	1420	2785	1290	2210
LUS210-2	18	3⅞	9	2	6	(8) 16d	(6) 16d	2580	4500	2320	3195
LUS210-3	18	4⅝	8⅞	2	5¼	(8) 16d	(6) 16d	2580	3345	2320	2375

1. d_o is the distance from the seat of the hanger to the highest joist nail.



Dome double-shear nailing prevents tabs breaking off (available on some models).

US Patent
5,603,580



Double-shear nailing top view.



This technical bulletin is effective until December 31, 2024, and reflects information available as of July 1, 2022. This information is updated periodically and should not be relied upon after December 31, 2024. Contact Simpson Strong-Tie for current information and limited warranty or see strongtie.com.

© 2022 Simpson Strong-Tie Company Inc. • P.O. Box 10789, Pleasanton, CA 94588

T-SPECLUS22 7/22 exp. 12/24

(800) 999-5099
strongtie.com

HUS/LJS — Double-Shear Joist Hangers

All hangers have double-shear nailing. This patented innovation distributes the load through two points on each joist nail for greater strength. It also allows the use of fewer nails, faster installation and the use of common nails for all connections. Do not bend or remove tabs.

Material: See table

Finish: G90 galvanized

Design:


- Factored resistances are in accordance with CSA O86-14 and CSA O86:19.
- Uplift resistances have been increased 15%. No further increase is permitted.
- Wood shear is not considered in the factored resistances given. The specifier must ensure that the joist and header capacities are capable of withstanding these loads.

Installation:


- Use all specified fasteners
- Nails: 16d = 0.162" dia. x 3½" long common wire
- Double-shear nails must be driven at an angle through the joist or truss into the header to achieve the table loads
- Not designed for welded or nailer applications

Options:


- See current catalogue for options

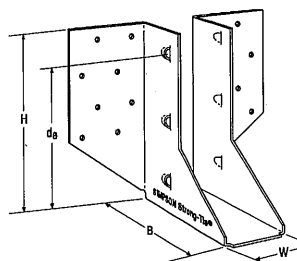


LJS26DS




HUS210
(HUS26, HUS28, similar)

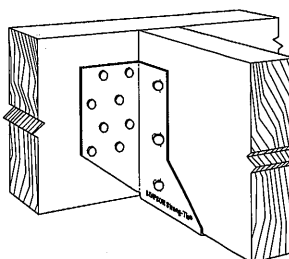

Typical LJS26DS Installation

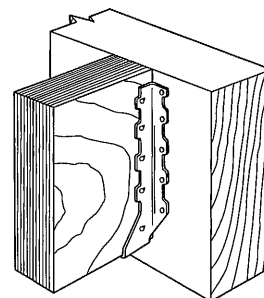


Typical HUS Installation




Typical HUS Installation
(Truss designer to provide fastener quantity for connecting multiple members together)

Model No.	Ga.	Dimensions (in.)				Fasteners		Factored Resistance (lb.)			
		W	H	B	d _e ¹	Face	Joist	D.Fir-L		S-P-F	
								Uplift (K _o =1.15)	Normal (K _o =1.00)	Uplift (K _o =1.15)	Normal (K _o =1.00)
LJS26DS	18	1⅞	5	3½	4⅝	(16) 16d	(6) 16d	2055	4265	1460	4115
HUS26	16	1⅝	5⅝	3	3⅞	(14) 16d	(6) 16d	2705	4940	2065	3875
HUS28	16	1⅝	7⅞	3	6⅞	(22) 16d	(8) 16d	3605	5365	2675	4345
HUS210	16	1⅝	9⅞	3	7⅞	(30) 16d	(10) 16d	4505	5795	4010	4740
HUS1.81/10	16	1⅞	9	3	8	(30) 16d	(10) 16d	4505	6450	4010	5200


1. d_e is the distance from the seat of the hanger to the highest joist nail.



Dome double-shear nailing prevents tabs breaking off (available on some models).
US Patent 5,603,580



Double-shear nailing side view. Do not bend tab back.



Double-shear nailing top view.



This technical bulletin is effective until December 31, 2024, and reflects information available as of July 1, 2022. This information is updated periodically and should not be relied upon after December 31, 2024. Contact Simpson Strong-Tie for current information and limited warranty or see strongtie.com.

© 2022 Simpson Strong-Tie Company Inc. • P.O. Box 10789, Pleasanton, CA 94588

T-SPECHUS22 7/22 exp. 12/24

(800) 999-5099
strongtie.com

HHUS — Double-Shear Joist Hangers

SIMPSON
Strong-Tie

All HHUS hangers have double-shear nailing. This patented innovation distributes the load through two points on each joist nail for greater strength. It also allows the use of fewer nails, faster installation and the use of common nails for all connections. Do not bend or remove tabs.

Material: 14 gauge

Finish: G90 galvanized

Design:


- Factored resistances are in accordance with CSA O86-14 and CSA O86:19.
- Uplift resistances have been increased 15%. No further increase is permitted.
- Wood shear is not considered in the factored resistances given. The specifier must ensure that the joist and header capacities are capable of withstanding these loads.

Installation:


- Use all specified fasteners
- Nails: 16d = 0.162" dia. x 3½" long common wire
- Double-shear nails must be driven at an angle through the joist or truss into the header to achieve the table loads
- Not designed for welded or nailer applications

Options:


- See current catalogue for options

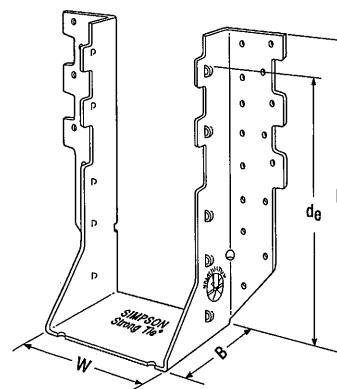

HHUS410

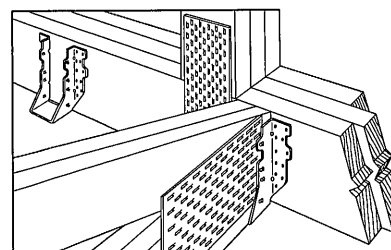


Typical HHUS Installation
(Truss designer to provide fastener quantity for connecting multiple members together)

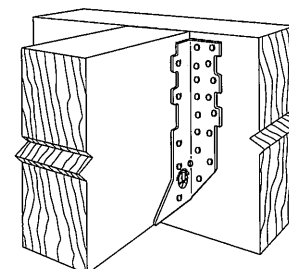


Typical HHUS Installation

Model No.	Ga.	Dimensions (in.)				Fasteners		Factored Resistance (lb.)			
		W	H	B	d _g ¹	Face	Joist	D-Fir-L		S-P-F	
								Uplift (K _g =1.15)	Normal (K _g =1.00)	Uplift (K _g =1.15)	Normal (K _g =1.00)
HHUS26-2	14	3 1/16	5 1/16	3	3 1/16	(14) 16d	(6) 16d	2850	7335	2065	5205
HHUS28-2	14	3 1/16	7 1/32	3	6 3/32	(22) 16d	(8) 16d	3765	8940	2675	6345
HHUS210-2	14	3 1/16	9 3/32	3	8	(30) 16d	(10) 16d	4670	9660	4235	7000
HHUS210-3	14	4 1/16	9	3	7 1/16	(30) 16d	(10) 16d	4670	9670	4235	6865
HHUS210-4	14	6 1/8	8 29/32	3	7 27/32	(30) 16d	(10) 16d	4670	10155	4235	7210
HHUS46	14	3 5/8	5 1/32	3	3 1/16	(14) 16d	(6) 16d	2540	7335	2065	5205
HHUS48	14	3 5/8	7 1/8	3	6 1/8	(22) 16d	(8) 16d	3765	8945	2267	6345
HHUS410	14	3 5/8	9	3	8	(30) 16d	(10) 16d	4670	9855	4235	7000
HHUS5.50/10	14	5 1/2	9	3	8	(30) 16d	(10) 16d	4670	10155	4235	7210
HHUS7.25/10	14	7 1/4	9	3 5/16	7 29/32	(30) 16d	(10) 16d	4670	10155	3370	7210


1. d_g is the distance from the seat of the hanger to the highest joist nail.



Dome double-shear nailing prevents tabs breaking off (available on some models).
US Patent 5,603,580



Double-shear nailing side view. Do not bend tab back.



Double-shear nailing top view.



This technical bulletin is effective until December 31, 2024, and reflects information available as of July 1, 2022. This information is updated periodically and should not be relied upon after December 31, 2024. Contact Simpson Strong-Tie for current information and limited warranty or see strongtie.com.

© 2022 Simpson Strong-Tie Company Inc. • P.O. Box 10789, Pleasanton, CA 94588

T-SPECHHUS22 7/22 exp. 12/24

(800) 999-5099
strongtie.com

TC – Truss Connectors

SIMPSON
Strong-Tie

The TC truss connector is an ideal connector for scissor trusses and can allow horizontal movement up to 1¼". The TC also attaches trusses to top plates or sill plates to resist uplift forces, and is typically used on one or both ends of truss as determined by the building designer.

Material: 16 gauge

Finish: G90 galvanized


Design: Factored resistances are in accordance with CSA O86-14 and CSA O86:19

Installation:


- Use all specified fasteners.
- Nails: 10d = 0.148" dia. x 3" long common wire, 10d x 1½" = 0.148" dia. x 1½" long.
- Drive 10d nails into the truss at the inside end of the slotted holes (inside end is towards the centre of the truss) and clinch on the back side. Do not seat these nails into the truss — allow room under the nail head for movement of the truss with respect to the wall.

Optional TC Installation:


- Bend one flange up 90°. Drive specified nails into the top and face of the top plates or install Titen® screws into the top and face of masonry wall. See optional load tables and installation details.

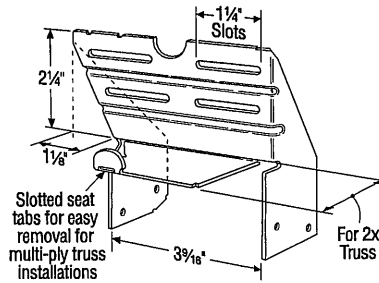


TC24
US Patent 4,932,173

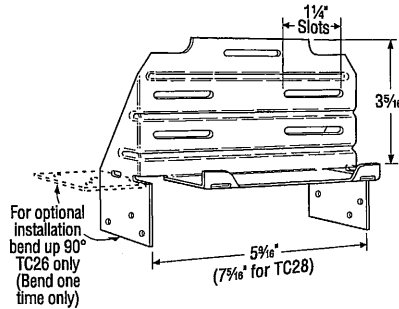


TC26
(TC28 Similar)

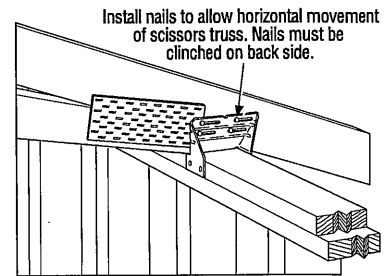

Typical TC24 Installation

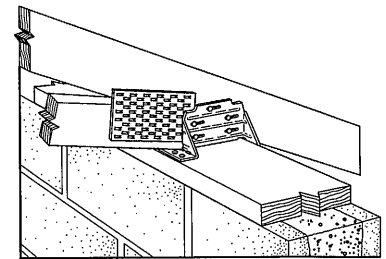

Optional TC26 Installation for Grouted Concrete Block using a Wood Nailer
(8", 10", 12" Wall Installation Similar)




Optional TC26 Installation for Grouted Concrete Block using Titen Screws

Model No.	Fasteners		Factored Resistance	
	Truss	Wall Plates	D.Fir-L	S-P-F
			Uplift (K ₀ =1.15)	Uplift (K ₀ =1.15)
			lb.	lb.
TC24	(4) 10d	(4) 10d	605	430
TC26	(5) 10d	(6) 10d	1015	720
TC28	(5) 10d	(6) 10d	1015	720

Optional TC Installation Table

Model No.	Fasteners		Factored Resistance	
	Truss	Wall Plates	D.Fir-L	S-P-F
			Uplift (K ₀ =1.15)	Uplift (K ₀ =1.15)
			lb.	lb.
TC26	(5) 10d	(6) 10d x 1½"	810	660
	(5) 10d	(6) 10d	930	660

1. Factored resistances have been increased 15% for earthquake or wind loading; no further increase allowed; reduce where other loads govern.
2. Grout strength is 15 MPa minimum.
3. Optional TC26 installation with 10d nails requires minimum 3" top plate thickness.
4. TC26 fastened to grouted concrete block with (6) – ¾" x 2¼" Titen screws has a factored uplift resistance of 275 lb.



This technical bulletin is effective until December 31, 2024, and reflects information available as of July 1, 2022. This information is updated periodically and should not be relied upon after December 31, 2024. Contact Simpson Strong-Tie for current information and limited warranty or see strongtie.com.

© 2022 Simpson Strong-Tie Company Inc. • P.O. Box 10789, Pleasanton, CA 94588

T-SPECTC22 7/22 exp. 12/24

(800) 999-5099
strongtie.com

H — Seismic and Hurricane Ties

SIMPSON

Strong-Tie

The H connector series provides wind and seismic ties for trusses and rafters.

Material: 18 gauge

Finish: G90 galvanized

Design:


- Factored resistances are in accordance with CSA O86-14 and CSA O86:19.
- Factored resistances have been increased 15%. No further increase is permitted.

Installation:

- Use all specified fasteners
- Nails: 8d = 0.131" dia. x 2½" long common wire, 8d x 1½" = 0.131" x 1½" long, 10d x 1½" = 0.146" x 1½" long
- H1 can be installed with flanges facing outwards
- Hurricane ties do not replace solid blocking


Factored resistances for more than one direction for a single connection cannot be added together. A factored load which can be divided into components in the directions given must be evaluated as follows: Factored Shear/Resisting Shear + Factored Tension/Resisting Tension ≤ 1.0.

Hurricane Tie Installations to Achieve Twice the Load (Top View)




Install diagonally across from each other for minimum 2x truss.


Nailing into both sides of a single ply 2x truss may cause the wood to split.




H1




H1 Installation




H2A




H2A Installation




H2.5A




H2.5A Installation




H2.5T




H2.5T Installation
(Nails into both top plates)




H3



H3 Installation



H10A



H10A Installation

Model No.	Ga.	Fasteners			Factored Resistance (lb.)					
					D.Fir-L			S-P-F		
		To Rafter	To Plates	To Studs	Uplift	Normal		Uplift	Normal	
						F ₁	F ₂		F ₁	F ₂
						(K ₀ =1.15)			(K ₀ =1.15)	
H1	18	(6) 8d x 1½"	(4) 8d	—	740	685	300	680	485	215
H2A	18	(5) 8d x 1½"	(2) 8d x 1½"	(5) 8d x 1½"	830	220	75	590	155	55
H2.5A	18	(5) 8d	(5) 8d	—	805	160	160	755	160	160
H2.5T	18	(5) 8d	(5) 8d	—	835	175	240	740	160	210
H3	18	(4) 8d	(4) 8d	—	740	180	265	615	125	190
H10A	18	(9) 10d x 1½"	(9) 10d x 1½"	—	1735	795	410	1505	565	290

1. Factored resistances have been increased 15% for earthquake or wind loading with no further increase allowed.
2. Factored resistances are for one anchor. A minimum rafter thickness of 2½" must be used when framing anchors are installed on each side of the joist and on the same side of the plate.

3. When cross-grain bending or cross-grain tension cannot be avoided, mechanical reinforcement to resist such forces should be considered.
4. Hurricane ties are shown installed on the outside of the wall for clarity. Installation on the inside of the wall is acceptable. For a Continuous Load Path, connections must be on same side of the wall.



This technical bulletin is effective until December 31, 2024, and reflects information available as of July 1, 2022. This information is updated periodically and should not be relied upon after December 31, 2024. Contact Simpson Strong-Tie for current information and limited warranty or see strongtie.com.

© 2022 Simpson Strong-Tie Company Inc. • P.O. Box 10789, Pleasanton, CA 94588

T-SPECH22 7/22 exp. 12/24

(800) 999-5099
strongtie.com

HGUS — Double-Shear Joist Hangers

SIMPSON
Strong-Tie

All HGUS hangers have double-shear nailing. This patented innovation distributes the load through two points on each joist nail for greater strength. It also allows the use of fewer nails, faster installation and the use of common nails for all connections. Do not bend or remove tabs.

Material: 12 gauge

Finish: G90 galvanized

Design:




- Factored resistances are in accordance with CSA O86-14 and CSA O86:19.
- Uplift resistances have been increased 15%. No further increase is permitted.
- Wood shear is not considered in the factored resistances given. The specifier must ensure that the joist and header capacities are capable of withstanding these loads.

Installation:

- Use all specified fasteners
- Nails: 16d = 0.162" dia x 3½" long common wire
- Double-shear nails must be driven at an angle through the joist or truss into the header to achieve the table loads
- Not designed for welded or nailer applications

Options:




- See current catalogue for options

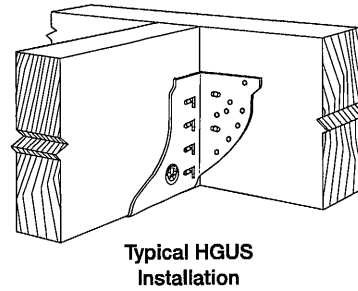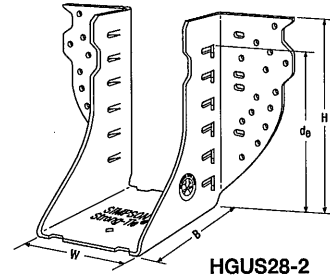

Typical HGUS Installation
(Truss designer to provide fastener quantity for connecting multiple members together)

Model No.	Ga.	Dimensions (in.)				Fasteners		Factored Resistance (lb.)			
		W	H	B	d ₀ ¹	Face	Joist	D.Fir-L		S-P-F	
								Uplift (K ₀ =1.15)	Normal (K ₀ =1.00)	Uplift (K ₀ =1.15)	Normal (K ₀ =1.00)
HGUS26	12	1½	5¾	5	4⅝ ₃₂	(20) 16d	(8) 16d	2685	6625	2685	5700
HGUS26-2	12	3⅝	5⅞	4	4⅞	(20) 16d	(8) 16d	4385	8950	3100	6355
HGUS26-3	12	4⅝	5½	4	4⅞	(20) 16d	(8) 16d	4385	8950	3100	6355
HGUS26-4	12	6⅞	5⅞	4	4⅞	(20) 16d	(8) 16d	4385	8950	3100	6355
HGUS28	12	1½	7⅞	5	6⅞	(36) 16d	(12) 16d	3310	7675	3100	6900
HGUS28-2	12	3⅝	7⅞	4	6⅞	(36) 16d	(12) 16d	6070	12980	4310	9215
HGUS28-3	12	4⅝	7¼	4	6⅞	(36) 16d	(12) 16d	6070	12980	4310	9215
HGUS28-4	12	6⅞	7⅞	4	6⅞	(36) 16d	(12) 16d	6070	12980	4310	9215
HGUS210-2	12	3⅝	9⅞	4	8⅞	(46) 16d	(16) 16d	6840	14015	4855	10270
HGUS210-3	12	4⅝	9¼	4	8⅞	(46) 16d	(16) 16d	6840	14645	4855	10400
HGUS210-4	12	6⅞	9⅞	4	8⅞	(46) 16d	(16) 16d	6840	14645	4855	10400
HGUS212-4	12	6⅞	10⅞	4	10⅞	(56) 16d	(20) 16d	7640	14995	5425	10645
HGUS214-4	12	6⅞	12⅞	4	11⅞	(66) 16d	(22) 16d	10130	16400	7195	11645

1. d₀ is the distance from the seat of the hanger to the highest joist nail.



This technical bulletin is effective until December 31, 2024, and reflects information available as of July 1, 2022. This information is updated periodically and should not be relied upon after December 31, 2024. Contact Simpson Strong-Tie for current information and limited warranty or see strongtie.com.

© 2022 Simpson Strong-Tie Company Inc. • P.O. Box 10789, Pleasanton, CA 94588

T-SPECHGUS22 7/22 exp. 12/24

(800) 999-5099
strongtie.com

LGT/MGT/VGT

Girder Tiedowns

The LGT, MGT and VGT are girder tiedowns for moderate- to high-load applications. The LGT and VGT are also suitable for retrofit applications.

LGT connectors provide a low-profile connection to the studs for easy installation of drywall. Simple to install and can be installed on the inside or outside of the wall.

The variable girder tiedown (VGT) is a higher capacity alternative to the LGT and MGT for girder trusses. It attaches with Strong-Drive® SDS Heavy-Duty Connector screws to the side of truss and features a predeflected crescent washer that allows it to accommodate top chord pitches up to 8:12. The VGT is also available with one flange concealed for attachment to trusses with no overhang.

Material: VGT — 7 gauge, LGT2 — 14 gauge, MGT, LGT3, LGT4 — 12 gauge




Finish: Galvanized

Installation:

- Before installing fasteners, ensure LGT3-SDS2.5 makes complete contact with bottom of truss.
- Strong-Drive SDS Heavy-Duty Connector screws included with LGT3, LGT4 and VGT series.
- Strong-Drive SDS Heavy-Duty Connector screws driven through truss plates must be approved by the Truss Designer. Predrilling using a $\frac{1}{8}$ " bit is required.
- VGT — Can be installed on roof pitches up to 8/12 or on a bottom chord designed to transfer the load.
- VGT — Screw holes are configured to allow for double installation on a two-ply (minimum) truss.
- VGT — The product can be installed in a single application or in pairs to achieve a higher uplift capacity.
- VGT — When installed on trusses with no overhangs, specify VGTR/L.
- VGT — Install washer component (provided) so that top of washer is horizontal as well as parallel with top of wall top plate.
- LGT3-SDS2.5 and LGT4-SDS3 — The four large hexagon holes are intended for GFCMU and concrete applications.
- MGT — Install a minimum of (6) 10d nails into the face of roof member that is on same side as MGT base.
- See p. 342 for masonry applications.

Options:

- LGT3 and LGT4 are available with reduced widths of $W = 4\frac{1}{16}$ " and $W = 6\frac{3}{16}$ " — order as LGT3N-SDS2.5 and LGT4N-SDS3.

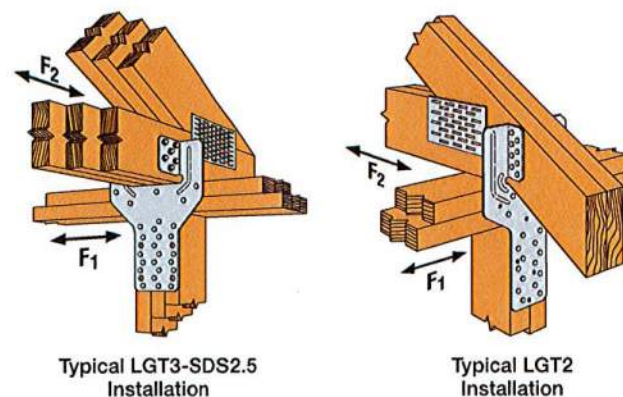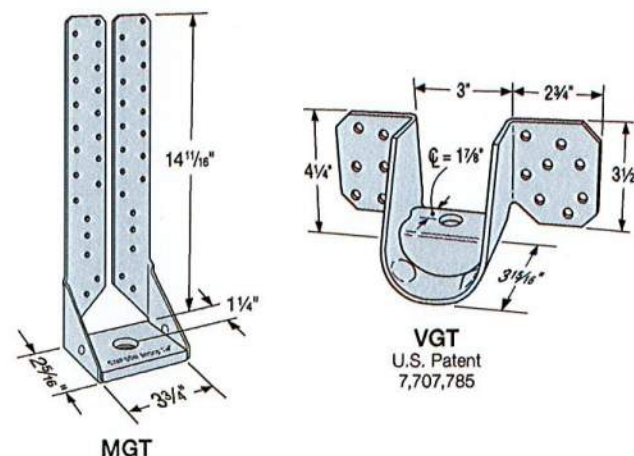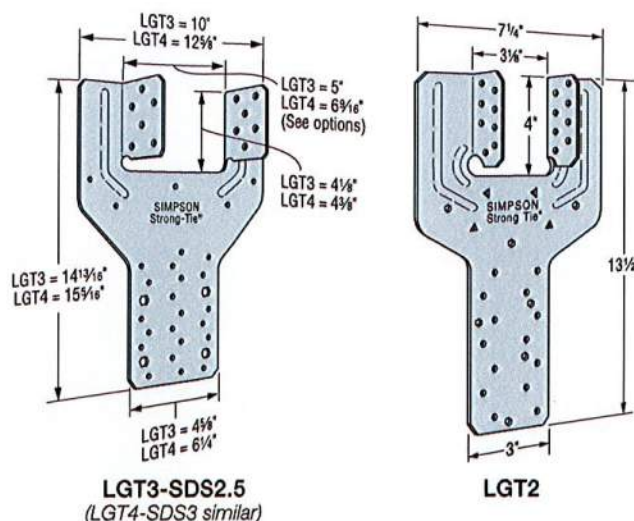


LGT/MGT/VGT

Girder Tiedowns (cont.)


These products are available with additional corrosion protection. For more information, see p. 24.

Model No.	Qty.	No. of Plies	Fasteners		Factored Resistance ($K_D = 1.15$)					
			Studs or Anchor	Girder Truss	D.Fir-L			S-P-F		
					Uplift	Lateral		Uplift	Lateral	
						F ₁	F ₂		F ₁	F ₂
					lb.	lb.	lb.	lb.	lb.	lb.
					kN	kN	kN	kN	kN	kN
LGT2	1	2 ply	(14) 10d ⁴	(16) 10d	3670	1170	285	2605	830	200
					16.33	5.20	1.27	11.59	3.69	0.89
LGT3-SDS2.5	1	3 ply	(26) 10d	(12) ¼" x 2½" SDS	6415	1335	670	4930	945	475
					28.54	5.94	2.98	21.93	4.20	2.11
LGT4-SDS3	1	4 ply	(30) 10d ⁵	(16) ¼" x 3" SDS	6030	2785	1125	3980	1980	800
					26.82	12.39	5.00	17.70	8.81	3.56
MGT	1	2 ply min.	(1) ⅝" diameter	(22) 10d	5610	—	—	3985	—	—
					24.96	—	—	17.73	—	—
VGT	1	2 ply min.	(1) ⅝" diameter	(16) ¼" x 3" SDS	8600	—	—	6195	—	—
					38.26	—	—	27.56	—	—
	2	2 ply min.	(2) ⅝" diameter	(32) ¼" x 3" SDS	11690	—	—	8420	—	—
					52.00	—	—	37.46	—	—
VGTR/L	1	2 ply min.	(1) ⅝" diameter	(16) ¼" x 3" SDS	3475	—	—	2505	—	—
					15.46	—	—	11.14	—	—
	2	2 ply min.	(2) ⅝" diameter	(32) ¼" x 3" SDS	6950	—	—	5010	—	—
					30.92	—	—	22.29	—	—


- Attached members must be designed to resist the factored resistances.
- Factored resistances have been increased 15% for uplift with no further increase allowed; reduce where other loads govern.
- Additional anchorage products to be designed by others.
- LGT2 — F₂ factored resistance requires installation of (4) 10d nails in optional nail holes.
- LGT4 — F₂ factored resistance requires installation of (7) 10d nails in optional nail holes.
- MGT can be installed with straps vertical for full table value provided 26-10d nails are installed to either a solid header or minimum double 2x6 web.
- Nails: 10d = 0.148" dia. x 3" long. See pp. 27–28 for other nail sizes and information.

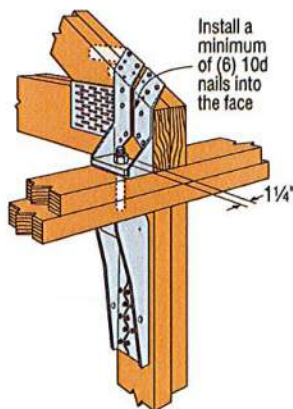


Typical MGT
Installation with HDU4

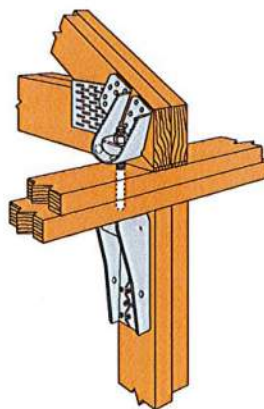

Typical VGTR Single
Installation with HDU2



Typical VGT Double
Installation with HDU4's

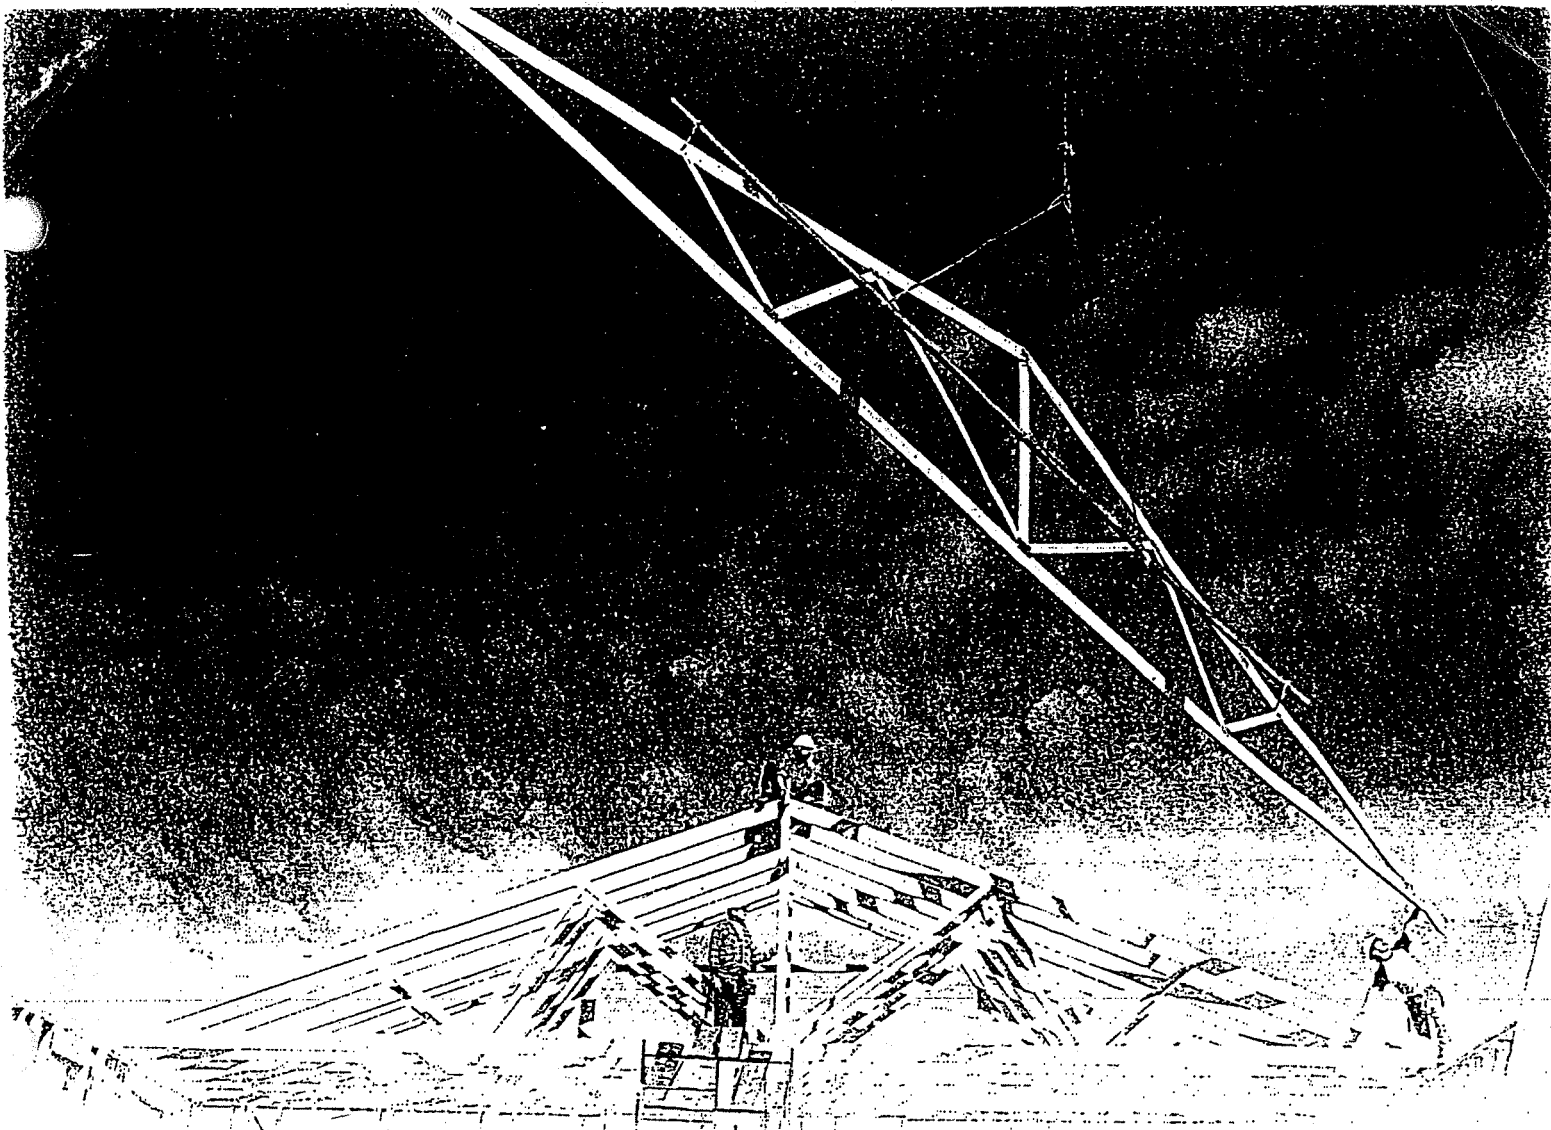


Wood Truss Installation

**A Guide to proper handling, erecting and bracing
metal plate connected wood trusses**

Table of Content

Warning.....	4
1 Unloading & Lifting.....	5
2 Job Site Handling.....	5
3 Hoisting.....	6
4 Beginning the Erection Process.....	7
5 Erection Tolerance.....	8
6 Bracing.....	8
7 Bracing Requirements for 3 Planes of Roof.....	9
8 Stacking Materials.....	10
Caution Notes.....	11

Warning



General

Familiarity with the Construction Design Documents, the Truss Design Drawings, and Truss Placement Plans (if required by the Construction Design Documents) is required to properly erect, brace, and connect the trusses to the building system.

All of the care and quality involved in the design and manufacture of wood trusses can be jeopardized if the trusses are not properly handled, erected, and braced.

The consequences of improper handling, erecting, and bracing may be a collapse of the structure, which at best is a substantial loss of time and materials, and at worst is a loss of life. The majority of truss accidents occur during truss installation and not as a result of improper design or manufacture.

Prior to truss erection, the builder/erector shall meet with the erection crew for a safety and planning meeting, making sure each crew member understands his or her roles and responsibilities during the erection process.

Temporary Erection Bracing

Trusses are not marked in any way to identify the frequency, or location of temporary erection bracing.

All temporary bracing shall comply with the latest edition of *Commentary and Recommendations for Handling, Installing & Bracing Metal Plate Connected Wood Trusses* (HIB), published by the Truss Plate Institute, and/or as specified in the Construction Design Documents prepared by the building designer.

Permanent Truss Bracing

Permanent bracing for the roof or floor trusses is the responsibility of the building designer and should be shown on the Construction Design Documents. Permanent bracing locations for individual compression members of a wood truss are shown on the Truss Design Drawings, and shall be installed by the building or erection contractor. This bracing is needed for the proper performance of individual trusses within the roof or floor system. The design and connection of the bracing to the truss and then to the overall building system is the responsibility of the building designer, and is in addition to the permanent bracing plan, which is also specified by the building designer.

Special Design Requirements

Special design requirements, such as wind bracing, portal bracing, seismic bracing, diaphragms, shear walls, or other load transfer elements and their connections to wood trusses must be considered separately by the building designer, who shall determine size, location, and method of connections for all bracing as needed to resist these forces.

1 Unloading & Lifting

Never handle trusses flat



Beginning with the unloading process, and throughout all phases of construction, care must be taken to avoid lateral bending of trusses, which can cause damage to the lumber and metal connector plates at the joints.



Avoid lateral bending


- Use special care in windy weather.
- If using a crane within 10 feet of an electric line, contact the local power company.
- If using a crane within 5 miles of an airport, contact the airport 30 days prior to erection to learn about any safety regulations that must be followed.

2 Job Site Handling

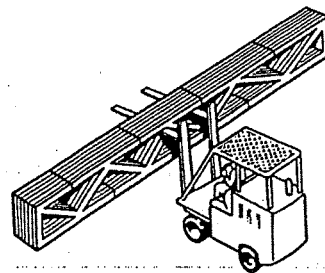


All trusses should be picked up at the top chords in a vertical position only

Proper banding and smooth ground allow for unloading of trusses without damage. This should be done as close to the building site as possible to minimize handling. Do not break banding until installation begins. Hand erection of trusses is allowed, provided excessive lateral bending is prevented.




Do not store unbraced bundles upright

If trusses are stored vertically they shall be braced in a manner that will prevent tipping or topping. Generally cutting of the banding is done just prior to installation.



Do not store on uneven ground

If trusses are stored horizontally, blocking should be used on eight to ten foot centers, or as required, to minimize lateral bending and moisture gain.




Care should be exercised when removing banding to avoid damaging trusses.


During long term storage, trusses shall be protected from the environment in a manner that provides for adequate ventilation of the trusses. If tarpaulins or other material is used, the ends shall be left open for ventilation. Plastic is not recommended, since it can trap moisture.

3 Hoisting


All trusses that are erected one at a time shall be held safely in position by the erection equipment until such time as all necessary bracing has been installed and the ends of the trusses are securely fastened to the building.

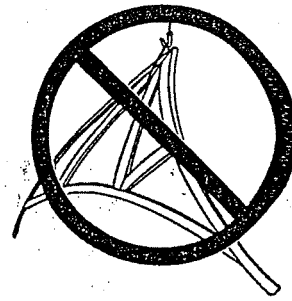


Avoid lateral bending

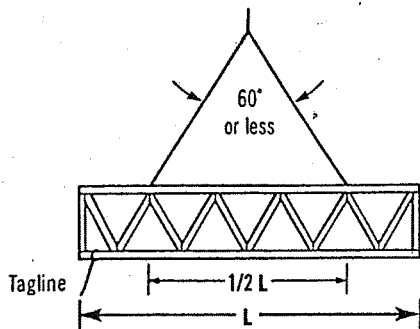


$L \leq 30'$

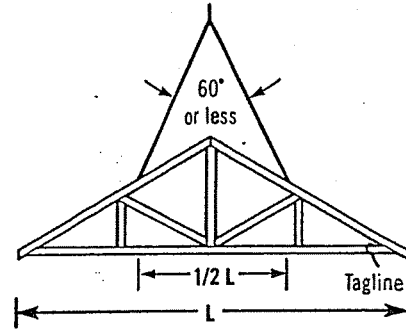


Truss sling is acceptable where these criteria are met.

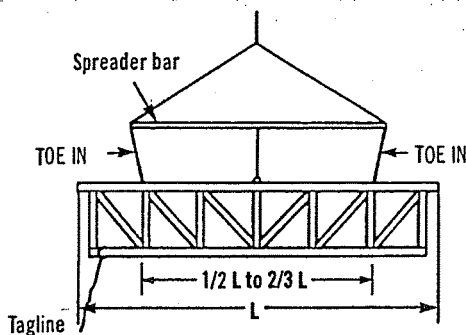


$30' < L \leq 60'$

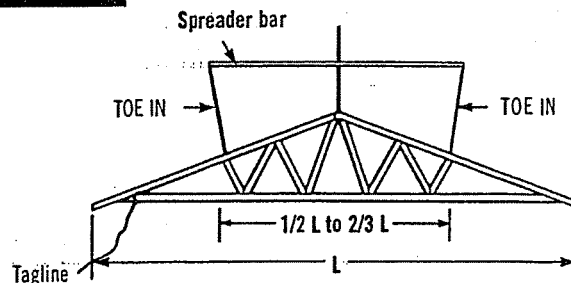

Use spreader bar in all other cases. It should be noted that the lines from the ends of the spreader bar "TOE IN"; if these lines should "TOE OUT" the truss may fold in half.

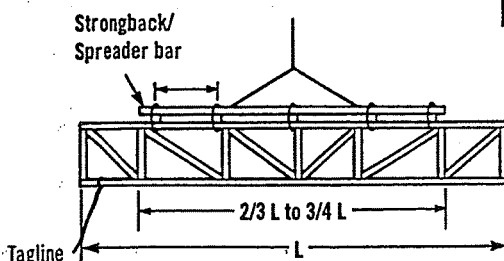

$L > 60'$

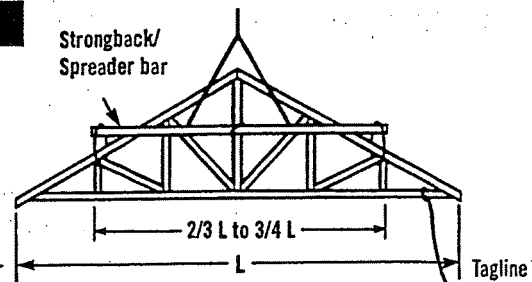


For lifting trusses with spans in excess of 60 feet, it is recommended that a strongback/spreader bar be used as illustrated. The strongback/spreader bar should be attached to the top chord and web members at intervals of approximately 10 feet. Further, the strongback/spreader bar should be at or above the mid-height of the truss to prevent overturning. The strongback/spreader bar can be of any material with sufficient strength to safely carry the weight of the truss and sufficient rigidity to adequately resist bending of the truss.

4 Beginning the Erection Process

It is important for the builder or erection contractor to provide substantial bracing for the first truss erected. The two or more trusses making up the rest of the first set are tied to and rely upon the first truss for stability. Likewise, after this first set of trusses is adequately cross-braced, the remaining trusses installed rely upon this first set for stability. Thus, the performance of the truss bracing system depends to a great extent on how well the first group of trusses is braced.

Ground Brace - Exterior




One satisfactory method ties the first unit of trusses off to a series of braces that are attached to a stake driven into the ground and securely anchored. The ground brace itself should be supported as shown below or it is apt to buckle. Additional ground braces in the opposite direction, inside the building, are also recommended.

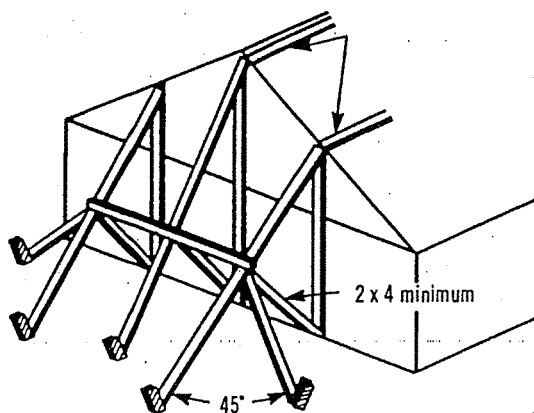

Note: Locate ground braces for first truss directly in line with all rows of top chord continuous lateral bracing (either temporary or permanent).

Ground Brace - Interior

Another satisfactory method where height of building or ground conditions prohibit bracing from the exterior is to tie the first truss rigidly in place from the interior at the floor level, provided the floor is substantially completed and capable of supporting the ground bracing forces. Securely fasten the first truss to the middle of the building. Brace the bracing similar to exterior ground bracing shown at left. Set trusses from the middle toward the end of the building. Properly cross-brace the first set of trusses before removing floor braces and setting remaining trusses.

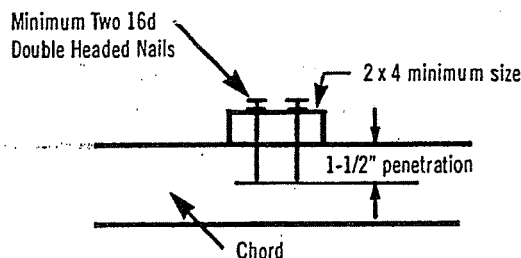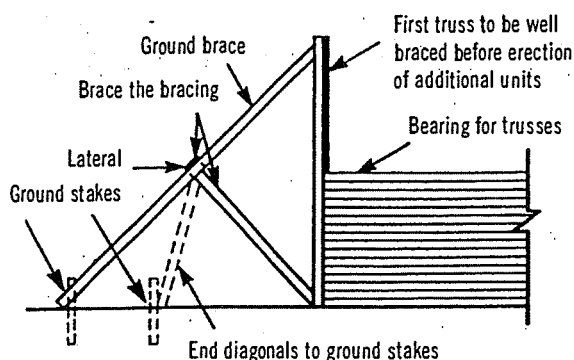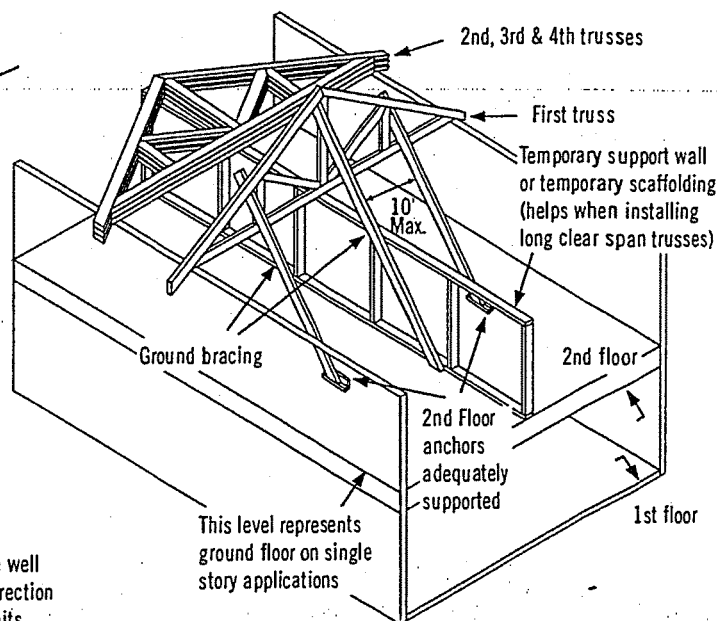


Inadequate size of bracing material or inadequate fastening is a major cause of erection dominoing.


5 Erection Tolerance

Complying with erection tolerances is critical to achieving an acceptable roof or floor line, and to accomplishing effective bracing. Setting trusses within tolerance the first time will prevent the need for the hazardous practice of respacing or adjusting trusses when roof sheathing or roof purlins are installed. Trusses leaning or bowing can cause nails to miss the top chords when sheathing is applied, and create cumulative stresses on the bracing, which is a frequent cause of dominoing.


When sheathing, make sure nails are driven into the top chord of the trusses.

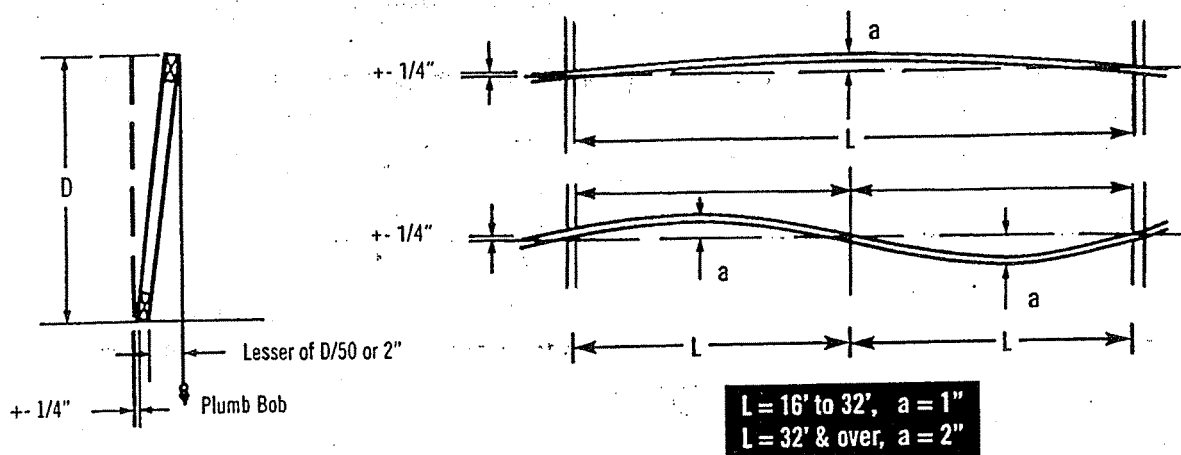

6 Bracing

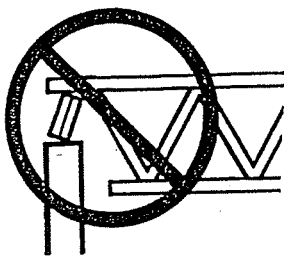


Do not install trusses on temporarily connected supports



Do not walk on unbraced trusses



Do not walk on trusses or gable ends lying flat

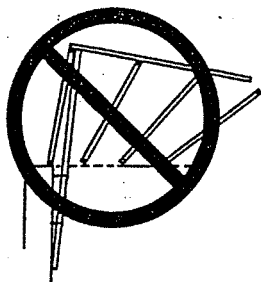


Nails in withdrawal (parallel to force)

All anchors, hangers, tie-downs, seats, bearing ledgers, etc., that are part of the supporting structure shall be accurately and properly placed and permanently attached before truss installation begins. No trusses shall ever be installed on anchors or ties that have temporary connections to the supporting structure.

Nailing scabs to the end of the building to brace the first truss is not recommended.

All nailing of bracing should be done so that nails are driven perpendicular to the direction of force, as shown at right.

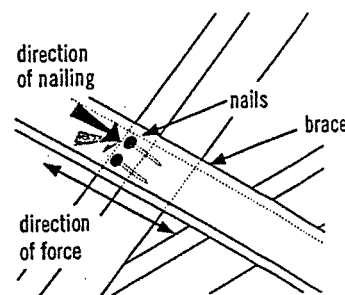


Well nailed (perpendicular to force)

7 Bracing Requirements for 3 Planes of Roof

Temporary erection bracing must be applied to three planes of the roof system to ensure stability: Plane 1) Top Chord (sheathing), Plane 2) Bottom Chord (ceiling plane), and Plane 3) Web Member plane or vertical plane perpendicular to trusses.

1) Top Chord Plane

Most important to the builder or erection contractor is bracing in the plane of the top chord. Truss top chords are susceptible to lateral buckling before they are braced or sheathed.

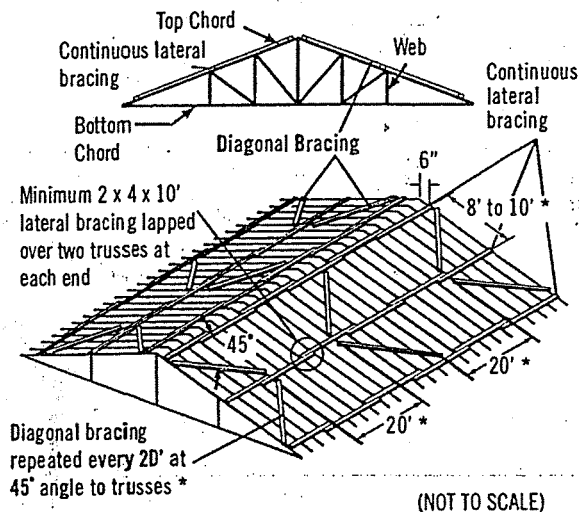


Exact spacing between trusses should be maintained as bracing is installed to avoid the hazardous practice of removing bracing to adjust spacing. This act of "adjusting spacing" can cause trusses to topple if connections are removed at the wrong time.

3) Web Member Plane

"X" bracing, as shown, is critical in preventing trusses from leaning or dominoing. Repeat as shown to create a succession of rigid units.


X-bracing should be installed on vertical web members wherever possible, at or near lateral bracing. Plywood or OSB may be substituted for X-bracing.

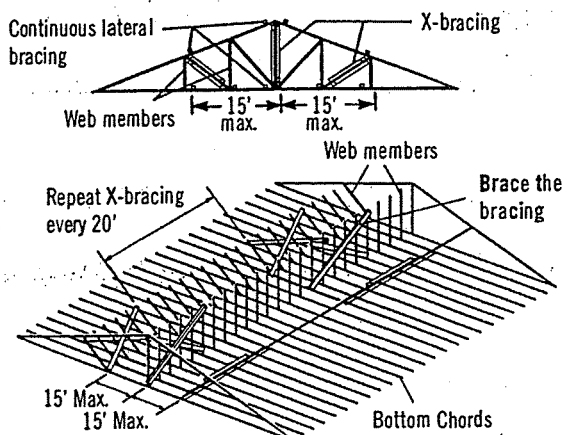

Note: Top chords and some web members are not shown, in order to make drawings more readable.


2) Bottom Chord Plane

In order to hold proper spacing on the bottom chord, temporary bracing is recommended on the top of the bottom chord.

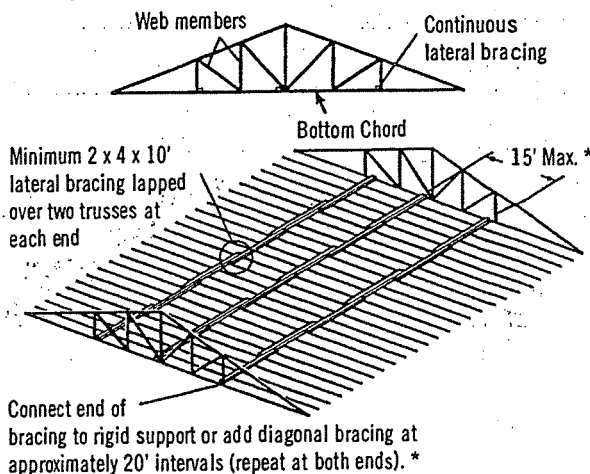


* Long spans, heavy loads or other spacing configurations may require closer spacing between lateral bracing and closer intervals between diagonals. Consult the building designer or HIB and DSB (Recommended Design Specification for Temporary Bracing of Metal-Plate Connected Wood Trusses) for details.

Diagonal or cross-bracing is very important!



Do not use short blocks to brace individual trusses without a specific bracing plan detailing their use





Bracing requirements using the same principles apply to parallel chord trusses

8 Stacking Materials

Do not proceed with building completion until all bracing is securely and properly in place



Never stack materials on unbraced or inadequately braced trusses




Platform must be rigidly braced

Proper distribution of construction materials is a must during construction.



Never stack materials near a peak

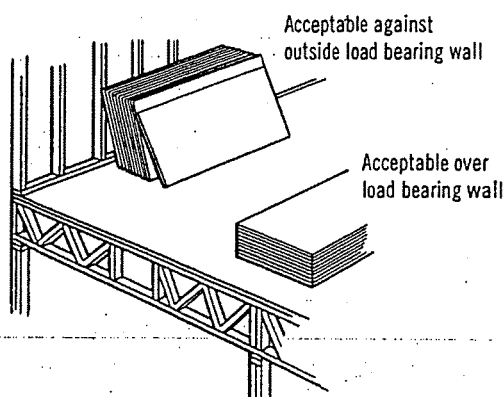

Never stack materials on the cantilever of a truss




Always stack materials over two or more trusses.





Single truss

Never overload small groups or single trusses. Position load over as many trusses as possible.



Roofing and mechanical contractors are cautioned to stack materials only along outside supporting members or directly over inside supporting members. Trusses are not designed for dynamic loads (i.e., moving vehicles). Extreme care should be taken when loading and stacking construction materials (rolled roofing, mechanical equipment, etc.) on the roof or floor system.

Never cut any structural member of a truss.



Sleepers for mechanical equipment should be located at panel points (joints) or over main supporting members, and only on trusses that have been designed for such loads.

Caution Notes

Errors in building lines and/or dimensions, or errors by others shall be corrected by the contractor or responsible construction trade subcontractor or supplier **before** erection of trusses begins.


Cutting of nonstructural overhangs is considered a part of normal erection and shall be done by the builder or erection contractor.

Any field modification that involves the cutting, drilling, or relocation of any structural truss member or connector plate shall not be done without the approval of the truss manufacturer or a licensed design professional.

The methods and procedures outlined are intended to ensure that the overall construction techniques employed will put floor and roof trusses safely in place in a completed structure. These recommendations for bracing wood trusses originate from the collective experience of leading technical personnel in the wood truss industry, but must, due to the nature of responsibilities involved, be presented only as a guide for use by a qualified building designer, builder, or erection contractor. Thus, the Wood Truss Council of America expressly disclaims any responsibility for damages arising from the use, application, or reliance on the recommendations and information contained herein.

[Selected text and figures referenced or reproduced from HIB and DSB by permission of the Truss Plate Institute, Madison, WI.]

THE CANADIAN WOOD TRUSS ASSOCIATION



L'ASSOCIATION CANADIENNE DES FABRICANTS DE FERMES DE BOIS

1400 Blair Place, Suite 210, Ottawa, ON K1J 9B8
Tel.: 613-747-5544 Fax: 613-747-6264



**Wood Truss Council
of America**

One WTCA Center
6300 Enterprise Lane, Madison, WI 53719-1140
Tel.: 608-274-4849 Fax: 608-274-3329
wtca@woodtruss.com www.woodtruss.com
