

CONSTRUCTION SUMMARY

North Oakville - 115 - 1 - WILLOW VALLEY (43-02) ELEV B

Register Plan Number: Municipal Address: Closing: 16-Jan-20

CABINETRY

Inv. 36 28 Line 573 2Nov19 / 6Nov19	1 - KITCHEN: INSTALL LEVEL 7 KITCHEN CABINETS Note:
Inv. 36 29 Line 576 2Nov19 / 6Nov19	1 - KITCHEN: INSTALL STACKED CABINETS (03A). SEE SKETCH FOR CABINETS DIMENTIONS Note:
Inv. 36 31 Line 578 2Nov19 / 6Nov19	1 - KITCHEN: INSTALL VALANCE UNDER UPEER CABINETS Note:
Inv. 36 32 Line 579 2Nov19 / 6Nov19	1 - KITCHEN: INSTALL WALL OVEN CABINET (18H) Note:
Inv. 36 33 Line 580 2Nov19 / 6Nov19	1 - KITCHEN: INSTALL RANGETOP CABINET WITH POT DRAWERS (25H) Note:
Inv. 36 35 Line 582 2Nov19 / 6Nov19	1 - KITCHEN: INSTALL DEEP FRIDGE CABINET (03H) Note:
Inv. 36 30 Line 605 2Nov19 / 6Nov19	1 - KITCHEN: INSTALL CROWN MOULDING ON KITCHEN STACKED CABINETS Note:
Inv. 36 55 Line 607 2Nov19 / 6Nov19	1 - KITCHEN: INSTALL DECOR HOOD CABINET (10H). INCLUDES 600CFM HOOD FAN Note:

CABINETRY ACCESSORIES

Inv. 2 15 Line 328 17Jun19 / 11Oct19	1 - KITCHEN: INSTALL VALANCE LIGHTING - UNDER CABINET - DOES NOT INCLUDE LIGHTING Note:
---	--

CARPET

Inv. 36 52 Line 602 2Nov19 / 6Nov19	1 - BEDROOMS: INSTALL 2ND UPGRADE UNDERPAD THROUGHOUT 2ND FLOOR BEDROOMS **DOES NOT INCLUDE UPPER HALL Note:
--	--

CEILING

Inv. 2 23 Line 349 17Jun19 / 11Oct19	1 - DINING ROOM: INSTALL COFFERED - TRAY CEILING - DINING ROOM Note:
---	---

North Oakville - 115 - 1 - WILLOW VALLEY (43-02) ELEV B

Registere Plan Number: Municipal Address: Closing: 16-Jan-20

Inv.2	1 - LIVING ROOM: INSTALL COFFERED - TRAY CEILING - LIVING ROOM	
24	Note:	
Line 350		
17Jun19 / 11Oct19		
Inv.2	1 - KITCHEN/BREAKFAST AREA: INSTALL COFFERED - TRAY CEILING - BREAKFAST AREA	
20	Note:	
Line 340		
17Jun19 / 11Oct19		
Inv.2	1 - GREAT ROOM: INSTALL COFFERED - TRAY CEILING - GREAT ROOM	
21	Note:	
Line 342		
17Jun19 / 11Oct19		
Inv.2	1 - FOYER: INSTALL COFFERED - TRAY CEILING - HALLWAY	
22	Note:	
Line 344		
17Jun19 / 11Oct19		

CERAMIC TILE

Inv.36	1 - ENTRY/ POWDER ROOM: INSTALL UPGRADE 6 FLOOR TILE THROUGHOUT ENTRY/	
37	POWDER ROOM	
Line 585	Note:	
2Nov19 / 6Nov19		
Inv.36	1 - MASTER ENSUITE: INSTALL 6TH UPGRADE FLOOR TILE IN MASTER ENSUITE	
38	Note:	
Line 586		
2Nov19 / 6Nov19		
Inv.36	1 - MASTER ENSUITE SHOWER: INSTALL 6TH UPGRADE WALL TILE IN MASTER ENSUITE	
39	SHOWER	
Line 587	Note:	
2Nov19 / 6Nov19		
Inv.36	1 - MASTER ENSUITE SHOWER FLOOR: INSTALL 6TH UPGRADE WALL TILE IN MASTER	
40	ENSUITE SHOWER FLOOR	
	MATTE FINISH	
Line 588	Note:	
2Nov19 / 6Nov19		

COUNTERTOP

Inv.36	1 - KITCHEN: INSTALL MSI LEVEL 3 QUARTZ THROUGHOUT KITCHEN AND SERVERY	
36		
Line 583	Note:	
2Nov19 / 6Nov19		
Inv.36	1 - KITCHEN: INSTALL GRANITE CUTOUT FOR 36" RANGETOP CABINET	
34		
Line 581	Note:	
2Nov19 / 6Nov19		
Inv.36	2 - MASTER ENSUITE: SUPPLY TWO (2) CUTOUTS FOR UNDERMOUNT SINKS IN MASTER	
42	ENSUITE	
Line 590	Note:	
2Nov19 / 6Nov19		

ELECTRICAL

CONSTRUCTION SUMMARY

North Oakville - 115 - 1 - WILLOW VALLEY (43-02) ELEVE B

Registere Plan Number: Municipal Address: Closing: 16-Jan-20

Inv.2 19	1 - KITCHEN: INSTALL ELECTRICAL - ROUGH-IN FOR 30 - 40 AMP BUILT-IN WALL OVEN
Line 339	Note:
17Jun19 / 11Oct19	
Inv.2 16	1 - KITCHEN: INSTALL CABINET LIGHTING - UNDERMOUNT T-5 LED VALANCE LIGHT (\$200 PER LIGHT)- FOR VALANCE
Line 329	Note:
17Jun19 / 11Oct19	
Inv.2 1	1 - TELEPHONE AND CABLE LOCATION SKETCH. LOCATION MAY VARY SLIGHTLY DUE TO JOIST LOCATION
Line 331	Note:
17Jun19 / 11Oct19	
Inv.2 13	1 - KITCHEN: INSTALL RECEPTACLES - ADDITIONAL 15 AMP 120 VOLT RECEPTABLE- FOR GAS STOVE
Line 326	Note:
17Jun19 / 11Oct19	
Inv.2 14	1 - LIVING ROOM: INSTALL CEILING LIGHT ROUGH IN - FOR 1 CEILING LIGHT, WITH SEPERATE SWITCH
Line 327	Note:
17Jun19 / 11Oct19	
Inv.2 7	1 - GREAT ROOM: INSTALL RECEPTACLES - DEDICATED 15 AMP 120 VOLT RECEPTABLE- ABOVE FIREPLACE FOR FUTURE TV. SEE SKETCH. LOCATION MAY VARY SLIGHTLY DUE TO JOIST LOCATION
Line 320	Note:
17Jun19 / 11Oct19	

HARDWOOD FLOORING

Inv.36 46	1 - KITCHEN: INSTALL LEVEL 3 HARDWOOD THROUGHOUT
Line 606	Note:
2Nov19 / 6Nov19	
Inv.36 45	1 - LIVING/ DINING ROOM: INSTALL LEVEL 3 HARDWOOD THROUGHOUT
Line 596	Note:
2Nov19 / 6Nov19	
Inv.36 47	1 - MAIN HALL: INSTALL LEVEL 3 HARDWOOD THROUGHOUT
Line 597	Note:
2Nov19 / 6Nov19	
Inv.36 48	1 - GREAT ROOM: INSTALL LEVEL 3 HARDWOOD THROUGHOUT
Line 598	Note:
2Nov19 / 6Nov19	
Inv.36 49	1 - LIBRARY: INSTALL LEVEL 3 HARDWOOD THROUGHOUT
Line 599	Note:
2Nov19 / 6Nov19	
Inv.36 50	1 - UPPER HALL: INSTALL LEVEL 3 HARDWOOD THROUGHOUT, IN LIEU OF STANDARD CARPET
Line 600	Note:
2Nov19 / 6Nov19	

North Oakville - 115 - 1 - WILLOW VALLEY (43-02) ELEV B

Register Plan Number: Municipal Address: Closing: 16-Jan-20

Inv.36	1 - STAIRCASE: INSTALL SANDED OAK LANDINGS ON STAIRCASE
51	Note:
Line 601	
2Nov19 / 6Nov19	

HVAC

Inv.2	1 - KITCHEN: INSTALL GAS PIPING AND OTHER - GAS LINE R/I FOR BASEMENT OR MAIN FLOOR - STOVE - UP TO 3/4 INCH LINE
12	Note:
Line 325	
17Jun19 / 11Oct19	
Inv.2	1 - FILTRATION - HUMIDIFICATION - CONTROL - FLO - THRU HUMIDIFIER LARGE HE205 - 18 GAL
17	Note:
Line 330	
17Jun19 / 11Oct19	

INTERIOR DOORS & TRIM

Inv.36	1 - MASTER ENSUITE: INSTALL FRAMELESS SHOWER IN MASTER ENSUITE
43	Note:
Line 594	
2Nov19 / 6Nov19	
Inv.36	1 - INSTALL UPGRADED HARDWARE THROUGHOUT HOME: VEGA - BLACK
44	Note:
Line 595	
2Nov19 / 6Nov19	

MISCELLANEOUS

Inv.36	1 - Purchaser has attended a Colour appointment at the Decor Centre & has DECLINED any additional upgrades and accepts and acknowledges that there will be no further structural changes/additions/deletions to be made
57	Note:
Line 609	
2Nov19 / 6Nov19	
Inv.36	1 - Purchasers are aware & accepts that ANY changes made to upgrades after signing this Purchasers Extra Form are subject to a minimum administration fee
58	Note:
Line 610	
2Nov19 / 6Nov19	
Inv.36	1 - BONUS PACKAGE: WORTH OF UPGRADES FROM VALERYHOMES DECOR CENTRE IS BEING APPLIED TOWARD THE COLOUR APPOINTMENT
59	Note:
Line 611	
2Nov19 / 6Nov19	
Inv.2	1 - Purchaser has attended a Structural appointment at the Decor Centre & has DECLINED any additional upgrades and accepts and acknowledges that there will be no further structural changes/additions/deletions to be made upon signing on August 23, 2019
26	Note:
Line 347	
17Jun19 / 11Oct19	
Inv.2	1 - Purchasers are aware & accepts that ANY changes made to upgrades after signing this Purchasers Extra Form are subject to a minimum administration fee
27	Note:
Line 348	
17Jun19 / 11Oct19	

PAINT

CONSTRUCTION SUMMARY

North Oakville - 115 - 1 - WILLOW VALLEY (43-02) ELEV B

Registere Plan Number: Municipal Address: Closing: 16-Jan-20

Inv.36	1 - STAIRCASE: STAIN STAIRS TO MORCHELLO
54	
Line 604	Note: **NOTE: PURCHASER IS AWARE THAT THE STAIN ON THE FLOORS SELECTED CAN NEVER BE EXACTLY MATCHED ON A RED OAK STAIRCASE
2Nov19 / 6Nov19	

PLUMBING

Inv.36	1 - POT FILLER PURCHASED AT COLOURS TO BE GOLD
56	
Line 608	Note:
2Nov19 / 6Nov19	
Inv.2	1 - MASTER ENSUITE: INSTALL POSI-TEMP TUB/SHOWER FAUCET WITH 3 FUNCTION TRANSFER VALVE/TRIM AND SLIDE BAR WITH HAND SHOWER
25	
	MODEL: TL183EP/3372/128284/T4171/62320/3669EP/A725 CROME
Line 351	Note:
17Jun19 / 11Oct19	
Inv.36	2 - MASTER ENSUITE: INSTALL TWO (2) UNDERMOUNT SINKS:
41	
	KOHLER CAXTON- K-200000
Line 589	Note:
2Nov19 / 6Nov19	
Inv.2	1 - KITCHEN: INSTALL POT FILLER- BEHIND STOVE
18	
	MOEN: MODERN 2 HANDLE POT FILLER FAUCET WITH DUAL SHUT-OFFS MODEL# S665.
Line 338	Note:
17Jun19 / 11Oct19	
Inv.2	1 - MASTER ENSUITE: INSTALL ROUGH-IN FOR SHOWER HEAD - RAINSHOWER HEAD MUST BE PURCHASED AT THE TIME OF COLOURS
8	
Line 321	Note:
17Jun19 / 11Oct19	
Inv.2	1 - SERVERY: INSTALL BAR SINK IN SERVERY
9	
Line 322	Note:
17Jun19 / 11Oct19	
Inv.2	1 - GARAGE: INSTALL EXTRA HOT FAUCET IN GARAGE, BESIDE STANDARD FAUCET
10	
Line 323	Note:
17Jun19 / 11Oct19	
Inv.2	1 - BACKYARD: INSTALL EXTRA HOT FAUCET IN GARAGE, BESIDE STANDARD FAUCET
11	
Line 324	Note:
17Jun19 / 11Oct19	

STAIRS

Inv.36	1 - STAIRCASE: INSTALL *DISPLAY 3A KNUCKLE SERIES, 1/2" METAL SINGLE
53	
Line 603	KNUCKLE/DBL KNUCKLE, TEXTURED BLACK, "B" RAIL, WITH BELLA POST
	Note:
2Nov19 / 6Nov19	

VACCUM/BELL

North Oakville - 115 - 1 - WILLOW VALLEY (43-02) ELEV B

Registere Plan Number: Municipal Address: Closing: 16-Jan-20

Inv.2	1 - WIRELESS ACCESS POINT PACKAGE - 2-CAT6 NETWORK CABLES AND 2-UBIQUITI AC LITE ACCESS POINTS	
3	Line 316	Note:
17Jun19 / 11Oct19		
Inv.2	1 - GARAGE: CENTRAL VACUUM - CENTRAL VAC PIPING COMPLETE TO GARAGE - ONE OUTLET IN BASEMENT	
4	Line 317	Note:
17Jun19 / 11Oct19		
Inv.2	1 - ATTIC: INSTALL CONDUIT - 1 1/4" ORANGE FLEX CONDUIT APPROX. 15FT FOR ATTIC	
5	Line 318	Note:
17Jun19 / 11Oct19		
Inv.2	1 - GREAT ROOM: INSTALL CONDUIT - 1 1/4" ORANGE FLEX CONDUIT APPROX. 35FT FOR FIREPLACE- FOR FUTURE TV. SEE SKETCH FOR LOCATION. LOCATION MAY VARY SLIGHTLY DUE TO JOIST LOCATION	
6	Line 319	Note:
17Jun19 / 11Oct19		

WINDOWS

Inv.2	4 - BASEMENT: INSTALL FOUR (4) BASEMENT WINDOW - ENLARGE STANDARD WINDOW - 36 X 30	
2	Line 315	Note:
17Jun19 / 11Oct19		


Customer: All elevations are approximate and subject to normal construction variances. Dimensions may exceed the usable floor area. Sizes and specifications subject to change without notice. Furniture is intended for dimension purposes only and does not necessarily reflect the actual plan for the site. Sales are sold as-is. All rights reserved. Pricing and trade conditions may apply. Contact a sales representative for further details. E.A.O.L. Privacy Policy 2018. All rights reserved.

Willow Valley


Elevation A
3,623 Sq.ft.

Elevation B
3,628 Sq.ft.

Includes 47 Sq.ft. of Finished Basement




GROUND FLOOR B

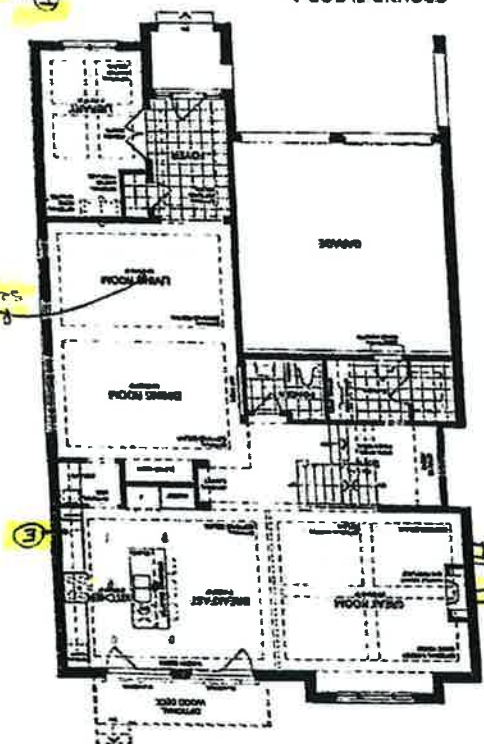


GROUND FLOOR A


47 sq. ft. of finished basement




SECOND FLOOR B

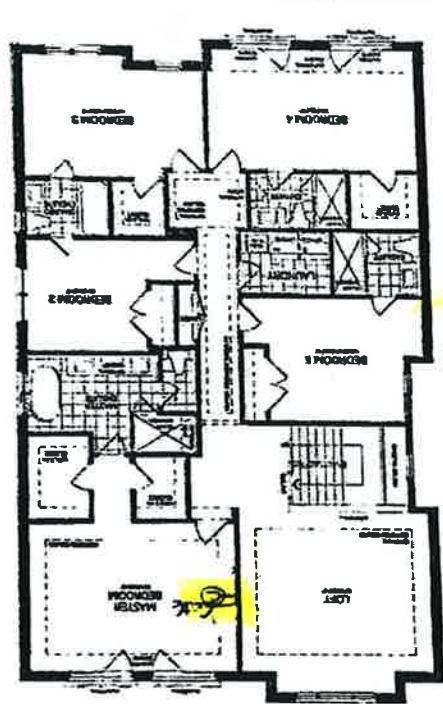

SECOND FLOOR A



BASEMENT B

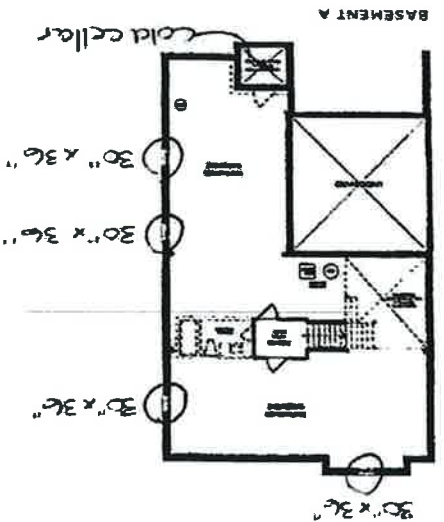


BASEMENT A

Lot 115
Aug 23, 19

36" (91.4 cm) models

Lot 115


083

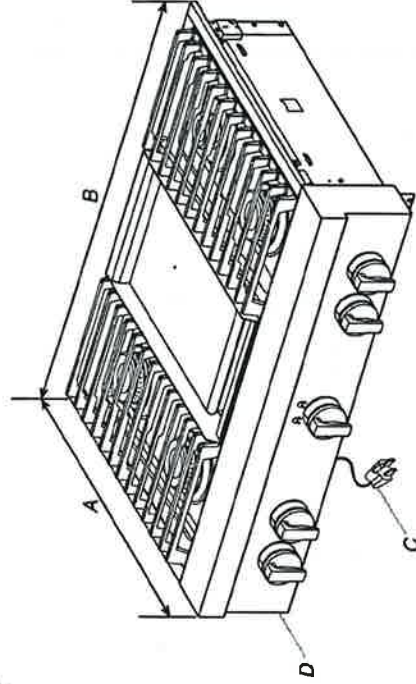

- A. 27¹/₈" (68.9 cm)
- B. 35¹/₄" (90.8 cm)

- C. 3 prong grounding-type power supply cord
- D. Model/serial/rating plate (located on the underside of the cooktop burner base)

Side View of Cooktop

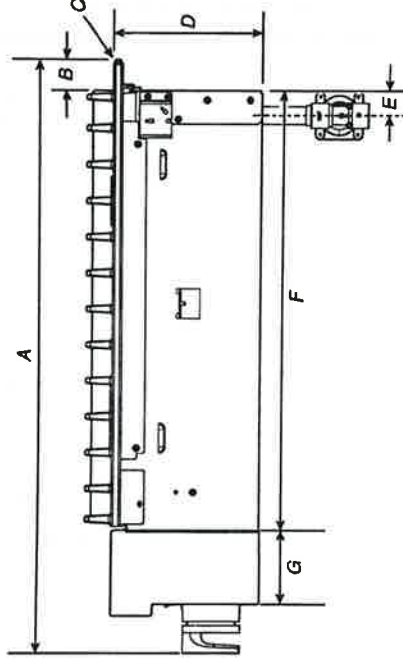


- A. 27¹/₈" (68.9 cm)
- B. 1¹/₄" (3.2 cm)
- C. Island trim or optional backguard
- D. 7¹/₈" (18.8 cm)

- E. Gas inlet is located 1⁷/₈" (4.8 cm) from the back of the cooktop burner base and 4¹/₈" (12.4 cm) in from left-hand side of the cooktop burner base.
- F. 22" (55.9 cm)
- G. 3⁷/₁₆" (8.4 cm)

Lot 115

Gas and Electric Connection Locations

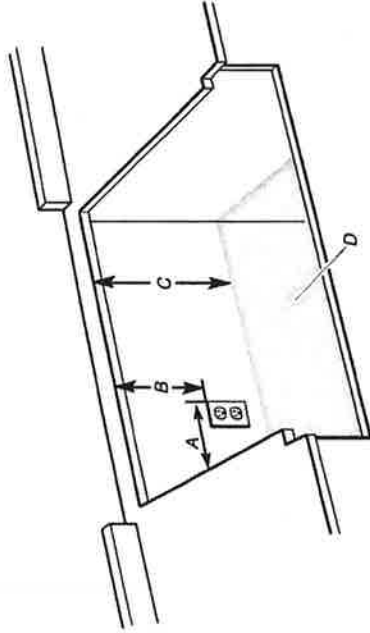


- A. Grounded 3 prong outlet should be located on left-hand side of the cutout 15" (40.6 cm) max. from enclosure sidewall
- B. 10" (25.4 cm) min. clearance from countertop to top of the outlet
- C. 14" (35.6 cm) countertop to the gas supply line
- D. Gas supply line should be located in this area on rear or side walls or the supply line can come up through the floor.

NOTE: Solid side and bottom of cutout enclosure not shown.

Cabinet Requirements

IMPORTANT: If installing a range hood or microwave hood combination above the cooking surface, follow the range hood or microwave hood combination installation instructions for dimensional clearances above the cooktop surface.

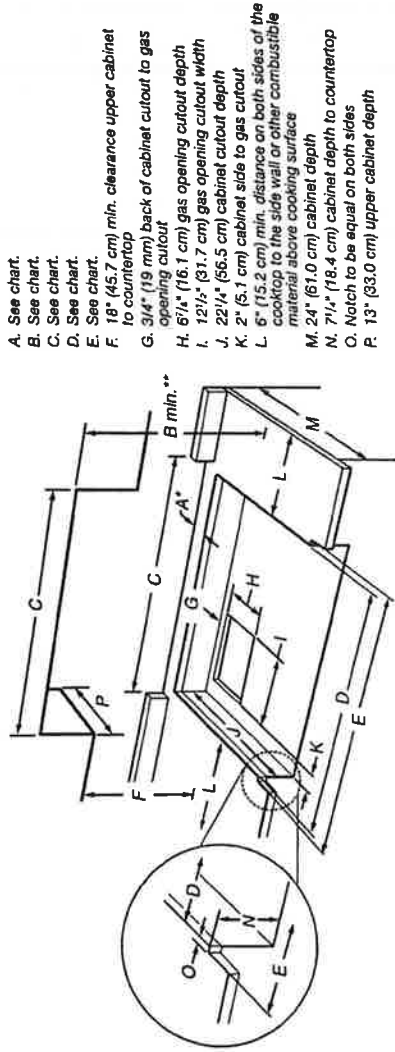

- A. See chart.
- B. See chart.
- C. See chart.
- D. See chart.
- E. See chart.
- F. 18" (45.7 cm) min. clearance upper cabinet to countertop
- G. 3/4" (19 mm) back of cabinet cutout to gas opening cutout
- H. 6 1/4" (16.1 cm) gas opening cutout depth
- I. 12 1/2" (31.7 cm) gas opening cutout width
- J. 22 1/4" (56.5 cm) cabinet cutout depth
- K. 2" (5.1 cm) cabinet side to gas cutout
- L. 6" (15.2 cm) min. distance on both sides of the cooktop to the side wall or other combustible material above cooking surface
- M. 24" (61.0 cm) cabinet depth
- N. 7 1/4" (18.4 cm) cabinet depth to countertop
- O. Notch to be equal on both sides
- P. 13" (33.0 cm) upper cabinet depth

Size	A* Cooktop Cutout to Back Wall	B** Cooktop to Cabinet	C Optional Backguard and Upper Cabinet Opening	D Cabinet and Countertop	E Countertop Only
30" (76.2 cm)	13/4" (4.4 cm)*	42" (106.7 cm)	30" (76.2 cm)	29 1/4" (74.3 cm)	29 1/4" (75.9 cm) for zero clearance
36" (91.4 cm)	13/4" (4.4 cm)*	58" (147.3 cm)	36" (91.4 cm)	35 1/4" (89.5 cm)	35 1/4" (90.8 cm) for zero clearance
48" (121.9 cm)	13/4" (4.4 cm)*	58" (147.3 cm)	48" (121.9 cm)	47 1/4" (120.0 cm)	47 1/4" (121.6 cm) for zero clearance

* NOTE: If back wall is constructed of a combustible material and a backguard is not installed, a minimum clearance of dimension A + 6" (15.2 cm) is required for all models.

** NOTES: Dimension "B" can be reduced by 6" (15.2 cm) when bottom of wood or metal cabinet is covered by not less than 0.25" (6.4 mm) flame retardant millboard covered with not less than No. 28 MSG sheet metal, 0.015" (0.4 mm) stainless steel, 0.024" (0.6 mm) aluminum, or 0.020" (0.5 mm) copper.

If installing a range hood above the cooktop, follow the range hood instructions for dimensional clearances above the cooktop surface.


NOTE: Due to manufacturing factory tolerances, these are nominal dimensions. You may need to readjust to meet your clearance.

Lot 115

- Electrical supply junction box should be located 3" (7.6 cm) maximum below the support surface when the oven is installed in a wall cabinet. A 1" (2.5 cm) minimum diameter hole should have been drilled in the left rear corner of the support surface to pass the appliance cable through to the junction box.
 - Oven support surface must be solid, level and flush with bottom of cabinet cutout. Floor must be able to support a total weight (microwave and built-in oven) of 208 lbs (95 kg) for 27" (68.6 cm) models or 249 lbs (113 kg) for 30" (76.2 cm) models.
- IMPORTANT:** To avoid damage to your cabinets, check with your builder or cabinet supplier to make sure that the materials used will not discolor, delaminate or sustain other damage. This oven has been designed in accordance with the requirements of UL and CSA International and complies with the maximum allowable wood cabinet temperatures of 194°F (90°C).

Product Dimensions

27" and 30" (68.6 cm and 76.2 cm) Ovens

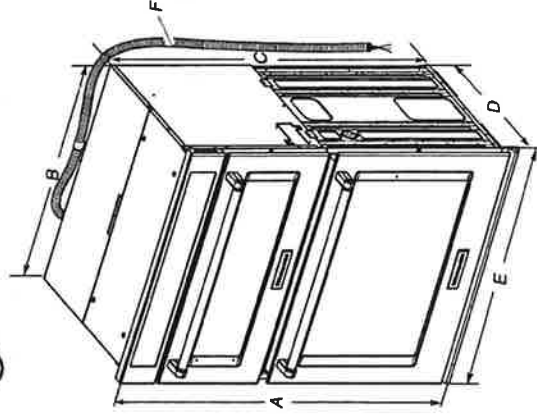

27" (68.6 cm) models


A. 42 3/8" (108.0 cm) overall height
B. 25 1/8" (64.6 cm) recessed width
C. 41" (104.1 cm) recessed height
D. 23 1/2" (59.1 cm) max. recessed depth
E. 27" (68.6 cm) overall width
F. 48" (121.9 cm) flexible conduit length measured from the conduit clamp located at the rear of the oven. Do not remove the conduit clamp.

30" (76.2 cm) models

A. 42 3/8" (108.0 cm) overall height
B. 28 3/8" (72.2 cm) recessed width
C. 41" (104.1 cm) recessed height
D. 23 1/2" (59.1 cm) max. recessed depth
E. 30" (76.2 cm) overall width
F. 48" (121.9 cm) flexible conduit length measured from the conduit clamp located at the rear of the oven. Do not remove the conduit clamp.

Cabinet Dimensions

27" and 30" (68.6 cm and 76.2 cm) Ovens

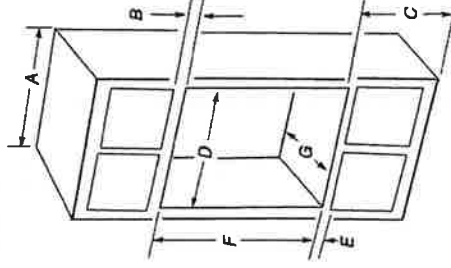

27" (68.6 cm) models

A. 27" (68.6 cm) min. cabinet width
B. 1" (2.5 cm) top of cutout to bottom of upper cabinet door
C. 19 1/2" (48.9 cm) bottom of cutout to floor is recommended.
D. 25 1/2" (64.8 cm) bottom of cutout to floor is acceptable.
E. 1 1/2" (3.8 cm) min. bottom of cutout to top of cabinet door
F. 41 3/8" (105 cm) recommended cutout height
G. 24" (60.7 cm) cutout depth

30" (76.2 cm) models

A. 30" (76.2 cm) min. cabinet width
B. 1" (2.5 cm) top of cutout to bottom of upper cabinet door
C. 19 1/2" (48.9 cm) bottom of cutout to floor is recommended.
D. 28 1/2" (72.4 cm) cutout width
E. 1 1/2" (3.8 cm) min. bottom of cutout to top of cabinet door
F. 41 3/8" (105 cm) recommended cutout height
G. 24" (60.7 cm) cutout depth

*NOTE: The cutout height can be between 41" and 41 1/2" (104.1 cm and 105.6 cm) for microwave/oven combination.

Electrical Requirements

If codes permit and a separate ground wire is used, it is recommended that a qualified electrical installer determine that the ground path and wire gauge are in accordance with local codes.

Check with a qualified electrical installer if you are not sure the oven is properly grounded.
This oven must be connected to a grounded metal, permanent wiring system.

Be sure that the electrical connection and wire size are adequate and in conformance with the National Electrical Code, ANSI/NFPA 70-latest edition or CSA Standards C22.1-94, Canadian Electrical Code, Part 1 and C22.2 No. O-M91-latest edition, and all local codes and ordinances.

A copy of the above code standards can be obtained from:

National Fire Protection Association
1 Batterymarch Park
Quincy, MA 02169-7471


CSA International
8501 East Pleasant Valley Road
Cleveland, OH 44131-5575

Lot 115

Electrical Connection

To properly install your oven, you must determine the type of electrical connection you will be using and follow the instructions provided for it here.

- Oven must be connected to the proper electrical voltage, amperage, and frequency as specified on the model/serial/rating plate. See the following illustration.



A. Model/serial/rating plate

- Models rated from 7.3 to 9.6 kW at 240 volts (5.4 to 7.4 kW at 208 volts) require a separate 40-amp circuit. Models rated at 4.8 kW and below at 240 volts (3.6 kW and below at 208 volts) require a separate 30-amp circuit.
- A circuit breaker is recommended.
- Connect directly to the fused disconnect (or circuit breaker box) through flexible, armored or nonmetallic sheathed, copper cable (with grounding wire). See "Make Electrical Connection" section.

- Flexible conduit from the oven should be connected directly to the junction box.
- Do not cut the conduit. The length of conduit provided is for serviceability of the oven.
- A UL listed or CSA approved conduit connector must be provided.
- If the house has aluminum wiring, follow the procedure below:

1. Connect a section of solid copper wire to the ends of the flexible conduit leads.

2. Connect the aluminum wiring to the added section of copper wire using special connectors and/or tools designed and UL listed for joining copper to aluminum. Follow the electrical connector manufacturer's recommended procedure. Aluminum/copper connection must conform with local codes and industry accepted wiring practices.

For power requirements, refer to the following table.

Model	Voltage	Amperage (L1)*	Amperage (L2)*	Rating (W)
KOCE507E/ KOCE500E	120/240	32	30	8000
KOCE507E/ KOCE500E	120/208	30	28	6600

*Amperage values noted above are for information purposes only: The units are rated in watts.

INSTALLATION INSTRUCTIONS

Prepare Built-In Microwave/Oven Combination

1. Decide on the final location for the oven. Locate existing wiring to avoid drilling into or severing wiring during installation.

! WARNING

Excessive Weight Hazard

Use two or more people to move and install oven.


Failure to do so can result in back or other injury.

2. To avoid floor damage, set the oven onto cardboard prior to installation. Do not use handle or any portion of the front frame for lifting.
3. Remember to remove bottom vent from the foam packing on top of oven.
4. Remove the shipping materials and tape from the oven.
5. Remove the hardware package from inside the bag containing literature.
6. Remove and set aside racks and other parts from inside the oven.
7. Move oven and cardboard close to the oven's final location.

Remove Oven Door(s)

IMPORTANT: Use two hands to remove oven door.

1. Prior to removing the oven door, prepare a surface where you will place it. This surface should be flat and covered with a soft blanket, or use the corner posts from your packaging material.
2. Open the oven door.
3. Locate the oven door hinge locks in both corners of the oven door, and then rotate the hinge locks toward the oven door to the unlocked position. If the door hinge lock is not rotated fully (see illustration B), the door will not remove properly.



A. Oven door hinge lock in locked position

B. Oven door hinge lock in unlocked position
