

CONSTRUCTION SUMMARY

North Oakville - 395 - 1 - EAGLE (38-07) Elev B

Register Plan Number: Municipal Address: Closing: 9-Apr-21

CONSTRUCTION

Inv. 164	1 - GRANITE COUNTER TOPS W/UNDERMOUNT SINKS IN ALL BATHROOMS AS PER BUILDER STANDARD SELECTIONS
1	OPTIONAL SINK IN SERVRY AS PER PLAN
	RELOCATE SINK IN KITCHEN AS PER SKETCH
	ADD WINDOW IN KITCHEN IN LIEU OF GARDEN DOOR AS PER SKETCH
Line 2064	Note:
21Aug20 / 21Aug20	
Inv. 164	1 - REDUCE SIZE OF KITCHEN ISLAND AND REMOVE SINK AS PER SKETCH
2	4 INCH ENGINEERED HARDWOOD FLOORING THROUGHOUT MAIN AND SECOND FLOOR INCLUDING STAIRCASE AS PER BUILDER STANDARD SELECTIONS
Line 2065	Note:
21Aug20 / 21Aug20	
Inv. 164	1 - VINYL FLOORING IN LIEU OF CARPET IN BASEMENT AS PER BUILDER STANDARD SELECTIONS
3	ADD GRANITE COUNTERTOP W/LOWER CABINETS AS PER SKETCH AS PER BUILDER STANDARD SELECTIONS
	OPTIONAL COLD STORAGE IN BASEMENT AS PER PLAN
Line 2066	Note:
21Aug20 / 21Aug20	

ELECTRICAL

Inv. 266	1 - BELL AND CABLE LOCATION SKETCH. LOCATIONS MAY VARY SLIGHTLY DUE TO JOIST LOCATIONS
4	
Line 5373	Note:
14Dec20 / 30Dec20	
Inv. 266	1 - GREAT ROOM: INSTALL RECEPTACLES - DEDICATED 15 AMP 120 VOLT RECEPTABLE ABOVE FIREPLACE FOR TV
12	
Line 5381	Note:
14Dec20 / 30Dec20	
Inv. 266	1 - KITCHEN: INSTALL RECEPTACLES - ADDITIONAL 15 AMP 120 VOLT RECEPTABLE FOR GAS STOVE
16	
Line 5385	Note:
14Dec20 / 30Dec20	
Inv. 266	1 - KITCHEN: APPLIANCE - RELOCATE STANDARD APPLIANCE- DISHWASHER TO GO BESIDE NEW SINK LOCATION
17	
Line 5386	Note:
14Dec20 / 30Dec20	
Inv. 266	4 - CEILING FAN - REINFORCE CEILING LIGHTS FOR CEILING FANS
19	
Line 5387	Note:
14Dec20 / 30Dec20	
Inv. 266	1 - MASTER ENSUITE TOILET ROOM: INSTALL RECEPTACLES - DEDICATED 15 AMP 120 VOLT GFCI RECEPTABLE (INTERIOR) BESIDE TOILET
21	
Line 5390	Note:
14Dec20 / 30Dec20	
Inv. 266	1 - EXTERIOR SOFFIT: INSTALL ONE (1) RECEPTACLES - DEDICATED 15 AMP 120 VOLT GFCI RECEPTABLE (EXTERIOR) IN SOFFIT, BY GARAGE
22	
Line 5392	Note:
14Dec20 / 30Dec20	



CONSTRUCTION SUMMARY

North Oakville - 395 - 1 - EAGLE (38-07) Elev B

Register Plan Number: Municipal Address: Closing: 9-Apr-21

Inv.266	1 - KITCHEN: INSTALL ELECTRICAL - ROUGH-IN FOR 30 - 40 AMP BUILT-IN WALL OVEN
14	
Line 5383	Note:
14Dec20 / 30Dec20	

EXTERIOR DOORS

Inv.266	1 - KITCHEN: BACK DOOR- CHANGE TO DOUBLE FRENCH DOORS WITH A SCREEN, IN LIEU
23	OF SINGLE FRENCH WITH SIDE LITES. THERE WILL BE NO SIDE WINDOWS.
Line 5393	Note:
14Dec20 / 30Dec20	
Inv.266	1 - KITCHEN: MOVE LOCATION OF KITCHEN BACK DOOR CLOSER TO GREAT ROOM TO
18	ACCOMMODATE FOR THE COUNTERTOP EXTENSION
Line 5394	Note:
14Dec20 / 30Dec20	

HVAC

Inv.266	1 - KITCHEN: INSTALL GAS PIPING AND OTHER - GAS LINE R/I FOR MAIN FLOOR - STOVE -
15	
Line 5384	Note:
14Dec20 / 30Dec20	
Inv.266	1 - AIR CONDITIONER - ROUGH - IN AIR CONDITIONER ONLY
20	
Line 5389	Note:
14Dec20 / 30Dec20	

MISCELLANEOUS

Inv.266	1 - Purchaser has attended a Structural appointment at the Decor Centre & has DECLINED any additional
24	upgrades and accepts and acknowledges that there will be no further structural
Line 5395	changes/additions/deletions to be made upon signing
14Dec20 / 30Dec20	Note:
Inv.266	1 - Purchasers are aware & accepts that ANY changes made to upgrades after signing this Purchasers
25	Extra Form are subject to a minimum administration fee
Line 5396	Note:
14Dec20 / 30Dec20	

PLUMBING

Inv.266	1 - BASEMENT: INSTLL EXTRA WET BAR ROUGH-IN. SEE SKETCH
10	
Line 5379	Note:
14Dec20 / 30Dec20	
Inv.266	1 - KITCHEN: INSTALL EXTRA ROUGH-IN LINE FOR FRIDGE ICE MAKER WITH SHUT-OFF
11	
Line 5380	Note:
14Dec20 / 30Dec20	

VACCUM/BELL

Inv.266	1 - GREAT ROOM: INSTALL CONDUIT - 1 1/4" ORANGE FLEX CONDUIT APPROX. 35FT FOR
13	FIREPLACE FOR TV
Line 5382	Note:
14Dec20 / 30Dec20	

North Oakville - 395 - 1 - EAGLE (38-07) Elev B

Register Plan Number: Municipal Address: Closing: 9-Apr-21

Inv. 266	1 - IPTV NETWORK CABLE PACKAGE - 4-CAT6 NETWORK CABLES AND TERMINATION	
5	Line 5374	Note:
14Dec20 / 30Dec20		
Inv. 266	1 - KITCHEN: INSTALL CENTRAL VACUUM - CENTRAL VAC KICKPLATE- ROUGH-IN ONLY	
6	Line 5375	Note:
14Dec20 / 30Dec20		
Inv. 266	1 - MASTER ENSUITE: INSTALL CENTRAL VACUUM - CENTRAL VAC KICKPLATE ROUGH-IN ONLY, UNDER ENSUITE VANITY SINK	
7	Line 5376	Note:
14Dec20 / 30Dec20		
Inv. 266	1 - GREAT ROOM: INSTALL SURROUND SOUND - ROUGH-IN SPEAKER WIRES (X5) SUBWOOFER CABLE (X1) 6.5 INCH SPEAKER ROUGH-IN BRACKETS (X5)	
8	Line 5377	Note:
14Dec20 / 30Dec20		
Inv. 266	1 - LOFT: INSTALL SURROUND SOUND - SINGLE ZONE AUDIO ROUGH-IN SPEAKER WIRES (X2) CAT-5E CABLES (X2) 6.5 INCH SPEAKER BRACKETS (X1 PAIR)	
9	Line 5378	Note:
14Dec20 / 30Dec20		


Lot 395

HLA
VLA

EAGLE

3,677 SQ. FT.

McLURE'S 835 34 01 EMPLOYED 065 0107

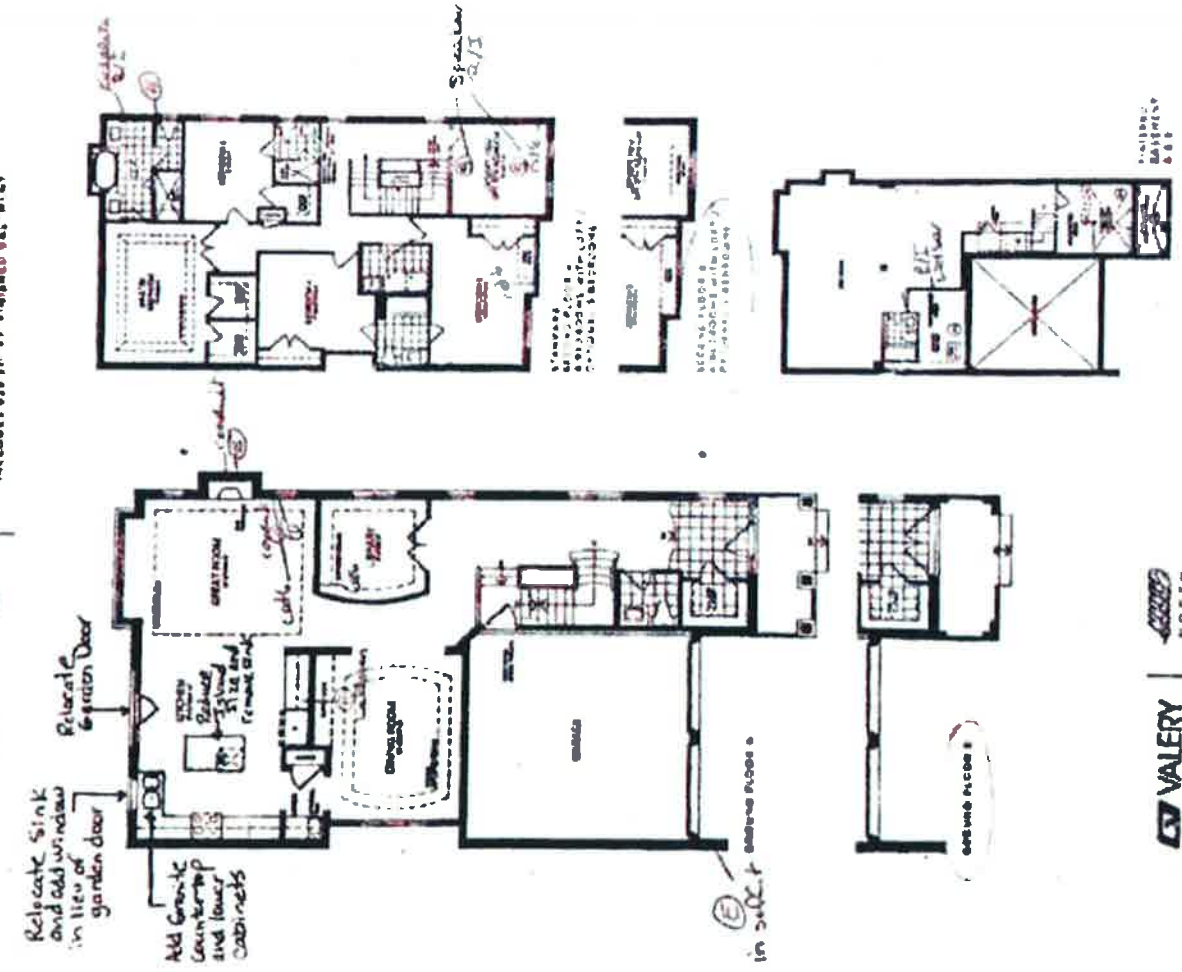

VALERY
NORTH
CARVILLE

HLA

M H - UVA



INCLUDES 025 SQ. FT. FINISHED BASEMENT

Doors to be double French w/screen. No side windows

Counter.
See attached
Plan
Conduit

1

10402
EXP-10402-01

A diagram showing a vertical cable with two square components. A bracket labeled 'a' indicates the distance between the two components.

Northville


“We are not alone in this,” says the author. “We are not alone in this.”

DEC 20 2020

DEC 20 2020



2013 395



DEC 20 2020
