

CONSTRUCTION SUMMARY

North Oakville - 68 - 1 - DOVE (38-03) Elev B

Register Plan Number: Municipal Address: Closing: 10-Mar-21
ELECTRICAL

Inv.260 1 Line 5277 9Dec20 / 10Dec20	1 - BELL AND CABLE ROUGH-IN LOCATIONS. LOCATIONS MAY VARY SLIGHTLY DUE TO JOIST LOCATIONS Note:
Inv.260 3 Line 5279 9Dec20 / 10Dec20	1 - GREAT ROOM: INSTALL RECEPTACLES - DEDICATED 15 AMP 120 VOLT RECEPTABLE FOR TV ABOVE FIREPLACE Note:
Inv.260 7 Line 5284 9Dec20 / 10Dec20	1 - KITCHEN: INSTALL RECEPTACLES - ADDITIONAL 15 AMP 120 VOLT RECEPTABLE FOR STOVE Note:
Inv.280 14 Line 5673 6Jan21 / 8Jan21	1 - KITCHEN: INSTALL ELECTRICAL - ROUGH-IN FOR 30 - 40 AMP BUILT-IN WALL OVEN Note:
Inv.280 15 Line 5675 6Jan21 / 8Jan21	1 - KITCHEN: INSTALL RECEPTACLES - ADDITIONAL 15 AMP 120 VOLT RECEPTABLE FOR MICROWAVE IN WALL OVEN Note:

HVAC

Inv.280 16 Line 5676 6Jan21 / 8Jan21	1 - KITCHEN: INSTALL GAS PIPING AND OTHER - UPGRADE STOVE VENT FROM 6 INCH TO 10 INCH Note:
Inv.260 10 Line 5288 9Dec20 / 10Dec20	1 - AIR CONDITIONER AND FLOW - THROUGH HUMIDIFIER AND MEDIA FILTER - ANX13 - 13 SEER - R - 410A - 3.0 TON - WITH FLOW THRU HUMIDIFIER AND 5 INCH MEDIA FILTER Note:
Inv.260 6 Line 5283 9Dec20 / 10Dec20	1 - KITCHEN: INSTALL GAS PIPING AND OTHER - GAS LINE R/I FOR MAIN FLOOR - STOVE Note:

MISCELLANEOUS

Inv.260 11 Line 5289 9Dec20 / 10Dec20	1 - Purchaser has attended a Structural appointment at the Decor Centre & has DECLINED any additional upgrades and accepts and acknowledges that there will be no further structural changes/additions/deletions to be made upon signing Note:
Inv.260 12 Line 5290 9Dec20 / 10Dec20	1 - Purchasers are aware & accepts that ANY changes made to upgrades after signing this Purchasers Extra Form are subject to a minimum administration fee Note:
Inv.280 13 Line 5672 6Jan21 / 8Jan21	1 - REOPENING FEE Note:

North Oakville - 68 - 1 - DOVE (38-03) Elev B

Register Plan Number: Municipal Address: Closing: 10-Mar-21

Inv.280	1 - Purchasers are aware & accepts that ANY changes made to upgrades after signing this Purchasers
17	Extra Form are subject to a minimum administration fee
Line 5677	Note:
6Jan21 / 8Jan21	

PLUMBING

Inv.260	1 - KITCHEN: INSTALL EXTRA ROUGH-IN 1/4" COLD WATER LINE FOR FRIDGE ICE MAKER
5	
Line 5282	Note:
9Dec20 / 10Dec20	
Inv.260	1 - BACKFLOW PREVENTER VALVE
9	
Line 5287	Note:
9Dec20 / 10Dec20	

VACCUM/BELL

Inv.260	1 - IPTV NETWORK CABLE PACKAGE - 4-CAT6 NETWORK CABLES AND TERMINATION
4	
Line 5280	Note:
9Dec20 / 10Dec20	
Inv.260	1 - GREAT ROOM: INSTALL CONDUIT - 1 1/4" ORANGE FLEX CONDUIT APPROX. 35FT FOR FIREPLACE
2	
Line 5278	Note:
9Dec20 / 10Dec20	

WINDOWS

Inv.260	3 - BASEMENT: ENLARGE THREE (3) BASEMENT WINDOW - EXTRA STANDARD WINDOW -
8	36 X 24
Line 5286	Note:
9Dec20 / 10Dec20	


Telephone — (T)
Cable — (C)
Electrical — (E)

Lot 68

DOVE

3,658 SQ. FT.

INCLUDES 842 SQ. FT. FINISHED BASEMENT

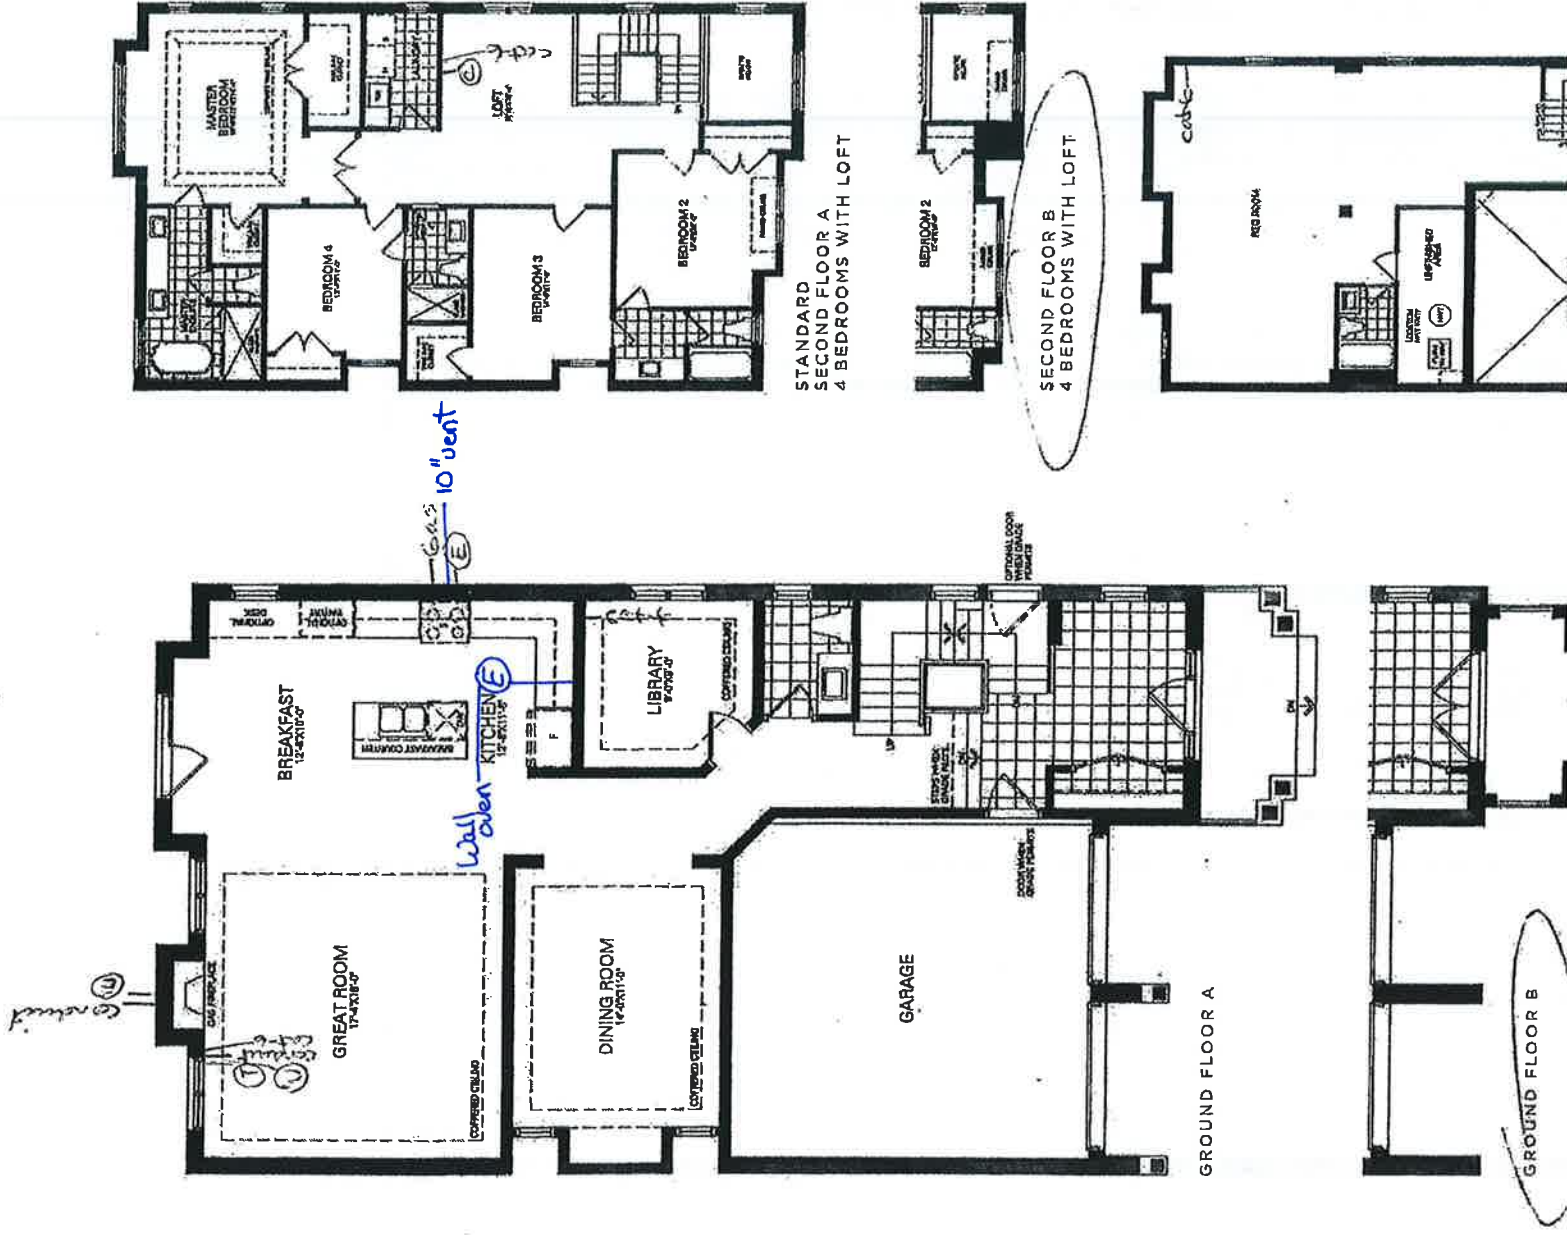

RECEIVED

JAN 08 2021




Telephone — (T)
Cable — (C)
Electrical — (E)

0768

DOVE

3,658 SQ. FT.

INCLUDES 842 SQ. FT. FINISHED BASEMENT

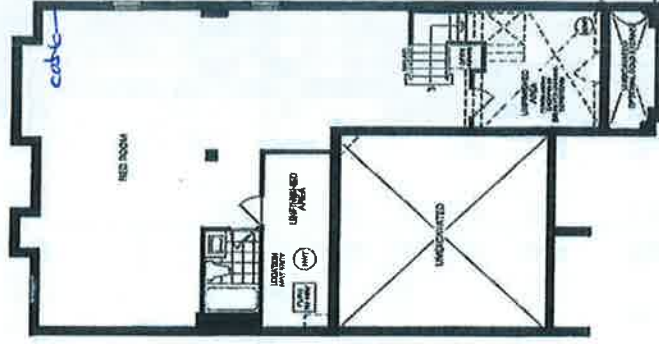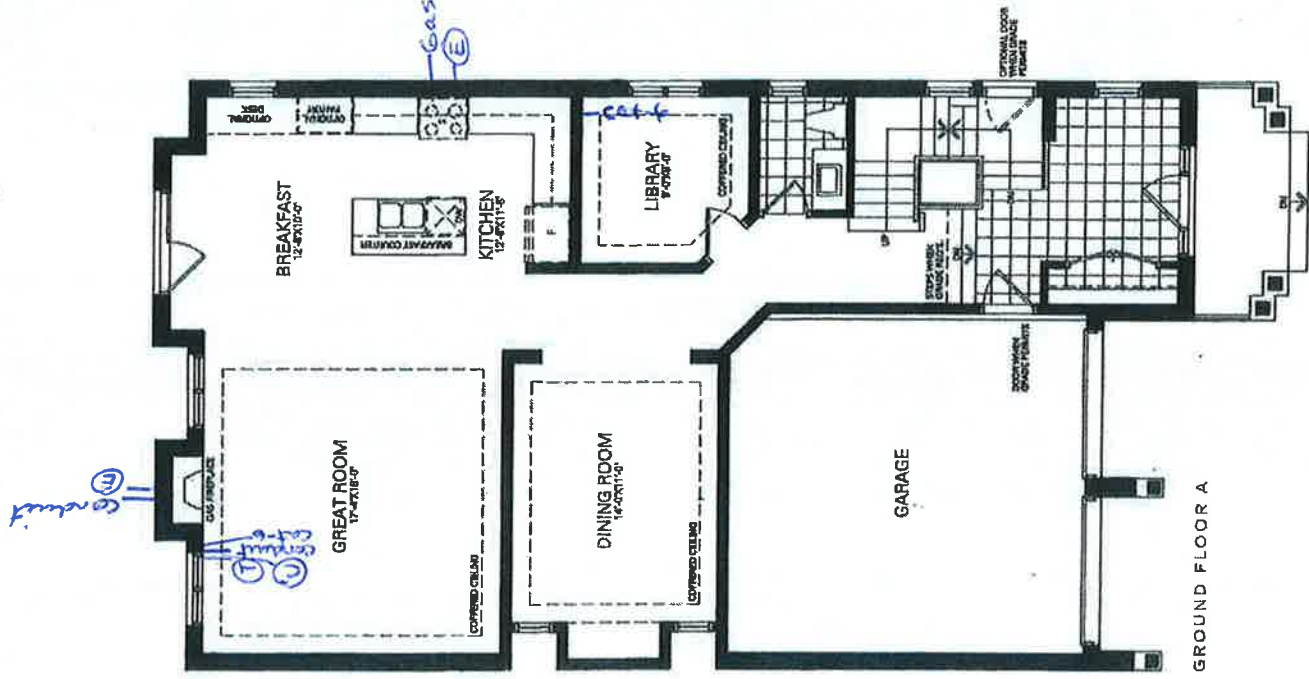

VALERY HOMES | NORTH OAKVILLE

All dimensions are approximate and subject to normal construction variances. Dimensions may exceed the usable floor area. Sizes and specifications subject to change without notice. Furniture is displayed for illustration purposes only and does not necessarily reflect the electrical plan for the suite. Suites are sold unimproved. Battery and brand variations may apply, contact a sales representative for further details. E&O.E. ©Valery Homes 2019. All rights reserved.

22
